

OFFICE OF THE CITY MANAGER LTC # 320-2010

LETTER TO COMMISSION

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jorge M. Gonzalez, City Manager (

DATE:

December 1, 2010

SUBJECT: REPORTS AND INFORMATIONAL ITEMS FOR THE DECEMBER 8, 2010

COMMISSION MEETING

Pursuant to the changes directed by the City Commission for meeting agenda distribution, the following reports will now be provided on a monthly basis via LTC and also posted on the City's website.

- 1. City Attorney's Status Report.
- 2. Parking Status Report - October 2010.
- 3. Informational Report To The Mayor And City Commission, On Federal, State, Miami-Dade County, U.S. Communities, And All Existing City Contracts For Renewal Or Extensions In The Next 180 Days.
- 4. Status Report On The Palm & Hibiscus Islands Underground Utilities Project.
- 5. CIP Monthly Construction Project Update.
- 6. Report Of The Itemized Revenues And Expenditures Of The Miami Beach Redevelopment Agency's City Center District & South Pointe (Pre-Termination Carry Forward Balances) For The Month Of October, 2010.
- Minutes From The Miami-Dade Metropolitan Planning Organization (MPO) Meeting 7. On October 21, 2010.

JMG/REP/Ic

F:\CLER\\$ALL\LILIA\Commission-Meetings\2010\September 15\LTC.doc



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

COMMISSION MEMORANDUM

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jose Smith, City Attorney

DATE:

December 8, 2010

SUBJECT: City Attorney's Status Report

LAWSUITS FILED BY OR AGAINST THE CITY OF MIAMI BEACH SINCE THE LAST REPORT

1. CL Real Estate Holdings, LLC vs. Donovan C. Michael, et al., Case No. 10-58680 CA 11 (Circuit Court – 11th Judicial Circuit in and for Miami-Dade County, Florida)

This is an action to quiet title on real property located at 5255 Collins Avenue, Boat Slip K, Miami Beach, Florida. The Summons and Complaint were served on the City on November 8, 2010.

The City's Answer and Affirmative Defense, asserting priority for any special assessments, including, but not limited to, utility water and sewer services, demolition or board-up liens, and resort taxes was filed on November 9, 2010.

2. Eastern National Bank, N.A. vs. Gustavo Santander, et al., Case No. 10-58983 CA 10 (Circuit Court – 11th Judicial Circuit in and for Miami-Dade County, Florida)

This is an action to foreclose a mortgage on real property located at 7315 Carlyle Avenue, Units 6 and 17, Miami Beach, Florida. The Summons and Complaint were served on the City on November 10, 2010.

The City's Answer and Affirmative Defense, asserting priority for any special assessments, including, but not limited to, utility water and sewer services, demolition or board-up liens, and resort taxes was filed on November 18, 2010.

3. State Farm Mutual Automobile Insurance Co. a/s/o William Multack v. City of Miami Beach, Case No. 08-47680 CA 08 (Circuit Court - 11th Judicial Circuit in and for Miami-Dade County, Florida)

The City was served with this complaint on November 18, 2010 alleging that on December 19, 2007, the plaintiff subrogor, William Multack, was driving his 2005 645 C BMW automobile on the road way at Collins Avenue and the intersection of 65th Street when the vehicle was damaged due to a pot hole existing at the location on said street. Plaintiff is suing for a total of \$25,719.39, which includes the \$500 deductable of the subrogor. The subject roadway is a State Road and is owned by FDOT. We shall either file a motion to dismiss on the premise that it is not our roadway or file an answer and assert that as an affirmative and then file a motion for summary judgment on the contention that it is not our roadway.

City Attorney's Report December 8, 2010 Page 2

4. Wells Fargo Bank, N.A. vs. Ana Maria Orozco, et al., Case No. 10-60591 CA 15 (Circuit Court – 11th Judicial Circuit in and for Miami-Dade County, Florida)

This is an action to foreclose a mortgage on real property located at 3710 Collins Avenue, Unit N-300, Miami Beach, Florida. The Summons and Complaint were served on the City on November 23, 2010.

The City's Answer and Affirmative Defense, asserting priority for any special assessments, including, but not limited to, utility water and sewer services, demolition or board-up liens, and resort taxes will be timely filed.

JS/Ir

F:\atto\AAOFF\sharp\AAOFF\FILE.#S\STATUSRE\STAT2010\STAT 120810.DOC

City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

COMMISSION MEMORANDUM

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jorge M. Gonzalez, City Manager

DATE:

December 8, 2010

SUBJECT: PARKING STATUS REPORT - OCTOBER 2010

During the month of October the Parking Department received revenue from different sources outlined in the categories listed below:

	REVENUE SOURCE	OCTOBER 2009	OCTOBER 2010	%INC/(DEC)
ı.	Meters (Single & Multi Space)\$	51,357,652.81	\$1,595,725.66	17.54%
II.	Off-Street Facilities			
	a. Garages and Attended	\$841,007.40	\$923,346.34	9.79%
	17 th Street Garage	\$304,539.47	\$307,193.86	0.87%
	City Hall Garage	,	\$42,840.67	N/A
	7 th Street Garage	\$182,389.38	\$178,664.00	(2.04%)
	Pennsylvania Ave Garag		\$1,453.52*	N/A
	17 th Street Lots (E & W)	\$34,870.58		N/A
	12 th Street Garage	\$32,090.38	\$37,303.73	16.25%
	13th Street Garage	\$80,678.41	\$90,379.04	12.02%
	42 nd Street Garage	\$34,082.24	\$27,297.95	(19.91%)
	16 th Street Garage	\$172,356.94	\$238,213 <i>.57</i>	38.21%
	b. Joint Venture	4		
	5 th & Alton Garage	N/A		N/A
	**46% of total revenue which represent	ts the City's pro-rata sho	are pursuant to the Develop	oment Agreement.
III.	Enforcement	\$331,414.46	\$286,481.35	(13.56%)
	a. M-D Cty Pkg Violations	\$313,864.46	\$265,581.35	(15.38%)
	b. Towing	\$17,550.00	\$20,900.00	19.09%
IV.	Permit Sales	\$286,396.31	\$309,511.03	8.07%
	a. Municipal Monthly Permits	\$44,789.35	\$62,034.38	38.50%
	b. Valet & Space Rental	\$111,945.10	\$116,549.48	4.11%
	c. Residential Permits	\$79,186.86	\$80,082.17	1.13%
٠.	d. Hotel Hang Tags (900 tags)e. In Vehicle Parking Meter	\$17,280.00	\$9,000.00	(47.92%)
	(136 iParks)	\$33,195.00	\$41,845.00	26.06%

December 8, 2010
City Commission Memorandum
Parking Status Report – October 2010
Page 2 of 2

Meters: the increase of meter revenue is primarily due to an increase in the hourly rate from \$1.25 to \$1.50 south of 23rd Street and extended hours of enforcement from 9a.m. to 3a.m.

<u>Garages & Attended Lots:</u> the overall revenue in the garages and lots increased by 9.79% primarily due to an increase in 17^{th} , 12^{th} , 13^{th} and 16^{th} Street garages off-set by a decrease in the 7^{th} and 42^{nd} Street Garages.

* The Pennsylvania Avenue Garage was open from 10/29/10 thru 10/31/10; the total revenue reported during the month of October of \$1,453.52 includes cash collected by the pay on foot stations totaling \$1,261.00 (87%).

<u>Enforcement:</u> revenue decreased by 13.56%. The decrease in revenue is due to a reduction in citation productivity.

<u>Permit Sales:</u> the overall revenue increase in permits sales is a result of increased municipal monthly permits, valet and space rental, residential permit and In Vehicle Parking Meter (IVPM) sales. Additionally, non-resident IVPMs are available at Publix supermarkets and select Walgreens. Since August 2009 we have sold a total of 504 devices to these retail stores (480 to Publix and 24 to Walgreens).

5th and Alton Garage:


The 5th and Alton Garage is a joint venture project (parking garage) with the "Developer" (Berkowitz Development Group) containing 1,080 parking spaces. The Developer and City own 54% and 46% of the parking spaces, respectively, and profit/loss is also shared in the same manner. The City's revenue portion (46%) is \$21,818.14; expenses have exceeded revenues which resulted in a loss of \$77,986.17, ending October 31, 2010. Pursuant to the Development Agreement, the City receives its proportionate share of profit or must subsidize any loss. The City and Developer continue to jointly pursue initiatives to promote the use of the garage. These initiatives include but are not limited to "after hours" flat rate parking; valet parking storage; monthly parking; and strategically placed electronic signage directing users to the facility. Future considerations include promotional rates for "after hours"; valet parking storage; and park and ride options to the entertainment districts. Attached are detailed reports for each category listed above that comprises the total monthly revenue.


F:\ping\\$MAN\RAR\Parking Status Report\FY 2010-2011\01 October 2010.doc

PARKING DEPARTMENT REVENUE

Cotober-10

			Garages &		<u>Meters</u>	Pern	nit Sales & Space	To	wing & Parking	
		Ŀ	<u> Attended Lots</u>	 	(SS & MS)		<u>Rentals</u>		<u>Violations</u>	TOTAL :
	Oct-09	\$	841,007.40	\$	1,357,652.81	\$	286,396.31	\$	331,414.46	\$ 2,816,470.98
	Oct-10	\$	922,085.34	\$	1,595,725.66	. \$	309,511.03	\$	286,481.35	\$ 3,113,803.38
Diff		 \$	81,077.94	\$	238,072.85	\$	23,114.72	\$	(44,933.11)	\$ 297,332.40
%			9.64%		17.54%		8.07%		-13.56%	10.56%

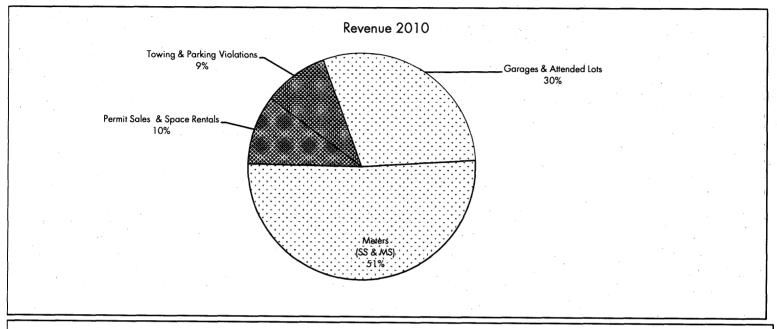


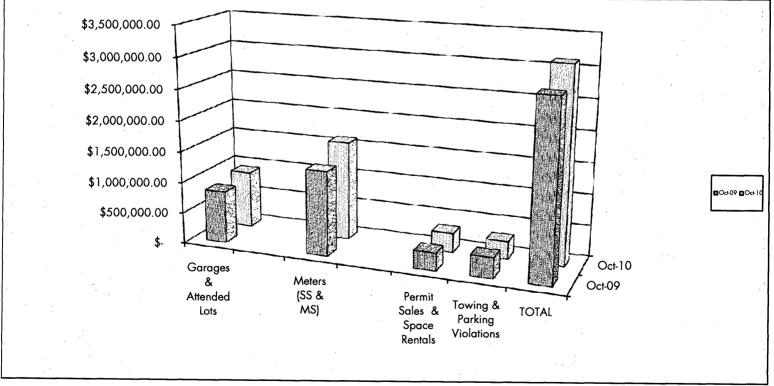

PARKING DEPARTMENT REVENUE YTD


October-10

	Garages &			Towing & Parking	
	Attended Lots	Meters (SS & MS)	Permit Sales	<u>Violations</u>	<u>TOTAL</u>
Oct-10	\$ 922,085.34	\$ 1,595,725.66	\$ 309,511.03	\$ 286,481.35	\$ 3,113,803.38
Nov-10			·		\$ -
Dec-10					\$ -:
Jan-11					\$ -
Feb-11					\$ -
Mar-11					\$
Apr-11					\$ -
May-11					\$ -
Jun-11					\$ -
Jul-11		1			\$
Aug-11					\$ -
Sep-11	·				\$ -
YTD	\$ 922,085.34	\$ 1,595,725.66	\$ 309,511.03	\$ 286,481.35	\$ 3,113,803.38

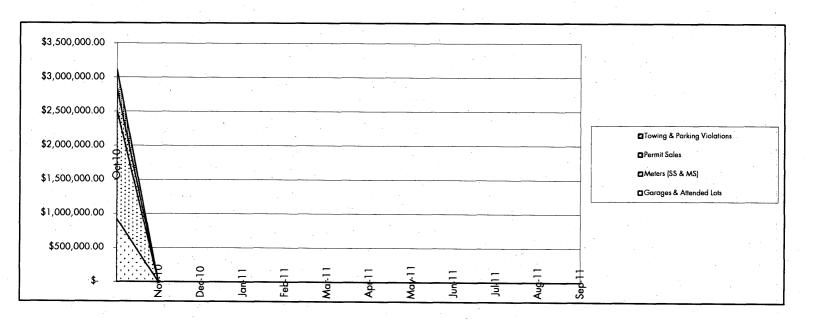

PARKING GARAGE REVENUE CATEGORIES October 10

					_		_
	TOTAL	694,339.07	45.976.27	181,770.00	•	922,085.34	
Garage -	Anchor	\$ 173,960.78	\$ 17.152.79 \$	\$ 47,100.00 \$	↔	\$ 37,303.73 \$ 90,379.04 \$ 27,297.95 \$ 238,213.57 \$ 922,085.34	
13th Street 42nd Street	Garage - 8A	\$ 5,597.95		\$ 21,700.00		\$ 27,297.95	
13th Street	Garage - 2A Garage - 17A Garage - 8A	\$ 31,003.73 \$ 80,299.04 \$ 5,597.95 \$ 173,960.78		6,300.00 \$ 10,080.00 \$ 21,700.00 \$ 47,100.00		\$ 90,379.04	
12th Street	Garage - 2A	\$ 31,003.73		\$ 6,300.00	:	\$ 37,303.73	
treet Garage 17th Street Lots - 12th Street	5A E & W					· •	
'th Street Garage	-16	\$ 162,014.00		\$ 16,650.00	i	\$ 178,664.00	
1775Meridian 7th St	CH Garage - GZ	61.769,8	28,823.48	5,320.00		92.52 \$ 42,840.67	
Ave Garage-	55	\$ 192.52				\$ 192.52	
17th Street	Garage - 2G	\$ 232,573.86		\$ 74,620.00		307,193.86	
		Ticket	Valet	Monthly Permits			

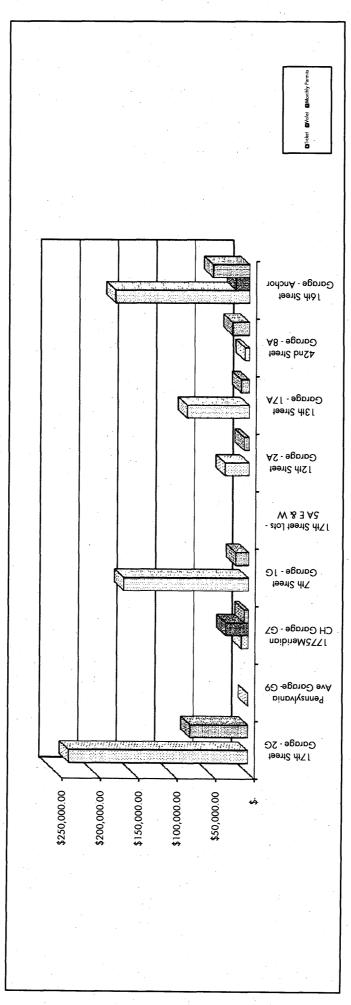

City of Miami Beach Parking Department

Parking Department
Daily Vehicle Entry Report - October 2010


		:1	17th Street Garage - 2G	9		7th St Garage - 1G		16th	16th Street Garage - ANCHOR	Ď.	1775	1775 Meridian Garage - G7	- G7
Date	Dαу	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count
1	ч.	3029	22:00-22:59	480	480	23:00-23:59	180	1281	14:00-14:59	220	612	17:00:17,59	168
7	ΥS	3375	20:00-20:59	640	970	15:00-15:59	274	1418	23:00-23:59	229	93	21:00-21:59	19
က	S	3086	15:00-15:59	573	573	16:00-16:59	290	1214	00:00-00:29	268	82	12:00-12:59	16
4	Q W	1565	17:00-17:59	295	295	15:00-15:59	109	763	17:00-17:59	126	612	17:00-17:59	167
ۍ.	2	2208	17:00-17:59	345	345	15:00-15:59	. 62	803	14:00-14:59	123	655	17:00-17:59	184
91		2545	20:00-20:59	420	420	17:00-17:59	ý. 2	860	18:00-18:59	122	629	06:00-06:59	180
· ·	E	2260	17:00:17:59	374	374	19:00-19:59	011	1063	18:00-18:59	142	643	17:00-17:59	178
ω (ш ;	3756	19:00-19:59	930	930	23:00-23:59	181	1322	23:00-23:59	177	608	04:00-04:59	202
<u>-</u>	δ.	3614	20:00-20:59	549	549	16:00-16:59	281	1869	17:00-17:59	231	356	18:00-18:59	80
2 :	DS :	3430	18:00-18:59	290	290	17:00-17:59	306	1394	00:00-00:29	256	336	04:00-04:59	85
= :	Q ¥	2274	17:00-17:59	360	360	17:00-17:59	193	892	15:00-15:59	166	703	06:00-06:59	197
12	2 ∶	1893	15:00-15:59	303	303	16:00-16:59	77	831	17:00-17:59	114	677	06:00-06:59	184
<u> </u>	} ;	2415	19:00-19:59	404	404	15:00-15:59	92	765	15:00-15:59	124	637	06:00-06:59	214
7 :	Ξ,	2016	00:00-00:26	363	363	17:00-17:59	76	759	17:00-17:59	127	638	08:00-08:59	171
15	ш ;	3563	20:00-20:59	591	591	23:00-23:59	153	1001	23:00-23:59	162	751	09:00-09:59	426
9 !	δ.	3878	19:00-19:59	706	706	15:00-15:59	280	1585	22:00-22:59	235	229	21:00-21:59	49
	ns :	2887	13:00-13:59	543	543	16:00-16:59	239	1061	00:00-00:29	279	62	00:00-00:29	50
8	Q	1874	17:00-17:59	286	286	14:00-14:59	81	770	14:00-14:59	119	632	08:00-08:59	174
6 9	2 :	2031	17:00-17:59	323	323	16:00-16:59	103	748	09:00-09:59	113	632	08:00-08:59	184
50	>	2112	17:00:17:59	346	346	17:00-17:59	86	800	17:00-17:59	118	199	17:00-17:59	173
22	Ξ,	2287	17:00:17:59	324	324	15:00-15:59	113	686	11:00:11:59	228	740	17:00-17:59	183
75	<u> </u>	2845	12:00-12:59	898	898	16:00-16:59	139	1081	23:00-23:59	148	929	17:00-17:59	170
2 2	۸ ۶	3707	19:00-19:59	585	585	17:00:17:59	256	1325	00:00-00:26	187	325	20:00-20:59	22
24	2 :	3103	18:00-18:59	543	543	14:00-14:59	230	1145	00:00-00:29	231	150	23:00-23:59	35
25	Q	2415	17:00:17:59	423	423	17:00-17:59	8	754	17:00-17:59	125	822	17:00-17:59	220
76		3431	17:00-17:59	494	494	18:00-18:59	81	875	17:00-17:59	139	843	17:00-17:59	222
77	}	3518	19:00-19:59	617	617	16:00-16:59	8	826	15:00-15:59	127	931	08:00-08:59	212
28	E	2259	17:00-17:59	369	369	15:00-15:59	66	860	17:00-17:59	120	652	17:00-17:59	172
29	u	3203	19:00-19:59	532	532	23:00-23:59	134	766	17:00-17:59	135	641	17:00-17:59	164
90	ک	3679	20:00-20:59	731	731	15:00-15:59	233	1417	23:00-23:59	266	160	23:00-23:59	31
<u></u>	S	4897	17:00-17:59	206	206	00:00-00:59	181	1724	23:00-23:59	294	750	19:00-19:59	303
												-	
1		89133			15514			33279			17169		

City of Miami Beach Parking Department Daily Vehicle Entry Report - October 2010


			0 10 Hot										
			Zim Sr Garage - ZA			3th St Garage - 17A			42nd St Garage - 8A		Pennsyl	Pennsylvania Avenue Garage- G9	age-G9
Date	Day	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count	Total Vehicle Entries	Peak Period	Peak Vehicle Count
_	L	253	17:00-17:59	33	436	17:00-17:59	62	379	08:00-08:59	74			
7	ΥS	293	14:00-14:59	42	029	15:00-15:59	107	147	06:00-06:59	32			
က	S	229	00:00-00:26	51	562	17:00-17:59	6	. [6	06:00-06:59	3.1			
4	QW W	145	17:00-17:59	36	226	17:00-17:59	14	396	09:00-00:60	. 08			
2	2	168	17:00-17:59	32	220	15:00-15:59	36	397	09:00-00:59	68			
9	≯	175	16:00-16:59	37	228	18:00-18:59	36	377	09:00-09:59	8 8			
_	Ξ	214	15:00-15:59	40	317	17:00:17:59	43	413	17:00-17:59	83			
ω	ட	338	23:00-23:59	58		23:00-23:59	22	398	09:00-00:20	83			
٥ :	SA	315	14:00-14:59	43	777	15:00-15:59	66	141	06:00-06:59	29			
0	S	254	18:00-18:59	14	930	15:00-15:59	112	88	06:00-06:59	25			
=	Q	153	14:00-14:59	26	414	16:00-16:59	89	296	09:00-09:59	58			
12	2	193	17:00-17:59	34	235	15:00-15:59	35	394	08:00-08:59	8			
<u></u>		210	12:00-12:59	38	218	23:00-23:59	37	391	09:00-09:59	282			
7	Ξ.	211	17:00-17:59	44	285	14:00-14:59	38	393	08:00-08:59	87	-		
15	ட	255	17:00-17:59	36	448	18:00-18:59	69	397	08:00-08:59	8			
9 !	δ.	343	16:00-16:59	53	129	17:00-17:59	92	126	06:00-06:59	31		,	ı
<u> </u>	OS :	178	01:00-01:59	36	559	15:00-15:59	=	92	06:00-06:59	26			
80 (Q V	162	17:00-17:59	35	281	15:00-15:59	54	379	08:00-08:59	86			
6	⊋ :	153	17:00-17:59	32	247	18:00-18:59	46	370	08:00-08:59	98			
50	، ≼	204	17:00-17:59	[4	240	18:00-18:59	42	392	08:00-08:59	75			
2 2	Ξ,	195	17:00-17:59	34	326	14:00-14:59	50	385	08:00-08:59	06			
7 2	<u> </u>	286	17:00-17:59	37	441	23:00-23:59	74	367	08:00-08:59	78			
3 2	ξ .	0/7	17:00-17:59	47	265	23:00-23:59	88	122	06:00-06:59	28			
4 4	کر د	69 !	00:00-00:26	47	525	15:00-15:59	88	64	14:00-14:59	22			
3 3	Ş ;	1/4	17:00-17:59	32	256	18:00-18:59	20	377	08:00-08:59	87			
9 7	⊇ ;	98 :	17:00-17:59	36	276	19:00-19:59	47	409	08:00-08:59	105		-	
/7	> ;	981	17:00-17:59	38	280	12:00-12:59	26	375	08:00-08:59	82			
28	Ξ,	203	17:00-17:59	35	327	18:00-18:59	57	383	08:00-08:59	89			
57	٠;	234	11:00-11:59	32	427	15:00-15:59	99	389	08:00-08:59	83	29	23:00-23:59	73
9	S.	266	13:00-13:59	38	900	13:00-13:59	92	131	07:00-07:59	26	449	23:00-23:59	207
	S	242	20:00-20:59	40	604	18:00-18:59	79	85	06:00-06:59	27	994	18:00-18:59	169
		6863		-	12815			0174			0271		
					2127			71/4			14/2		

PARKING GARAGE EXPENSES October-10

F	ſ			<u>ال</u>	.92	19	14.35%
			TOTAL	\$ 266.400	\$ 304,615.92	\$ 38,215.61	
		h St Garage -	Anchor	41.911.62 \$ 266.400.31	43,266.12	1,354.50 \$	3.23%
		7th St Garage - 17th St Lots - 5A 12th St Garage - 13th St Garage - 42nd St Garage - 16th St Garage	8A	15,423.22 \$	15,968.12	544.90 \$	3.53%
		13th St Garage -	17A	\$ 22,245.63 \$	\$ 21,636.93 \$	\$ (02.809) \$	-2.74%
		12th St Garage -	2A	\$ 16,503.48	\$ 16,898.60	\$ 395.12	2.39%
		17th St Lots - 5A	E&W	\$ 15,378.11	↔	(140.05) \$ (15,378.11)	-100.00%
		7th St Garage -	<u>1G</u>	\$ 62,931.14 \$	\$ 62,791.09	\$ (140.05)	-0.22%
		1775 Meridian	Garage- G9 CH Garage · G7			\$ 32,685.23	
		Pennsylvania Ave 1775 Meridian	Garage- G9		\$	\$ 255.75 \$	
		17th St Garage -			\$ 111,114.08	\$ 19,106.97	20.77%
				00 to 0	Oct-10 (DIFF	%

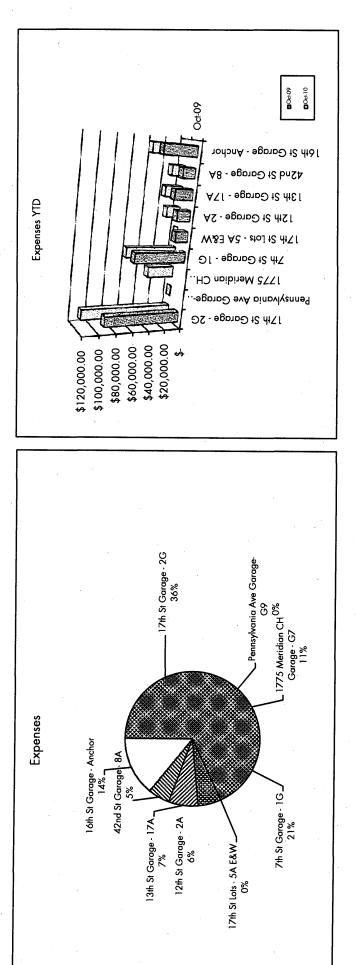

	TOTAL \$ 304,615.92 \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	\$ 304,615.92
	16th Street Garage - Anchor \$ 43,266.12	15,968.12 \$ 43,266.12 \$ 304,615.92
	13th Street Garage - 17A 21,636.93 \$	16,898.60 \$ 21,636.93 \$
PENSES YTC	12th Street Garage - 2A (4 16 898.60 \$, 16,898.60 3
ARAGE EXI	SAE&W \$ \$, ·
PARKING GARAGE EXPENSES YTD	h Street Garage 1G 62,791.09	07,791.09
	17th Street Garage Pennsylvania Ave 1775 Meridian 7th Street Garage 17th Street Lots 2G Garage-G9 CH Garage-G7 1G 5A E & W \$ 111,114.08 \$ 255.75 \$ 32,685.23 \$ 62,791.09 \$	
	Pennsylvania Ave 17 Garage. G9 CF \$ \$ 255.75 \$	
	7th Street Garage - 2G 111,114.08	00.411,111
	Oct-10 \$ Nov-10 Dec-10 Jan-11 Apr-11 Apr-11 Aug-11 Sep-11 Sep-11	*



PARKING GARAGE EXPENSES CATEGORIES October 10

TOTAL	\$ 68,358.43	\$ 41,370.01	\$ 29,294.62	\$ 304,615.92							Security (S.A. & TransValue)	DAttendont Labar	D Electricity	G Maintenance ◆				
16th Street Garage - Anchor	\$ 7,657.10 \$ 21.983.20	\$ 7,507.01	\$ 2,615.61	\$ 43,266.12]	٠.			
42nd Street Garage - 8A	\$ 3,805.53	\$ 2,700.00	\$ 2,388.82	\$ 15,968.12					1	· 			<u> </u>					
13th Street Garage - 17A	\$ 2,240.77	\$ 1,900.00	\$ 1,924.91	\$ 21,636.93						-		(3.33.33			, and the second		eet 16th Street 8A Garage - Anchor
12th Street Garage - 2A	\$ 1,307.82 \$ 11,773.18	\$ 2,084.93	\$ 108.54	ľ		-						-						13th Street 42nd Street Garage 17A Garage 8A
17th Street Lots - 5A E & W		•		·													F	12th Street 13 Garage - 2A Gar
Zth Street Garage - 1G	\$ 15,872.53 \$ 23,823.25	\$ 7,810.05	\$ 3,340.14	\$ 62,791.09														rage 17th Street Lots - 5A E & W
1775 Meridian CH Garage - G7	\$ 3,989.68 \$ 7,521.77		\$ 11,276.78 \$ 176.00	\$ 32,685.23														Pennsykania Ave 1775 Meridian 7th Street Garage 17th Street Lats . Garage- G9 CH Garage · G7 · 1G · 5A E & W
Pennsylvania Ave Garage G9	\$ 255.75			5 255.75	rveillance						,						0	Pennsylvania Ave 177 Garage- G9 CH C
	33,485.00	9,647.02	7,639.82	111,114.08	ontrol, Elevator & Su		20.00	00.00	00.00	00.00	00.00	00.00	00.00	00:00	00.00	00:00		17th Street Garage - 2G
	(e)	↔	∽	₩	Revenue Co		\$50,000.00	\$45,000.00	\$40,000.00	\$35,000.00	\$30,000.00	\$25,000.00	\$20,000.00	\$15,000.00	\$10,000.00	\$5,000.00		
· .	Security (SA & TransValue) Attendant Labor	Janitorial	Electricity Maintenance *		* Includes Landscape, Revenue Control, Elevator & Surveillance												-	

CITY OF MIAMI BEACH PARKING DEPARTMENT FINANCIAL REPORT SUMMARY OCTOBER 2010

	,	REV	REVENUE			LVDENGE	ou.				· (
LOCATION	2009 October	2010 October	Increase/ (Decrease)	Percent of Increase/ (Decrease)	2009 October	2010 October	Increase/ (Decrease)	Percent of Increase/ (Decrease)	2009 October	PROFIT(LOSS) 2010 Incr October (Dec	LOSS) Increase/ (Decrease)	Percent of Increase/
17 St. Garage	304,539.47	307,193.86	2,654.39	0.87%	92,007.11	111,114.08	19,106.97	20.77%	212,532.36	196,079.78	(16,452.58)	-7.74%
City Hall Garage	0.00	42,840.67	42,840.67		0.00	32,685.23	32,685.23		0.00	10,155.44	10,155.44	
7th St. Garage	182,389.38	178,664.00	(3,725.38)	-2.04%	62,931.14	62,791.09	(140.05)	-0.22%	119,458.24	115,872.91	(3,585.33)	-3.00%
Penn Ave Garage	00:0	192.52	192.52		0.00	255.75	255.75		0.00	-63.23	(63.23)	
17th St. Lots	34,870.58	00:00	(34,870.58)	-100.00%	15,378.11	00.00	(15,378.11)	-100.00%	19,492.47	00.0	(19,492.47)	-100.00%
12th St. Garage	32,090.38	37,303.73	5,213.35	16.25%	16,503.48	16,898.60	395.12	2.39%	15,586.90	20,405.13	4,818.23	30.91%
13th St. Garage	80,678.41	90,379.04	9,700.63	12.02%	22,245.63	21,636.93	(608.70)	-2.74%	58,432.78	68,742.11	10,309.33	17.64%
42nd St. Garage	34,082.24	27,297.95	(6,784.29)	-19.91%	15,423.22	15,968.12	544.90	3.53%	18,659.02	11,329.83	(7,329.19)	-39.28%
16th St Anchor	172,356.94	238,213.57	65,856.63	38.21%	41,911.62	43,266.12	1,354.50	3.23%	130,445.32	194,947.45	64,502.13	49.45%
Totals	841,007.40	922,085.34	81,077.94	9.64%	266,400.31	304,615.92	38,215.61	14.35%	674,607.09	617,469.42	42,862.33	7.46%

	Revenue Per Space	Expenses Per Space	Profit/(Loss) Per Space	
17 St. Garage	210.41	76.11	134.30	The 17th Street Garage has 1,460 spaces.
City Hall Garage	65.91	50.28	15.62	The City Hall Garage has 650 spaces.
7th St. Garage	276.57	97.20	179.37	The 7th Street Garage has 646 spaces.
Penn Ave Garage	0.35	0.47	(0.11)	The Penn Street Garage has 550 spaces.
17th St. Lots	0.00	0.00	0.00	The 17th Street Lots have 506 spaces.
12th St. Garage	278.39	126.11	152.28	The 12th Street Garage has 134 spaces.
13th St. Garage	316.01	75.65	240.36	The 13th Street Garage has 286 spaces.
42nd St. Garage	44.03	25.76	18.27	The 42nd Street Garage has 620 spaces.
16th St Anchor	296.65	53.88	242.77	The 16th Street - Anchor Garage has 803 spaces.

CITY OF MIAMI BEACH PARKING DEPARTMENT FINANCIAL REPORT SUMMARY-YEAR TO DATE OCTOBER 2010

		REV	REVENUE			EXDENSES	o L			1990 1111111111111111111111111111111111	á	
LOCATION	2009 October	2010 October	Increase/ (Decrease)	Percent of Increase/ (Decrease)	2009 October	2010 October	Increase/ (Decrease)	Percent of Increase/ (Decrease)	2009 October	2010 October	LOSS) Increase/ (Decrease)	Percent of Increase/
17 St. Garage	304,539.47	307,193.86	2,654.39	0.87%	92,007.11	111,114.08	19,106.97	20.77%	212,532.36	196,079.78	(16,452.58)	-7.74%
City Hall Garage	0.00	42,840.67	42,840.67		0.00	32,685.23	32,685.23		0.00	10,155.44	10,155.44	
7th St. Garage	182,389.38	178,664.00	(3,725.38)	-2.04%	62,931.14	62,791.09	(140.05)	-0.22%	119,458.24	115,872.91	(3,585.33)	-3.00%
Penn Ave Garage	00:0	192.52	192.52		0.00	255.75	255.75		0.00	-63.23	(63.23)	
17th St. Lots	34,870.58	0:00	(34,870.58)	-100.00%	15,378.11	0.00	(15,378.11)	-100.00%	19,492.47	00.00	(19,492.47)	-100.00%
12th St. Garage	32,090.38	37,303.73	5,213.35	16.25%	16,503.48	16,898.60	395.12	2.39%	15,586.90	20,405.13	4,818.23	30.91%
13th St. Garage	80,678.41	90,379.04	9,700.63	12.02%	22,245.63	21,636.93	(608.70)	-2.74%	58,432.78	68,742.11	10,309.33	17.64%
42nd St. Garage	34,082.24	27,297.95	(6,784.29)	-19.91%	15,423.22	15,968.12	544.90	3.53%	18,659.02	11,329.83	(7,329.19)	-39.28%
16th St Anchor	172,356.94	238,213.57	65,856.63	38.21%	41,911.62	43,266.12	1,354.50	3.23%	130,445.32	194,947.45	64,502.13	49.45%
Totals	841,007.40	922,085.34	81,077.94	9.64%	266,400.31	304,615.92	38,215.61	14.35%	674,607.09	617,469.42	42,862.33	7.46%

	Revenue Per Space	Expenses Per Space	Profit/(Loss) Per Space	
17 St. Garage	210.41	76.11	134.30	The 17th Street Garage has 1,460 spaces.
City Hall Garage	65.91	50.28	15.62	The City Hall Garage has 650 spaces.
7th St. Garage	276.57	97.20	179.37	The 7th Street Garage has 646 spaces.
Penn Ave Garage	0.35	0.47	(0.11)	The Penn Street Garage has 550 spaces.
17th St. Lots	0.00	0.00	0.00	The 17th Street Lots have 506 spaces.
12th St. Garage	278.39	126.11	152.28	The 12th Street Garage has 134 spaces.
13th St. Garage	316.01	75.65	240.36	The 13th Street Garage has 286 spaces.
42nd St. Garage	44.03	25.76	18.27	The 42nd Street Garage has 620 spaces.
16th St Anchor	296.65	53.88	242.77	The 16th Street - Anchor Garage has 803 spaces.


City of Miami Beach 5th and Alton Parking Garage Fiscal Year beginning October 1, 2010 ending September 30, 2011 For the current month ending October 31, 2010


			Current Month		Fiscal YTD
		Total Revenues / Expenses	Berkowtiz Development 54% Portion	CMB 46% Portion	CMB 46% Portion
Operating revenue:					
484-8000-344405	5th & Alton Garage - Monthly	\$ 2,100.00	\$ 1,134.00	\$ 966.00	\$ 966.00
484-8000-344406	5th & Alton Garage - Transient	19,177.48	10,355.84	8,821.64	8,821.64
484-8000-344410	5th & Alton Garage - Tenant	26,125.00	14,107.50	12,017.50	12,017.50
484-8000-369999	Miscellaneous Revenue	28.27	15.27	13.00	13.00
	Total operating revenue	47,430.75	25,612.61	21,818.14	21,818.14
Operating sympasses					
Operating expenses:					
484-0470-000312	Professional Services	25,186.20	13,600.56	11,585.64	11,585.64
484-0470-000313	Bank Fees	210.19	113.50	96.69	96.69
484-0470-000314	Electricity	12,243.91	6,611,71	5,632.20	5,632.20
484-0470-000316	Telephone	204.26	110.30	93.96	93.96
484-0470-000317	Water	1,968.35	1,062.91	905.44	905.44
484-0470-000318	Sewer Charges	1,312.23	708.60	603.63	603.63
484-0470-000319	Sanitation Fees	368.39	198.93	169.46	169.46
484-0470-000321	Postage and Shipping			100.10	100.10
484-0470-000325	Contract Maintenance	16,157.92	8,725.29	7,432.63	7,432.63
484-0470-000327	Advertising	10,107.02	0,720.29	7,402.00	7,432.03
484-0470-000329	Storm Water	•	_	•	-
484-0470-000342	Repairs/Maintenance Supply	32.22	17.40	14.82	44.00
484-0470-000343	Other Operating Expenditures	2.170.13	1,171.87	998.26	14.82 998.26
484-0470-000349	Other Contractual Services	12,767.69	6,894.55		
484-0470-000349	Taxes & Licenses	12,707.09	0,094.00	5,873.14	5,873.14
484-0470-000375	Misc Insurance	144,346.26	77.046.00	-	- 00 000 00
404-0470-000373	Total operating expenses	216,967.75	77,946.98 117,162.60	66,399.28 99.805.15	66,399.28 99,805.15
	rotal operating expenses	270,007.70	117,102.00	33,000.10	99,000.10
Nonoperating revenue					
484-8000-361130	Interest-Repurchase Agreement	1.83	0.99	0.84	0.84
	Total nonoperating revenue	1.83	0.99	0.84	0.84
Net income/(loss)		(169,535.17)	(91,549.00)	(77,986.17)	(77,986.17)
Net assets, beginning Net assets, ending		(286,729.51) \$ (456,264.68)	(154,833.92) \$(246,382.92)	(131,895.59) \$ (209,881.76)	(131,895.59) \$ (209,881.76)

Source - Berkowitz Monthly Financial Statements

Prepared by: Finance Department 11/29/2010

PARKING DEPARTMENT METER REVENUE % of USAGE Oct-10

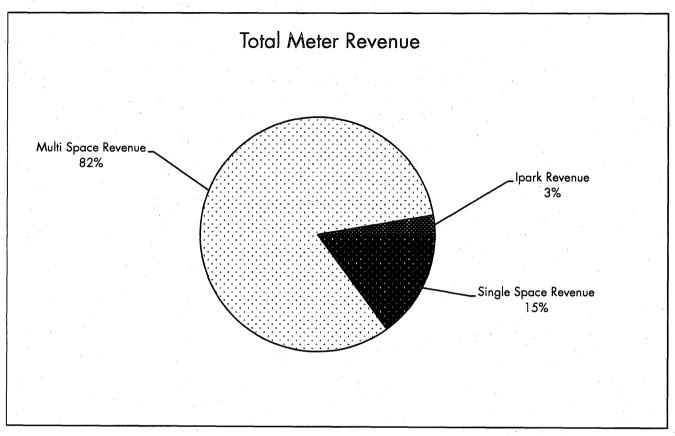



IPARK SALES Oct-10

GRAND TOTAL		28,975.00 \$ 31,275.00	\$ 10,570.00	\$ 41,845.00
TOTAL RELOADS GRAND TOTAL			\$ 10,150.00 \$ 10,570.00	\$ 39,125.00
\$50 - RELOAD SALES	QTY AMOUNT	392 \$ 19,600.00	144 \$ 7,200.00	536 \$ 26,800.00 \$ 39,125.00 \$ 41,845.00
\$25 - RELOAD SAIES \$50	AMOUNT	9,375.00	\$ 2,950.00	493 \$ 12,325.00
	JUNI JUNI	2,300.00 375 \$	420.00 118 \$	
IPARK DEVICE SALES	QTY AMOUNT	115 \$ 2,30	21 \$ 42	136 \$ 2,720.00
		RESIDENT	NON-RESII	

IPARK SALES

	IFA	KK DEVICE S	ALES	\$25 - KELOAD SALES	SALES	\$50 - RELOAD SALES	AD SALES	TOTAL REVENUE
	Resident	Non-Resident	Total	Resident N	Resident Non-Resident	Resident	Non-Resident	
Oct-10	115	21	136	375	118	392	144	\$ 41.845.00
Nov-10			0					
Dec-10			0					
Jan-11			0					
Feb-11			0					
Mar-11			0					
\pr-1]			0					
ay-11		1,	0					
un-]]			0					
Jol-11			0					
Aug-11			0					
Sep-11			0					
YTD	115	21	136	375	118	392	144	144 \$ 41,845.00

CITY OF MIAMI BEACH PARKING DEPARTMENT ELECTRONIC METER REVENUE COMPARISON October 2010

		······································		1		
LOCATION	Accounting Code	# of Spaces	2009 October	2010 October	increase/ (Decrease)	% of Inc/(Dec)
1X - (Washington - 4th & Lincoln) - On Street	480-8000-344501	291	\$72,297.44	\$95,260.40	22,962.96	31.76%
P2 {1A - {1st Street & Ocean Dr.} - Off Street) P2 {1A - {1st Street & Ocean Dr.} - Attended} Total	480-8000-344502 480-8000-344502	62 0 62	\$3,560.87 \$18,925.24 22,486.11	\$20,404.85 \$1,039.25 21,444.10	(1,042.01)	-4.639
P3 (1B - (78 Washington Avenue) - Off Street)	480-8000-344617	12	\$439.98	\$618.99	179.01	40.699
2X - (Washington - 5th & Lincoln) - On Street	480-8000-344503	370	\$75,648.70	\$76,417.08	768.38	1.02%
P11 (2B - (6/7 & Meridian) - Off Street)	480-8000-344505	25	\$1,001.82	\$1,288.27	286.45	28.59%
3X - (Collins & Euclid Ave.) On Street	480-8000-344507	68	\$16,823.84	\$17,740.91	917.07	5.45%
4X - (Alton 7th St Dade Blvd.) - On Street		491				
	480-8000-344509		\$185,222.06	\$123,830.27	(61,391.79)	-33.14%
4B - (Alton & 20th St. Purdy-Dade Blvd.) - On Street	480-8000-344511	213	\$20,260.17	\$17,351.17	(2,909.00)	-14.36%
P24 (4C - (West Ave & 17th St.) - Off Street)	480-8000-344512	66	\$11,967.80	\$12,047.51	79.71	0.67%
P23 (4D - (West Ave & Lincoln Rd.) - Off Street)	480-8000-344513	30	\$3,367.32	\$3,738.91	371.59	11.04%
P29 (5C - (Convention Ctr. Dr. & 17th Street) - Off Street P29 (5C - (Convention Ctr. Dr. & 17th Street) - Attended		85 · .	\$4,662.40 0.00	\$18,296.65 18,420.56		
Total	· · · · · · · · · · · · · · · · · · ·	85	4,662.40	36,717.21	32,054.81	687.52%
5F - (Meridian Ave & 18th Street) - Off Street	480-8000-344519	97	\$0.00	\$0.00		
5F - (Meridian Ave & 18th Street) - Attended Total	480-8000-344519	97	0.00	0.00	0.00	#DIV/0
P33 (5H - (19th Street & Meridian Ave) - Off Street)	480-8000-344521	27	\$2,185.11	\$2,217.95	32.84	1.50%
5M - [17th & Meridian Ave] - Off Street (TEMP P-LOT)	480-8000-344506	27	\$2,657.61	\$0.00		
5M - (17th & Meridian Ave) - Attended	480-8000-344506		0.00	0.00		
Total			2,657.61	0.00	(2,657.61)	-100.00%
6X - (Collins - 20th to 24th St) - On Street	480-8000-344522	236	\$43,832.49	\$51,593.28	7,760.79	17.719
P48 (6A - (22nd Street & Park) - Off Street) P48 (6A - (22nd Street & Park) - Attended)	480-8000-344523 480-8000-344523	14 0	\$1,350.41 \$33,366.38	\$780.22 \$0.00		0.00%
Total			\$34,716.79	\$780.22	(33,936.57)	-97.75%
(6B - (Collins Ave & 21st Street) - Off Street)	480-8000-344524	190	\$8,198.50	\$68,256.27		0.00%
P49 (6B - (Collins Ave & 21st Street) - Attended) Total	480-8000-344524	190	8,198.50	68,256.27	60,057.77	732.55%
PX - (Ocean - Biscayne - 15th St) - On Street	480-8000-344525	442	\$106,072.07	\$138,058.96	31,986.89	30.16%
7A - (Collins Ave, 4th to 15th St) - On Street	480-8000-344526	591	\$195,736.32	\$238,917.32	43,181.00	22.06%
P14 (7C - (Collins Ave & 6th St) - Off Street)	480-8000-344528	14	\$861.43	\$789.54		
P14 (7C (Collins Ave & 6th St) - Attended) Total	480-8000-344528	14	0.00 861.43	789.54	(7) 90)	0.25%
8X · (Pinetree-Alton - 40th to 42nd St) - On Street	480-8000-344530				(71.89)	-8.35%
S/ 104 140 15: 10 10 10 10 10 10 10 10 10 10 10 10 10		. 386 .	\$14,903.40	\$24,317.82	9,414.42	63.17%
263 (8B - (42nd Street & Royal Palm) - Off Street)	480-8000-344531 480-8000-344532	172	\$430.43	\$470.34	39.91	9.27%
63 (8B - (42nd Street & Royal Palm) - Attended)	480-8000-344532	173 0	\$3,437.97 0.00	\$3,441.64 0.00		
Total	•	173	3,437.97	3,441.64	3.67	0.11%
260 (8C - (40/41 Street & Chase) - Off Street)	480-8000-344533	88	\$1, 7 01.12	\$1,813.11	111.99	6.58%
(8D - (47th Street & Pinetree) - Off Street)	480-8000-344534	16	\$64.09	\$0.00	(64.09)	-100.00%
61 (8E - (41st Street & Alton) - Off Street)	480-8000-344535	40	\$2,939.88	\$3,722.49	782.61	26.62%
62 (8F - (41st Street & Jefferson) - Off Street)	480-8000-344536	. 30	\$520.45	\$511.51	(8.94)	-1. 72 %
X - (Collins - 64th to 79th St) - On Street	480-8000-344537	527	\$33,772.14	\$37,691.57	3,919.43	11.61%
84 (9A - (Harding & 71 st St) - Off Street)	480-8000-344538	48	\$1,284.22	\$0.00	(1,284.22)	-100.00%
92 (9B - (72nd St. & Collins) - Off Street) 92 (9B - (72nd St. & Collins) - Attended)	480-8000-344539	0	\$7,085.53	\$10,595.20		
Total	480-8000-344539	0 0	7,085.53	10,595.20	3,509.67	49.53%
85 (9C (Carlyle & 71st St) Off Street)	480-8000-344540	14	. \$43.12	\$39.52	(3.60)	-8.35%
. "					11	

CITY OF MIAMI BEACH PARKING DEPARTMENT ELECTRONIC METER REVENUE COMPARISON October 2010

LOCATION	Accounting Code	# of Spaces	2009 October	2010 October	Increase/ (Decrease)	% of Inc/(Dec)
P86 (9D - (Collins & 76th St) - Off Street)	480-8000-344541	33	\$1,186.39	\$1,561.20	374.81	31.59%
P83 (9E - (71st St. & Harding) - Off Street)	480-8000-344542	31	\$1,090.15	\$1,410.78	320.63	29.41%
P106 (9F - (75th & Collins) - Off Street)	480-8000-344543	106	\$3,622.96	\$4,072.09	449.13	12.40%
P25 (10A - (Lincoln Lane & Lenox) - Off Street)	480-8000-344544	. <i>7</i> 0	\$26,886.00	\$31,223.18	4,337.18	16.13%
I OB - (Lincoln Lane & Michigan) - Lease	480-8000-344545	0	\$14,583.33	\$16,355.14		
10B - (Lincoln Lane & Michigan) - Attended Total	480-8000-344545	0	0.00	0.00	1,771.81	12.15%
P27 (10C - (Lincoln Lane & Meridian) - Off Street)	480-8000-344546	141	\$42,861.83	\$63,188.43	20,326.60	47.42%
P20 (10D - (Lincoln Lane & Jefferson - W) - Off Street)	480-8000-344547	62	\$21,262.52	\$27,192.22	5,929.70	27.89%
P19 (10E - (Lincoln Lane & Jefferson - E) - Off Street)	480-8000-344548	19	\$7,415.40	\$8,689.87	1,274.47	17.19%
P18 (10F - (Lincoln Lane & Euclid) - Off Street)	480-8000-344549	36	\$14,711.57	\$17,676.08	2,964.51	20.15%
P21 (10G - (Lincoln Lane & Michigan) - Off Street)	480-8000-344550	21	\$6,748.49	\$7,855.63	1,107.14	16.41%
P15 (11X (Collins & 11th Street) - Off Street)	480-8000-344551	0	\$0.00	\$0.00	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	
P15 (11X - (Collins & 11th Street) - Attended) Total	480-8000-344551	<u> </u>	0.00	0.00	0.00	#DIV/OI
P12 (12X - (Washington & 9th Street) - Off Street)	480-8000-344552	23				
212 (12X - (Washington & 9th Street) - Attended)	480-8000-344552	0	\$4,612.17 0.00	\$9,406.92 0.00	4,794.75	103.96%
Total		23	4,612.17	9,406.92	4,794.75	103.96%
P13 (13X - (Washington & 10th Street) - Off Street) P13 (13X - (Washington & 10th Street) - Attended)	480-8000-344553 480-8000-344553	33 0	\$6,279.24 0.00	\$15,463.81 0.00		
Total		33	6,279.24	15,463.81	9,184.57	146.27%
15X - (16th to 18th East of Collins) - On Street	480-8000-344556	43	\$30,934.70	\$33,033.14	2,098.44	6.78%
15A - (Washington, 17th to 20th) - On Street	480-8000-344557	91	\$13,841.05	\$837.42	(13,003.63)	-93.95%
5B - (Convention Center Drive) - On Street	480-8000-344558	46	\$4,960.40	\$6,816.98	1,856.58	37.43%
6X - (25th to 32nd, E of Collins) - On Street	480-8000-344559	78	\$9,962.72	\$1 <i>7</i> ,123.82	7,161.10	71.88%
6A - (35th to 43rd, E of Collins) - On Street	480-8000-344560	117	\$9,486.16	\$20,789.73	11,303.57	119.16%
6B - (Indian Crk Dr, 27th to 32nd) - On Street	480-8000-344561	219	\$8,722.57	\$9,419.50	696.93	7.99%
6C - (Indian Crk - 33rd to 43rd) - On Street	480-8000-344562	230	\$12,469.08	\$13,082.17	613.09	4.92%
256 [16D - (Collins Ave & 34th St) - Off Street)	480-8000-344563	64	\$3,129.88	\$2,547.43		
256 (16D - (Collins Ave & 34th St) - Attended) Total	480-8000-344563	64	3,129.88	2,547.43	(582.45)	-18.61%
257 (16E - (Collins Ave & 35th St) - Off Street)	480-8000-344564	<i>7</i> 2	\$4,228.39	\$3,513.42		
57 (16E - (Collins Ave & 35th St) - Attended) Total	480-8000-344564	72	4.228.39	3,513.42	(714.97)	-16.91%
16 (17X - (Collins & 13th Street) - Off Street)	480-8000-344565	54	\$6,341.84	\$19,753.60	<i>(</i> , , , , , , , , , , , , , , , , , , ,	10.7170
16 (17X - (Collins & 13th Street) - Attended) Total	480-8000-344565	0	9,378.50	5,228.96		50.000
		54	15,720.34	24,982.56	9,262.22	58.92%
82 (18X - (Indian Crk & 65th St) - Off Street)	480-8000-344567	53	\$0.00	\$759.65	759.65	#DIV/0!
81 (18A - (Collins & 64th St) - Off Street) 81 (18A - (Collins & 64th St) - Attended)	480-8000-344568 480-8000-344568	67	\$3,182.48 0.00	\$6,888.56 0.00		
Total	•	67	3,182.48	6,888.56	3,706.08	116.45%
71 (19X - (Collins & 46th Street) - Off Street) 71 (19X - (Collins & 46th Street) - Attended)	480-8000-344569	449	\$20,186.17	\$65,719.81		
Total	480-8000-344569	449	38,970.10 59,156.27	90,129.16	30,972.89	52.36%
9A - (Collins & 46th Street) - On Street	480-8000-344570	19	\$1,382.74	\$442.44	(940.30)	

CITY OF MIAMI BEACH PARKING DEPARTMENT ELECTRONIC METER REVENUE COMPARISON October 2010

LOCATION	Accounting Code	# of Spaces	2009 October	2010 October	Increase/ (Decrease)	% of Inc/(Dec)
72 (19B - (Collins & 53rd Street) - Off Street)	480-8000-344571	158	\$5,132.59	\$7,454.36		
72 (19B - (Collins & 53rd Street) - Attended) Total	480-8000-344571	158	5,132.59	7,454.36	2,321.77	45.24
255 (20X - (Collins Ave & 27th St) - Off Street)	480-8000-344572	1,21	\$5,980.18	\$3,660.46		
255 (20X - (Collins Ave & 27th St) - Attended) Total	480-8000-344572	121	0.00 5,980.18	3,660.46	(2,319.72)	-38.79
91 (22X - (Carlyle & 72nd St) - Off Street)	480-8000-344574	45	\$741.62	\$745.27	3.65	0.49
2110 (23X - (83rd & Abbott) - Off Street)	480-8000-344575	25	. \$87.81	\$46.42	(41.39)	-47.14
24X - (Normandy Isle & Bay Dr) - On Street	480-8000-344576	102	\$5,339.58	\$5,997.33	657.75	12.32
89 (24A - (Normandy Isle & Bay Dr) - Off Street)	480-8000-344577	26	\$925.30	\$1,260.10	334.80	36.18
288 (24B - [Normandy Isle & Vendome] - Off Street	480-8000-344578	22	\$645.10	\$731.62	86.52	13.41
187 (24C - (Normandy Isle & Bay Rd S/S) - Off Street)	480-8000-344579	33	\$830.46	\$1,325.68	495.22	59.63
90 (25X - (Bonita Drive & 71st St) - Off Street)	480-8000-344580	15	\$480.90	\$370.08	(110.82)	-23.04
26X - (Collins, 79th to 87th Terr) - On Street	480-8000-344581	283	\$7,635.48	\$4,860.25	(2,775.23)	-36.35
26Z - (Collins & 87th Street) - Off Street	480-8000-344616	15	\$186.52	\$150.32	(36.20)	-19.419
26 (10X - (Lincoln Lane & Lenox) - Off Street) 26 (10X - (Lincoln Lane & Lenox - Attended)	480-8000-344582 480-8000-344582	99 0	\$37,935.52 0.00	\$44,224.50 0.00		
Total		99	37,935.52	44,224.50	6,288.98	16.589
108 (26A - (Collins & 80th Street) - Off Street) 108 (26A - (Collins & 80th Street) - Attended)	480-8000-344584 480-8000-344584	62 0	\$982.69 0.00	\$1,107.14		
Total	400-0000-344304	62	982.69	1,107.14	124.45	12.66
111 (26B - (Collins & 84th Street) - Off Street)	480-8000-344585	62	\$1,182.30	\$878.84	(303.46)	-25.67
46 (4E (Purdy & 18th Street) Off Street)	480-8000-344586	39	\$7,991.81	\$8,186.04		
46 (4E (Purdy & 18th Street) - Attended) Total	480-8000-344586	39	7,991.81	8,186.04	194.23	2.439
58 (8G - (40th Street & Royal Palm) - Off Street)	480-8000-344592	43	\$2,812.05	\$2,012.23	(799.82)	-28.449
59 (8H - (40th Street & Prairie) - Off Street)	480-8000-344594	71	\$2,751.08	\$1,685.86	(1,065.22)	-38.729
107 (26C - (Collins & 79th Street) - Off Street)	480-8000-344600	34	\$271.89	\$423.77	151.88	55.869
109 (26D - (Collins & 83rd Street) - Off Street)	480-8000-344601	95	\$162.79	\$119.57	(43.22)	-26.559
109 (26D - (Collins & 83rd Street) - Attended) Total	480-8000-344601	95	\$0.00 162.79	\$0.00 119.57	(43.22)	-26.55
1 (SLSPOO - (South Point Lot) - Off Street)	480-8000-344602	215	\$26,246.84	\$25,591.40	(17.1=4)	
1 (SLSPOO - (South Point Lot) - Attended) Total	480-8000-344602	215	0.00 26,246.84	8,491.60 34,083.00	7 024 14	29.869
5 (4th & Alton Lot - Off Street)	480-8000-344604	21		•	7,836.16	
A - 1833 Bay Road - Off Street		_	\$976.11	\$949.98	(26.13)	-2.689
	480-8000-344608	0	\$0.00	\$0.00	0.00	#DIV/C
D - 10-11th & Collins (Lease)	480-8000-344529	0	\$3,500.00	\$3,663.55	163.55	4.679
22 (10H - (Lincoln Rd. So. & Lenox) - Off Street)	480-8000-344611	0	\$6,229.94	\$7,518.65	1,288.71	20.699
4A - 16th Street & Washington (Lease)	480-8000-344555	0	\$14,583.33	\$16,355.14	1,771.81	12.159
4 - (137 Washington Avenue) - Off Street	480-8000-344516	0	\$4,057.73	\$5,523.19	1,465.46	36.129
50 - (24th Street & Flamingo Drive) - Off Street	480-8000-344619	23	\$0.00	\$0.00	0.00	#DIV/0
51 - (23rd Street & Liberty Avenue East) - Off Street 51 - (23rd Street & Liberty Avenue East) - Attended	480-8000-344620 480-8000-344620	20 0	\$7,936.98	\$7,685.62		
Total	400-000-044020	-	7,936.98	7,685.62	(251.36)	-3.179
52 - (23rd Street & Liberty Avenue West) - Off Street	480-8000-344621	35	\$8,574.70	\$10,195.04	*	
52 - (23rd Street & Liberty Avenue West) - Attended Total	480-8000-344621	0 _	0.00 8,574.70	10,195.04	1,620.34	18.90%
85 - (71 st Street & Byron) - Off Street	480-8000-344618	o	\$414.37	\$378.76		
85 - (71st Street & Byron) - Attended Total	480-8000-344618	0 -	0.00 414.37	<u>0.00</u> 378.76	(35.61)	-8.59%
G7 (MMPF-1755 Meridian Ave)	480-8000-344414		0.00	0.00	0.00	#DIV/0
•			3.00	0.00	0.00	

NOTE: SLSP00-(SOUTH POINT LOT) CLOSED DURING AUGUST/2007. NOTE: ZONES WITH MULTI-SPACE PAYSTATIONS ARE ITALICIZED.

City of Miami Beach Parking Department Profit & Loss Statement Garages & Lots - FY09/10

17th Street Garage - 2G	.26													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010
														T T T
Revenue-Ticket	480-8000-344583	235,239.47	223,264.49	247,140.15	280,683.18	276,852.33	312,994.40	311,041.08	234,529.94	187,814.96	211,132.71	187,982.24	172,263.53	2,880,938.48
Revenue - Space Rental	480-8000-344583	5,950.00	5,950.00	5,950.00	5,950.00	5,950.00	00:00	00'0	00:00	00.0	0.00	0.00	00'0	29,750.00
Revenue-Monthly Permits	480-8000-344514	63,350.00	63,350.00	62,300.00	64,260.00	62,440.00	62,930.00	64,750.00	66,640.00	71,190.00	80,570.00	77,280.00	76,300.00	815,360.00
	17th St 2G REVENUE (Sales Tax Excluded)	304,539.47	292,564.49	315,390.15	350,893.18	345,242.33	375,924.40	375,791.08	301,169.94	259,004.96	291,702.71	265,262.24	248,563.53	3,726,048.48
Expenses		25 035 00			;									
Attendant/Cashier Labor		49,028,19	51,350,24	26,769.73	19,889 //	19,466.69	24,077.76	18,350.51	18,357.66	19,652.70	24,000.28	19,643.37	24,820.40	256,561.34
FP&L		8,370.27	8,847.04	9,055.86	7,774.65	6,694.38	6,685.69	6,779.65	7,407.77	6,986.11	7.637.50	7.536.65	7,965 03	91 740 60
Kevenue Control Equipment Maintanance	Maintanance	4,295.40	4,045.40	6,250.15	4,045.40	4,045.40	6,723.40	4,045.40	4,347.40	4,649.40	4,649.40	4,137.05	5,442.90	56,676,70
Armed Guard Kevenue Pickup	۵	485.33	485.33	485.33	485.33	483.55	483.55	485.33	485.33	485.33	485.33	485.33	485.33	5,820.40
Lievator Maintenance		00.0	0.00	0.00	00:0	00.0	2,500.00	1,250.00	7,685.00	3,037.50	1,800.00	3,222.00	1,250.00	20,744.50
Landscape and Lot Maintenance	nce	362.50	362.50	362.50	362.50	362.50	362.50	00:00	0.00	352.00	176.00	176.00	220.00	3,099.00
Carage Cleaning/Maintenance		8,706.67	8,706.67	8,706.67	8,706.67	8,706.67	13,606.67	8,706.67	8,706.67	8,706.67	13,606.67	8,706.67	8,706.67	114,280.04
-	17th St 2G EXPENSES	92,007.11	94,570.90	113,500.75	90,526.51	95,327.81	120,165.56	92,881.20	95,665.10	95,554.61	109,251.49	89,434.18	105,898.96	1,194,784.18
	17th St. PROFIT/(LOSS)	212,532.36	197,993.59	201,889.40	260,366.67	249,914.52	255,758.84	282,909.88	205,504.84	163,450,35	182.451.22	175.828.06	142 664 57	2 531 264 30
												-	10110101	2011001

LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010 TOTAL
City Hall Garage - G7														
Revenue-Ticket	480-8000-344407	00.00	93.66	13,728.05	18,688.74	37,535.53	30,225.26	27,693.45	7,565.38	8,429.91	8,539.27	5,218.67	7,894.39	166,152.31
Revenue - Space Rental	480-8000-344409	00:00	00.00	0.00	00.0	0.00	4,280.00	5,350.00	4,280.00	0.00	4,280.00	6,250.00	20,000.00	74,440.00
Revenue-Monthly Permits	480-8000-344408	0.00	0.00	0.00	770.00	1,190.00	5,670.00	4,760.00	4,760.00	7,140.00	7,140.00	7,070.00	5,460.00	43,960.00
	CHG - G7 REVENUE (Sales Tax Excluded)	0.00	633.66	13,728.05	19,458.74	38,725.53	40,175.26	37,803.45	16,605.38	16'695'51	19,959.27	18,538.67	63,354.39	284,552.31
Expenses														
Security Personnel		00.00	00.00	00:00	3,418.53	3,415.98	4,270.78	3,412.80	3,415.98	4,707.06	5,716,74	3,988.40	4.990.75	37,337,02
Attendant/Cashier Labor		00.00	00:00	12,267.97	9,552.91	11,360.78	13,522.59	10,867.09	9,712.53	9,427.99	8,081.63	6,783.85	8,498,85	100,076,19
rrel		00.00	00.00	7,414.84	4,088.29	9,191.51	8,340.41	8,067.22	11,067.98	11,279.45	11,867.70	10,672,43	10,846.55	92,836,38
Kevenue Control Equipment Maintanance	Aaintanance	0.00	0.00	179.00	00.0	00:0	00.0	00.0	00.0	00.0	00.00	000	000	179.00
Armed Guard Kevenue Pickup	c	00.0	00:00	0.00	0.00	00:00	00:0	00.0	00:00	00.00	0.00	0000	000	00.0
Elevator Maintenance		00.00	0.00	0.00	00:0	00.0	0.00	00.00	00:00	00.0	0.00	000	000	000
Landscape and Lot Maintenance	. apr	00:00	0.00	00:00	0.00	00.00	00.0	00.0	00.00	0.00	00'0	00.0	176.00	176.00
Sarage Cleaning/Maintenance	ice	00.0	0.00	6,213.51	7,000.00	7,000.00	8,000.00	7,775.00	9,991.00	9,721.00	9,721.00	9.721.00	9.721.00	84.863.51
	CHG - G7 EXPENSES	00:0	00:00	26,075.32	24,059.73	30,968.27	34,133.78	30,122.11	34,187.49	35,135.50	35,387.07	31,165.68	34,233.15	315,468.10
	CHG PROFIT/(LOSS)	00'0	633.66	.12.347.27	00 00 97	7 757 7	97 (707)	7 401 34	17 603 11	03 373 01	00 207 31			

City of Miami Beach Parking Department Profit & Loss Statement Garages & Lots - FY09/10

<u>9</u>
ge
ä
ð
ee
꺆
Ħ

OI - affining lealing in 7	2													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010
	٠													IOIAL
7th Street Garage - 1G														
Kevenue-licket	142-8000-344404	166,039.38	148,840.19	137,367.28	171,403.76	161,802.83	214,551.39	181,189.74	221,905.62	152,613.93	193,339.21	163,528.93	144,045.78	2,056,628.04
Revenue-Monthly Permits	142-8000-344404	16,350.00	16,350.00	16,425.00	16,350.00	16,350.00	16,650.00	17,925.00	16,875.00	16,650.00	16,650.00	16,650.00	16,650.00	199,875.00
	7th Street Garage - 1G R 182,389.38 (Sales Tax Excluded)	182,389.38	165,190.19	153,792.28	187,753.76	178,152.83	231,201.39	199,114.74	238,780.62	169,263.93	209,989.21	180,178.93	160,695.78	2,256,503.04
Expenses														
Security		14,635.65	14,642.28	18,299.17	14,082.29	14,079.76	17,584.60	14,076.60	14,079.76	15,291.32	18,065.73	14,624.80	18,316,03	187 777 99
Ariendani/Cashier Labor		26,730.61	26,661.66	30,563.38	27,418.54	29, 193.16	36,807.32	29,039.45	27,238.68	27,201.81	48,955.40	37,164.32	37,817.46	384,791,79
Landscape Maintenance		5,934.80	2,967.40	1,483.70	1,483.70	1,483.70	1,483.70	00.0	00.00	4,656.54	14,062.00	9,313.08	20,153.08	63,021.70
Pavenue Control Faminana Mainte	#	3,834.38	3,465.07	3,290.13	4,360.67	2,678.90	2,273.50	2,540.21	2,866.31	3,205.36	3,241.16	3,394.44	3,235.16	38,385.49
Gardee Cleaning (Maintaine)	Mainienance	2,628.75	7,007.31	1,057.75	878.75	1,180.75	878.75	1,237.50	5,560.75	1,180.75	878.75	878.75	878.75	18,704.31
Armed Guard Revenue Pickus	י בפ	7,080.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	7,086.13	85,033.56
Flevator Maintenance	1	465.33	483.33	485.33	485.33	485.00	485.33	485.33	485.33	485.33	485.33	485.33	485.33	5,823.63
Surveillance System Maintenance	90	67:565'1	1,400.54	1,210.29	2,695.29	1,210.29	1,884.04	1,595.29	3,335.29	1,760.29	1,210.29	1,210.29	1,210.29	20,883.48
	Tak Ga Comment 10 round	0.00	0.00	0.00	0.00	00:0	561.15	00:00	920.00	212.50	0.00	255.00	00.00	1,948.65
	/m Sr. Garage - 1G EXPE 62,931.14	62,931.14	58,/38.72	63,475.88	58,490.70	57,397.69	69,044.52	15.090,95	61,572.25	61,080.03	93,984.79	74,412.14	89,182.23	806,370.60
	7th St 1G Estimated De 59,500.00	59,500.00	59,500.00	99,500.00	59,500.00	59,500.00	59,500.00	59,500.00	59,500.00	59,500.00	29,500.00	59,500.00	29,500.00	714,000.00
	7th St 1G PROFIT/(LOS:	59,958.24	46,951.47	30,816.40	90,763.06	61,255.14	102,656.87	83,554.23	117,708.37	48,683.90	56,504.42	46,266.79	12,013,55	736, 132, 44
		!												

_
≥
⋖ŏ
ш
2 ∀
•
₽
Lots
Street
Š

LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010
														IOIAL
17th Street Lots - 5A East and West	ist and West													
Revenue-Ticket	480-8000-344515	29,620.58	22,546.73	19,584.11	17,257.01	26,014.01	4,135.52	00.00	00.00	00.00	00.00	00.00	0.00	119,157.96
Revenue-Valet	480-8000-344515	0.00	00.00	0.00	00.00	00:00	0.00	0.00	00.0	00:0	00:00	00.0	00:0	0.00
Revenue-Monthly Permits	480-8000-344596	5,250.00	5,250.00	5,110.00	5,110.00	4,760.00	0.00	00:00	0.00	00:00	00:00	00.00	0.00	25,480.00
	17th Lots - 5A REVENUE (Sales Tax Excluded)	34,870.58	27,796.73	24,694.11	22,367.01	30,774.01	4,135.52	00.0	0.00	00.00	00:00	0.00	00.0	144,637.96
Expenses Security Personnel		1,144.80	1,144.80	1,144.80	1,144.80	1,144.80	1,144.80	00.0	00.0	000	000	00	000	A 848 BO
Attendant/Cashier Labor Revenue Control Fauinment Maintenance	Maintenance	13,841.83	13,824.48	7,443.15	4,649.90	5,347.27	4,597.75	0.00	0.00	00.00	00.0	00:0	00.00	49,704.38
Landscape and Lot Maintenance	9200	8.0	800	800	9.00	000	00:0	00:0	0.00	00.0	00.0	00:00	0.00	00.00
FP&L	3	301.48	301.48	30.748	000	0.00	0.00	00.0	00.0	00.0	00.0	00.00	0.00	00.00
	1 4 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1			071.40	371.40	371.40	391.48	00.0	0.00	0.00	000	0.00	0.00	2,348.88
	17th Lots - 5A EXPENSES 5,378.	15,378.11	15,360.76	8,979.43	6,186.18	6,883.55	6,134.03	00.0	00.00	00:00	00:00	00:0	00.0	58,922.06
	17th Lots PROFIT/(LOSS) 19,492.47	19,492.47	12,435.97	15,714.68	16,180.83	23,890,46	1,998.51	0000	000	000	000	000		06 715 00
							10:07:4	80.0	20.0	00.0	8.0	0.00	0.00	05,715,90

City of Miami Beach Parking Department Profit & Loss Statement Garages & Lots - FY09/10

12th Street Garage - 2A	- 2A													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010 TOTAI
12th Street Garage - 2A			,											
Revenue-Ticket	480-8000-344504	26,280.38	29,058.88	23,682.21	36,494.38	34,300.96	45,435.49	33,199.09	43,680.36	33,473.80	35,414.01	35,597.18	30,714.03	407,330.77
Revenue-Monthly Permits	480.8000.344593	5,810.00	5,810.00	4,900.00	90.060,9	6,930.00	5,810.00	6,230.00	6,230.00	5,250.00	5,110.00	5,180.00	5,250.00	00.009,89
	12th St 2A REVENUE (Sales Tax Excluded)	32,090.38	34,868.88	28,582.21	42,584.38	41,230.96	51,245.49	39,429.09	49,910.36	38,723.80	40,524.01	40,777.18	35,964.03	475,930.77
Expenses Security Personnel		15.618	820.88	1,025.34	959.15	704.22	880.44	703.57	704.22	4,437.40	976.95	822.23	1,028.86	13,882.77
Affendant/Cashier Labor		11,868.97	11,810.27	14,757.61	13,419.20	13,154.90	14,828.88	11,839.62	11,877.36	12,783.90	14,862.42	11,898.32	14,134.33	157,235.78
Revenue Control Equipment Maintanance	rt Maintanance	933.55	933.55	1,112.55	933.55	933.55	933.55	933.55	933.55	933.55	933.55	933.55	933.55	11,381,60
Elevator Maintenance		162.58	162.58	162.58	162.58	162.58	162.58	162.58	162.58	162.58	162.58	162.58	162.58	1,950.96
Cardge Cleaning/Maintenance	nce	00.006,1	00:006,1	00.006,1	1,900.00	1,900.00	2,900.00	1,900.00	2,170.00	2,400.00	1,900.00	1,900.00	1,900.00	24,570.00
Armod Guard Pougan Bishin		225.00	225.00	225.00	225.00	225.00	225.00	0.00	00:0	1,056.00	528.00	528.00	90.099	4,122.00
Amiled Godin Revenue Fickly		485.33	485.33	483.55	483.55	483.55	485.33	485.33	485.33	485.33	485.33	485.33	485.33	5,818.62
	12th St 2A EXPENSES	16,503.48	16,446.15	19,775.17	18,191.57	17,672.34	20,524.32	16,133.19	16,441.58	22,367.30	19,957.37	16,838.55	19,413.19	220,264.21
	12th St 2A PROFIT/(LO: 15,586.90	15,586.90	18,422.73	8,807.04	24,392.81	23,558.62	30,721.17	23,295.90	33,468.78	16,356.50	20,566.64	23,938.63	16,550.84	255,666.56

13th Street Garage - 17A	1ZA													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010 TOTAL
13th Street Garage - 17A Revenue-Ticket	4 480-8000-3445-66	70,108.41	76,040.20	66,412.13	88,101.87	88,648,60	102.694.37	88.194.41	94 037 42	78.123.37	93 882 81	84 844 82	NZ 210 0Z	1 002 004 15
Revenue-Monthly Permits	480-8000-344527	10,570.00	10,570.00	9,590.00	10,290.00	10,220.00	9,870.00	10,150.00	9,870.00	10,150.00	9,870.00	9,800.00	10,080.00	121,030.00
	13th St 17A REVENUE (Sales Tax Excluded)	80,678.41	86,610.20	76,002.13	78'166'86	09'898'86	112,564.37	98,344.41	103,907.42	88,273.37	103,752.81	94,644.82	80,997.74	1,123,036.15
Expenses Security Personnel Attendant/Cashire Labor landscape Maintenance FPRL Revenue Control Equipment Maintenance Elevator Maintenance Fixed Guard Revenue Pickup Garage Cleaning/Maintenance Surveillance System Maintenance 13th St.	lenance 3th St 17A EXPENSES	1,749.14 13.878.25 237.50 2,494.36 1,096.05 405.00 485.33 1,900.00 0.00 22,245.63	1,752.08 13.855.11 237.50 23.60.73 933.55 210.00 485.33 1,900.00 2,634.30	2,188.47 17,213.64 237.50 2,556.69 1,112.55 210.00 485.33 1,900.00 0.00 25,884.18	1,885.76 14,871.11 237.50 2,036.62 933.55 2,950.00 485.33 1,900.00 25,299.87	1,503.04 14,876.31 237.50 2,060.78 933.55 210.00 483.55 1,900.00 0.00 22,204.73	1,879.15 18,561.30 237.50 1,905.34 933.55 210.00 485.00 2,400.00 820.00 27,431.84	1,501,64 14,047,72 0.00 1,918.87 1,292.30 1,423.00 485.33 1,900.00 0.000 22,568.86	1,503.04 13,870.15 0.00 1,920.90 933.55 4,472.00 2,170.00 0.00 25,354.97	2,788.36 14,588.73 1,056.00 2,030.76 933.55 2,675.00 485.33 2,600.00 0.00	2,085,10 17,458,86 528,00 2,090,05 933,55 210,00 485,33 1,900,00 0,00 25,690,89	1,754 88 13,810.57 528.00 1,709.61 933.55 210.00 4465.33 1,900.00 0.00 21,331.94	2, 195, 91 16,806,86 660,00 2,053,09 933,55 210,00 1,900,00 0,00 25,244,74	22,786.57 183,838.61 4,197.00 25,017.80 11,902.85 13,395.00 5,821.85 24,070.00 820.000

City of Miami Beach Parking Department Profit & Loss Statement Garages & Lots - FY09/10

Ho - anno lague - ou	- 0A													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010 TOTAL
42nd Street Garage - 8A Revenue-Ticket	1A 480-8000-344531	3,282.24	2,883.18	3,205.59	3,275.65	8,215.90	4,336.38	3,367.22	3,312.09	3,841.06	3,971.87	4,823.21	4,946.52	49,460.91
Revenue-Monthly Permits	480-8000-344595	30,800.00	30,800.00	27,440.00	24,220.00	25,830.00	25,900.00	26,110.00	26,950.00	24,640.00	23,450.00	23,590.00	21,980.00	311,710.00
	42nd St 8A REVENUE (Sales Tax Excluded)	34,082.24	33,683.18	30,645.59	27,495.65	34,045.90	30,236.38	29,477.22	30,262.09	28,481.06	27,421.87	28,413.21	26,926.52	361,170.91
Expenses Security Personnel		3,791.83	3,798.20	4,744.21	3,260.42	3,258.33	4,073.67	3.255.30	3,258,33	3.261.36	4.520.17	3 804 32	4 760 40	45 786 54
Attendant/Cashier Labor FP&L		4,212.58	4,309.74	5,295.22	4,327.09	5,475.66	5,357.68	4,361.64	4,285.45	4,436.66	5,270.93	4,209.11	5,215.13	56,756.89
Revenue Control Equipment Maintenance	Maintenance	1,244.74	1,244.74	1,423.74	1,244.74	1,905.49	1,911.00	1,918.22	2,076.55	2,213.17	2,198.19	2,496.47	2,321.04	27,669.98
Elevator Maintenance		450.00	2,220.00	450.00	450.00	450.00	450.00	450.00	450.00	450.00	450.00	450.00	450.00	7,170.00
Landscape Maintenance		462.50	462.50	462.50	462.50	462.50	462.50	00.0	00.00	880.00	440.00	440.00	550.00	5,085.00
Surveillance System Maintenance	ance	2,700.00	2,700.00	2,700.00	2,700.00	2,700.00	3,700.00	2,700.00	2,700.00	2,700.00	2,700.00	2,700.00	2,700.00	33,400.00
	42nd St 8A EXPENSES	15,423.22	17,429.81	17,878.13	14,843.72	16,329.69	382.30 17,582.09	14,288.65	14,015.07	0.00	0.00 16,824.03	15,344.64	17,241.31	382.50
	42nd St. PROFIT/(LOSS)	18,659.02	16,253.37	12,767.46	12,651.93	17,716.21	12,654.29	15,188.57	16,247.02	13,295.13	10,597.84	13,068.57	9,685.21	168,784.62

16th Street Garage - Anchar

ימוים באסוים ויים ויים	DIDIO													
LOCATION	ACCOUNTING CODE	2009 October	2009 November	2009 December	2010 January	2010 February	2010 March	2010 April	2010 May	2010 June	2010 July	2010 August	2010 September	FY 2009/2010
16th Street - Anchor Garage	900													2
Revenue-Ticket	463-8000-344911	114,148.53	126,963.56	119,479.43	142,969.14	166,071.01	196,165.94	180,250.47	185,281.31	142,967.31	192,778.51	173,062.62	143,948.59	1,884,086.42
Revenue - Valet	463.8000.344587	18,208.41	22,337.37	24,598.60	25,908.87	29,995.32	31,492.98	26,655.66	18,829.91	22,082.24	30,728.04	29,065.88	17,758.40	307,661.68
Revenue-Monthly Permits	463-8000-344903	40,000.00	25,300.00	22,650.00	45,043.50	19,864.00	18,800.00	41,686.45	43,600.00	50,000.00	46,600.00	46,500.00	45,700.00	445,743.95
	16th St. Anchor - REVENL 172,356.94 (Sales Tax Excluded)	. 172,356.94	174,600.93	166,728.03	213,921.51	215,930.33	246,458.92	248,592.58	257,711.22	215,049.55	270,106.55	248,628.50	207,406.99	2,637,492.05
Expenses														50011
Security Personnel		4,911.04	4,919.28	6,144.52	4,223.21	4,220.07	5,276.07	4.216.14	4 220 07	5 507 92	5 854 36	5,610,01	6.410.00	61 523 40
Attendant/Cashier Labor		22,850.72	23,284.04	29,680.00	23,485.59	24,632.43	29,984.90	25,158,68	22,890,34	23.360.82	26 775 75	21 091 57	25 922 80	200 117 64
FP&L		3,108.99	3,278.62	2,728.16	2,671.93	2,444.69	2.520.86	2 593 55	2 887 90	2 614 67	2 684 74	3 015 00	2 484 74	23 23 4 84
Revenue Control Equipment Maintanance	laintanance	1,712.50	1,462.50	1,641.50	1,821.25	1,462.50	1 462 50	1 82 1 25	1 462 50	1 462 50	1 462 50	1 462 50	1 462 50	19 404 50
Armed Guard Revenue Pickup		485.33	485.33	485.33	485.33	485.33	485.33	485.33	485 33	485.33	485.33	485 33	485.33	5 823 04
Elevator Maintenance		1,535.70	1,535.70	1,535.70	1,920.70	1,948.20	1,535.70	1,535.70	1.920.70	2.553.20	1.535 70	1.535.70	1 825 70	20,020,00
Landscape and Lot Maintenance	ICe	152.00	190.00	152.00	152.00	152.00	190.00	0.00	255.00	820.70	425.00	4.158.75	340.00	6.987.45
Carage Cleaning/Maintenance	e e	6,528.20	6,528.20	6,528.20	6,528.20	6,528.20	10,028.20	6,528.20	7,281.50	10,028.20	6,528.20	6,528.20	6,528.20	86,091.70
Sanifation (Waste Kemoval)		242.14	242.14	242.14	242.14	253.27	253.27	253.27	253.27	254.33	461.59	254.33	254.33	3,206.22
Fire Aldrim Service		385.00	320.12	250.00	250.00	250.00	250.00	250.00	250.00	2,259.88	250.00	250.00	250.00	5,215,00
Surveillance System Maintenance	nce	00:0	00:0	0.00	0.00	0.00	2,090.00	00.00	00:00	00.00	00:0	00:00	00.00	2,090.00
	16th St Anchor EXPENS 41,911.62	41,911.62	42,245.93	49,387.55	41,780.35	42,376.69	54,076.83	42,842.12	41,906.61	49,347.55	46,463.17	44,393.28	46,173.50	542,905.20
	16th St. PROFIT/(LOSS)	130,445.32	132,355.00	117,340.48	172,141.16	173,553.64	192,382.09	205,750.46	215,804.61	165,702.00	223,643,38	204.235.22	161,233,49	2 094 586 85



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

COMMISSION MEMORANDUM

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jorge M. Gonzalez, City Manager

DATE:

December 8, 2010

SUBJECT: INFORMATIONAL REPORT TO THE MAYOR AND CITY COMMISSION, ON FEDERAL, STATE, MIAMI-DADE COUNTY, U.S. COMMUNITIES, AND ALL EXISTING CITY CONTRACTS FOR RENEWAL OR EXTENSIONS IN THE NEXT

180 DAYS.

The City Commission adopted Resolution No. 2000-24141, which provided that all existing City contracts for renewal or extensions, which by their terms or pursuant to change orders exceed \$10,000, and all extensions or renewals of such contracts, shall be presented as an informational report to the Mayor and City Commission, at least 180 days prior to the contract extension or renewal date. Subsequent thereto, the City Commission adopted Resolution No. 2001-24332, changing the reporting requirement from \$10,000 to \$25,000.

The Administration in addition to reporting on all existing City contracts, will now report information relative to Miami-Dade County, State of Florida, U.S. Communities and Federal GSA contracts that are approved for utilization by the City Manager. Pursuant to information contained in Miami-Dade County, State of Florida, U.S. Communities and Federal General Services Administration (GSA) bid list, the following are contracts that will expire within the next 180 days:

	DESCRIPTION	VENDOR	EXPIRATION DATE	RENEWAL TERMS
1.	For Removal and Disposal of Derelict Vessels	Blue Water Marine Services, Inc.	5/6/2011	2 One year options to renew
2.	For Removal and Disposal of Derelict Vessels	H20 Tow	5/6/2011	2 One year options to renew
3.	For Removal and Disposal of Derelict Vessels	Biscayne Towing & Salvage, Inc.	5/6/2011	2 One year options to renew

JMG:PDW:GL

T:\AGENDA\2010\December 8\Consent\180DayReport.doc

	DESCRIPTION	VENDOR	EXPIRATION DATE	RENEWAL TERMS
4.	For Removal and Disposal of Derelict Vessels	Dock and Marine Construction, Inc.	5/6/2011	2 One year options to renew
5.	Unarmed Security Guard Services	Security Alliance	4/30/2011	3 One year options to renew
6.	The Review of Water, Sewer, and Stormwater utility for un-read, mis-read, and un-metered services	Meter Reading Specialist, Inc.	5/28/2011	None
7.	Purchase and Installation of Video Monitoring Equipment for City Garages	Gisnet Telecom, Inc.	5/8/2011	2 Option years to renew
8.	For Elevator Inspection Services	Dade Inspections, Inc.	4/31/2011	One Options years to renew
9.	For Elevator Inspection Services	Miami Elevator Inspection	4/31/2011	One Options years to renew
10.	For Elevator Inspection Services	Vertical Assessment Associates, LLC	4/31/2011	One Options years to renew



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

COMMISSION MEMORANDUM

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jorge M. Gonzalez, City Manager

DATE:

December 8, 2010

SUBJECT: STATUS REPORT ON THE PALM & HIBISCUS ISLANDS UNDERGROUND UTILITIES PROJECT

At its May 13, 2009 meeting, the City Commission adopted Resolution No. 2009-27065 – A Resolution Endorsing, As Required Pursuant To Section 18-2 Of The Miami-Dade County Code, The Creation By Miami-Dade County Of A Special Taxing District For Palm Island And Hibiscus Island, Respectively, For The Undergrounding Of Overhead Utilities, Subject To And Contingent Upon Compliance With And Satisfaction Of The Requirements For The Creation Of Special Taxing Districts, As Set Forth In Chapter 18 Of The Miami-Dade County Code.

These overhead utilities are electric (FPL), telephone (AT&T), and cable TV (Atlantic Broadband). Construction plans are complete, and the current estimated cost is \$1,348,344 for Palm Island and \$2,151,602 for Hibiscus Island, for a total cost of \$3,499,946. This cost is for the excavation, trenching, conduit, pull boxes, transformer pad construction, and road reconstruction by a City-hired contractor. It also includes the utilities' costs to furnish and install their wire and equipment and to provide a working system. The cost estimate represents approximately \$1.5 million in savings due to procurement by the City in lieu of the utilities.

The Palm-Hibiscus-Star Islands Association (HOA) has elected to pursue the creation of a Special Taxing District with Miami-Dade County in order to finance the expense associated with its underground utilities project. The following is a synopsis of the County process for creating a Special Taxing District.

Step I – The Petition Process

An HOA must request the creation of a Special Taxing District. A petition is then provided by the County to the HOA. Within four months, the HOA must gather a minimum of 50% of resident property owners.

Status:

On April 26, 2010, Miami-Dade County Special Taxing Division provided the HOA official notification of the successful Petition drives on both Palm and Hibiscus Islands. On April 9, 2010, the HOA submitted the signed petition to Miami-Dade County Public Works Department Special Taxing Districts Division.

Step II – Cost and Feasibility Study

Upon petition validation, the County prepares a Cost and Feasibility Study and holds an informational meeting with the residents where the County discusses the proposed improvements, cost estimates, and assessment method. This informational meeting is likely to be held two weeks after the petition is validated.

Step III - District Creation

A public hearing is held at which the Miami-Dade County Board of County Commissioners (BCC) considers the district creation ordinance. The public hearing is likely to be held two months after the informational meeting. At this time, new binding estimates must be received from the utilities.

Status:

On April 26, 2010, Miami-Dade County Special Taxing Division provided the HOA official notification of the successful Petition drives on both Palm and Hibiscus Islands. The next steps in the process include a meeting with the residents at a public location to be coordinated and advertised by the HOA. This meeting is anticipated to be held in early June followed by two County Commission Meetings—one in June and one in July, with the July meeting to include a Public Hearing. A forty five (45) day period between the Public Hearing and the election is required in order to give persons the opportunity to register to vote. The meeting in June was cancelled by Miami-Dade County and the Public Hearing set for July was not scheduled since the County Attorney could not prepare the ordinance due to lack of financial information related to obtaining County bond proceeds. In addition, the public hearing scheduled for September 1, 2010 was cancelled and will be re-schedule for September 21, 2010. The Miami-Dade County Commission passed unanimously on September 21, 2010 the Ordinances to create Special Taxing Districts for both Palm Island and Hibiscus Island. The matter will now go forward with an Election on December 7, 2010 of registered voters as the final step in the process to obtain funding from the County.

Step IV - District Ratification

Ballots are mailed to all registered voters within the district. A majority vote of returned ballots is needed to ratify district creation. Ballots are likely to be mailed two months after the Board of County Commissioners endorses the creation of a Special Taxing District.

Step V – Collection of Special Assessments

The assessment of each property owner was calculated and a public hearing was held to address inequities. The public hearing was held on September 21, 2010. If the majority of the votes approves Commission action then distric is valid and collection thru the tax roll will begin. This will be retroactive to November 2010 tax bill.

Step VI - Commencement

The City and County negotiate an interlocal agreement to build the improvements, and the County must review and approve the design and bids. An interlocal agreement might be negotiated one or two months after the public hearing. The plan and bid review would occur simultaneously. The construction phase can begin once an interlocal agreement is executed and the plans and bids are approved. Notices to Proceed would then likely be issued one of two months after the execution of the interlocal agreement.

JMG\JGG\CC\MR\AJC



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

COMMISSION MEMORANDUM

TO:

Mayor Matti Herrera Bower and Members of the City Commission

FROM:

Jorge M. Gonzalez, City Manager

DATE:

December 8, 2010

SUBJECT: CIP Monthly Construction Project Update

Attached you will find the monthly update, through the 18th of November, for active City of Miami Beach construction projects under the purview of the CIP Office.

Attachment

Status through November 18, 2010

Scope of Work

Construction Status

All six overhead doors and motors are completed and installed. Interior

Fire Station 1 - Interior and Bay Doors

Hernandez, M

Project Name

Project Mgr.

District

Replacement

properly. The metal rails are also showing signs of age. The interior hollow metal and hollow wood core doors are aged, not fire rated, beyond rated life expectancy, general, not working properly. The exterior overhead, scratched, utilizing non compliant hardware and, in vehicle bay, doors are aged and damaged. The hardware is worn and some doors do not close

Renovation of the South-East small hydraulic elevator and bring it up to current codes.

City Hall Southeast Small Passenger

Elevator

Middle Beach Iglesias, E.

Preconstruction meeting took place July 28, 2010. Elevator shop doors are being ordered.

August 30, 2010 The elevator machine room exhaust fan specifications elevator machine room scope of work including new drywall ceiling, new electrical panel and new A/C unit with exterior louver was completed by drawings reviewed & approved. Elevator stored materials were verified lead in the machine room was relocated on September 25, 2010. The were approved by Luis Mojicar on September 23, 2010. Fire sprinkler The electrical scope of work in the machine room commenced on at Oracle's warehouse on August 27, 2010.

emporarily back in service from October 22, 2010 through November 3, 2010 due to scheduling conflicts with Oracle's crew. The elevator will remain shut down until December 3, 2010.

Oracle's scope of work within the elevator shaft and in the cab is The elevator was shut down on September 20, 2010. It was

October 31, 2010.

headers, tracks, call buttons, shaft wiring and car station buttons is approximately 20% complete. The demolition of the elevator doors, November 16, 2010. The new elevator doors will be installed on November 17, 2010. complete. The old controller was replaced and will be wired on

Final inspections and punch list items are scheduled to be completed from December 6 through December 10, 2010.

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

Middle Beach Iglesias, E.

Improvements

Collins Park / Rotunda and ROW

(Parking Lot). Streetscape improvements on 21st and 22nd Streets. Restoration of the exterior of the historic Renovation and redesign of Collins Park; west of Collins Ave. (Bass Museum), east of Collins Ave. Rotunda. All to be done in coordination with the Cultural Campus Master Plan.

Construction Status

Street is currently under construction. The street will have a new median park was officially open to the public. Relocation of overhead utilities to was opened to the public. Collins Park, west of Collins Avenue between perimeter construction fence was taken down on the same day and the Remaining utility removal work will commence after Art Basel weekend Construction on Phase I of the project, all work east of Collins Avenue, 21st Street parking lot and all on-street parking east of Collins Avenue and the contractor fully mobilized on Phase II of the project. Site work, and be completed by Spring 2011. Park Ave from 22nd Street to 21st Certificate of Completion was received on October 23, 2009 and the 21st and 22nd Streets, was completely closed on February 15, 2010 nardscape, tree and plant installation, irrigation and electrical work is September 28, 2010. Final inspections are 100% complete and turncompleted. Restoration of the Rotunda and reflecting pool is also commenced May 4, 2009 and is substantially complete. A Partial over to Parks Department took place on October 29, 2010. The completed. Phase If construction was substantially complete on curb/gutter, and will also be milled and resurfaced. The work is underground work on 22nd Street has been completed by FPL. with added landscaping, new sidewalks on the west side, new scheduled for completion prior to Art Basel.

Monthly Construction Report Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

Fire Station 2 - Bldg. A

Middle Beach

Cabañas, H.

columns. The wood floor systems will be removed and structural deficiencies, such as cored structural beams renovated / remodeled in its entirety and be made fully throughout all the grade beams, reinforced beams and The existing wainscot high, wall tile, which is located in code. They will also match the existing historical look the old machine room will be restored as needed. The building will have a new roof installed and minimal site building will be reduced from 15,094 to 11,305 square repairs will be made on the interior of the building not new elements will mimic the historical connectors that renovated to meet ADA standards and an elevator in existed at one point in time. The building will also be replaced with structural concrete slabs. All existing mechanical, and plumbing systems will be installed. serve as the main administrative offices for the Fire feet. The current building additions which are not of will be corrected as part of the scope. The exterior restrooms and will also serve as exit points. These ADA accessible. This building has severe spalling building walls will remain untouched and structural structurally fastened to the existing beams to meet "connector" additions will be added. Said additions work as part of this scope. The entire building will historical significance will be demolished and new Administration Building A. - This building will be to disturb the exterior historical brick finish of the connecting hallway between the buildings, stairs, Department. The existing square footage of the of the existing windows. New lighting, electrical, will be a two-story element that will contain a building. New windows will be installed and the main building will be provided.

refurbishment will return the ability of fire companies to operations. The window openings and the glass block will remain untouched. The existing stand pipe system The building will be sealed, painted and re-roofed. The The hose tower will be refurbished in its entirety. The extensive spalling throughout the tower. The window is inoperable and will be replaced with a new system bulk of the work will address structural repairs to the openings were covered with non removable louver windows that preclude using the tower for ladder use it for high rise training.

Fire Station 2 Hose Tower

Middle Beach

Cabañas, H.

Refurbishment

Construction Status

on 4/26/2010. The demolition was restarted on 4/28/2010 and has been was hired to develop a shoring plan and that scope of work commenced Plans were submitted for Building Department review and approved for permitting. Demo permit approved 12/15/2009 BD100031 and interior demolition commenced on 12/20/2009, by H.A. Contracting and was stopped due to structural concerns on 2/15/2010. A shoring engineer completed.

#B1001433. NTP#1 was issued and corrections to the documents had Project has been awarded to Edgewater Construction. Building permit 10/28/2010 at the site. Mobilization started on 10/29/2010. Project is to be performed to the CPM, schedule of values and shop drawing resubmitted, reviewed and approved with comments. NTP #2 was issued on 10/25/2010. Pre construction meeting was held on submittals. This was due on 10/22/2010. Documents were progressing and demolition has begun.

Selective demolition By H.A. Contacting has occurred and test results integrated to main building renovation scope and is part of the overall have been given to the structural consultant. Recommendation for repairs have been made and hose tower scope of work has been main project renovation.

started on 10/29/2010. Project is progressing and demolition has begun 10/22/2010. Documents were resubmitted, reviewed and approved with construction meeting was held on 10/28/2010 at the site. Mobilization Project has been awarded to Edgewater Construction. Building permit documents had to be performed to the Construction Project Manager, #B1001433. Notice-to-Proceed #1 was issued and corrections to the schedule of values and shop drawing submittals. This was due on comments. Notice-to-Proceed #2 was issued on 10/25/2010. Pre

Status through November 18, 2010

Scope of Work

Fire Station 3 - Replace Exterior Windows to Impact

Hernandez, M.

Middle Beach

Project Name

Project Mgr.

District

Replacement of all glass windows and doors with new Dade County Product Approved impact resistant

systems.

Replacement of the built up roof for the entire building with a new roof system.

Fire Station 3 - Roof Replacement - Flashing

Hernandez, M.

Middle Beach

Construction Status

and final inspections passed on 8/23/10. Interior and exterior paint and patching complete and blinds are installed. Project is in final close-out Window and door replacement complete. Punch out work is complete

Initial roof work completed. However, roof curbs are being replaced and new flashing being installed around curbs under new proposal. JOC contracts for Phase II repair work are in process and work is scheduled to commence once rainy season passes.

Status through November 18, 2010

Scope of Work

Project Name
Indian Creek WaterWastewater

Project Mgr.

District

Rehabilitation 26th to 41st Streets

Middle Beach Carmenates, A.

The work consists of water main replacement, sanitary sewer replacement and asphalt re-surfacing along Indian Creek Drive from 26th to 41st Streets.

Construction Status

ssued on October 22, 2009 and the contractor mobilized after receiving and side street and DOH had approved mainline between 26th thru 30th he permit process in October 2009. The second Notice to Proceed was Street and side street between 26th and 30th Street. PWD is reviewing 40th. 35th Street is pending clearance of existing line and removal of a water main between 35th and 41st and side streets north of 35th Street 2009, and an inter-departmental coordination meeting between all City and 41st Street (sta 30+00 to sta 75+20) as well as all the side streets approval on the Maintenance of Traffic Plan and installed the advance the As-builts from 30th Street to 41st Street and all the remainder side Proceed #1 was issued by PWD on June 16, 2009. A pre-construction Water Main: 4,520 LF of water main has been installed between 26th streets. Contractor completed the comments on the red lines for the water line and remove red clouds, etc.). Public Works is waiting on a section and connection to new 12" water main. Road restoration and meeting with the residents and business owners was held on July 22, The contract with Horizon was executed on May 28, 2009. Notice to departments was held on October 15, 2009. The contractor finalized at 27th,28th,29th,30th,31st,32nd,33rd,34th,36th, 37th,38th,39th and the first lift of asphalt over the trench line are complete between 26th Pressure test and Bacteorological Test passed on all the water main (i.e, locations of ARV, offset at water line, show offset below new 12" traffic warning devices and safety barriers ahead of the work area. and 41st Street. Flushing was done between 26th and 40th Street. memo from CIP's inspector to forward the documents for DOH clearance.

installed on the mainline between 27th and 40th Street (sta 41+20 to sta FPL duct bank which on the plans was shown to be at a sufficient depth allow for the sanitary sewer installation. FPL indicated duct bank is too the FPL duct bank was shallower than as indicated on the plans and in conflict with the proposed sanitary sewer line. A meeting was held with high and would be required to be lowered. FPL will have to procure for relocated to the lower ducts and have the duct bank reduced in size to FPL can resolve the adjustment to the existing duct bank. The sanitary line video inspection is completed and the manhole exfiltration test will are complete between 28th and 41st Street. Sewer is on hold and the 71+40). Road restoration and the first lift of asphalt on the trench line a dive team and will require a permit from DERM to perform the work. conflict manhole to connect the old sanitary line with the new line until contractor demobilized the well point system due to a conflict with an to clear the proposed sanitary line. After excavation it was found that FPL on May 18, 2010 to review if cables on the upper ducts could be Sewer: Approximately 3,020 LF out of 3,100 LF of sewer has been FPL had questions on elevation which are being address by PWD. resolution. The EOR-PWD agree to have the contractor provide a Contractor will follow up progress and stay on top of FPL for be scheduled with PWD

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

Construction Status

Trench Drains at 27th , 28th, 29th, 30th , 31st, 32nd, 33rd,34th,35th, 36th, 38th,39th and 40th Street comers are completed.
Change Order #1-8 extended the contract completion by (68) days providing a revised final completion date of October 30, 2010. A settlement agreement was reached between the contractor and the City for the water main abandonement and the contractor has indicated that they will re-start the water service transfer the week of November 22, 2010. It is estimated the project will be finalized around May 20, 2011. The project is approximately 84% complete.

Status through November 18, 2010

Scope of Work

Construction Status

Miami Beach Golf Course - Cart Barn Middle Beach Rodriguez, R.

Project Name

Project Mgr.

District

New Golf Cart Storage Facility for the Miami Beach Golf Course.

substantial completion inspection, BEA Architect produced a master list Construction. On April 5, 2010, CIP transmitted the official punch-list to Alpine Construction. On April 7, 2010, Alpine Construction Architects, declared the facility substantially completed and issued the On March 24, 2010 a substantial completion inspection walk-thru was acknowledged receipt of the official punch-list. On April 12, 2010, BEA states that in accordance with Section 2.2 of the Contract, Contractor contractual requirements within 30 calendar days from April 12, 2010. Certificate of Substantial Completion", Form 00925. The certificate will complete or correct the work on the punch-list plus complete all and on March 29, 2010, it was transmitted to the City and Alpine conducted by BEA Architects and Parks Department. From this On May 10, 2010, the Building

transmitted a revised letter listing all pending items that were incomplete Official issued a temporary Certificate of Occupancy which excluded the scheduled to take place on May 12, 2010, but Alpine Construction failed caused by its failure to complete the project on time. On June 10, 2010, use of storage rooms 106 and 107. Final completion of the project was documents to BEA Architects. On September 8, 2010, BEA Architects responded to Alpine Construction with a letter listing all pending items Occupancy, Certificate number BCO10132.On July 2, 2010, Mr. Tim to complete all the contractual requirements. On May 18, 2010, CIP the building official approved the facility and issued the Certificate of completed review of the September 4, 2010 close-out submittal and hat were incomplete or missing from the close-out documents. On Office notified Alpine Construction of potential liquidated damages September 4, 2010, Alpine transmitted for a second time close-out documents to BEA Architects. On July 12, 2010, BEA Architects Jones of Alpine Construction delivered the outstanding close-out or missing from the close-out documents.

On September 30, 2010, BEA Architects completed the review of closeout documents. This was the third review of the close-out documents. Some items are still pending to complete package.

Management participated in a final punch-list inspection of the Cart Barn On September 17, 2010, BEA Architects and Green Space and all items were completed and approved by both parties.

parties came to a settlement. Alpine will provide all outstanding items by Once all documents are accepted by all department and agencies, then November 12, 2010 and the City will release 50% of the retainage. On November 10, 2010, a mediation meeting took place and both the City will pay the balance of the agreed amount.

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

Nautilus BP 7 ROW Improvements

Carmenates, A. Middle Beach

scope is Nautilus West (approx. 22,200 I.f.). Phase II scope is Orchard Park (approx. 12,700 I.f.). Integrated within the street ROW; and entryway features. Phase I with waterline replacements throughout the Phase II area, and with drainage improvements to Basins 92, provide pedestrian lighting; enhanced landscaping street lighting upgrades to correct deficiencies and resurfacing; swale restoration; repair of sidewalks; Area-wide street improvement including: street 97, 98, and 99 per Stormwater Master Plan.

Construction Status

The Nautilus Project is approximately 99% complete. The following tems remain outstanding:

- consisting of one pump per station on April 19, 2010 and completed the . During the installation of the pumps a problem was detected and the installation. The second batch of one pump per station was sent back inspection was held with PWD on August 3, 2010 and a punch list was inspected and re-certified by the manufacturer they will be shipped to contractor completed the installation on August 2, 2010. A preliminary to the manufacturer for re-certification on April 26, 2010. This second patch of pumps are anticipated to be back at the end of August 2010. The second batch of pumps were received on July 28, 2010 and the manufacturer's facilities for re-certification. Once the pumps are the site and re-installed. The contractor received the first batch pump manufacturer requested the pumps to be sent back to the submitted to the contractor.
- provided the as-built for the signing and pavement markings and a walk thru was held with PWD on 3-23-10. Punch list items were provided to 2. Punch list for the roadway and pavement markings. The contractor with PWD. PWD did not show to the walk thru. CIP confirmed all the inspection and review. A walk thru was schedule on October 6, 2010 the contractor. The contractor indicated these punch list items are completed and will be submitting documentation for City's final tems were completed and/or responded.
- contractor is working on modifying the initial installation and a final walk modifications on the additional planting design for 42nd Street. The 3. Additional scope by Parks Department. Parks requested thru will be scheduled.
- September 17, 2010 for review and final acceptance. PWD Engineering contractor on June 25, 2010. The contractor submitted on September certifications. The close out documentation was submitted to PWD on made comments on the pump stations system and are being address responded on October 29, 2010 with no comments. PWD operations watermain and landscape as well as one close out permit binder with 15, 2010 signed and sealed certifications of service points at pump South Florida Electric warranty letter, FDOT permits, South Florida stations, signing and pavement markings, hardscape and drainage, power and pumps warranty letter, The Garden R Us warranty letter, 4. As-Built and Certifications. A close out list was provided to the WMD permit, DERM permits, FDEP permits and drainage well by the contractor and pump manufacturer

Status through November 18, 2010 Scope of Work

Construction Status

Project Name Project Mgr.

District

Oceanfront BP 6 ROW - Phase 1b - 40th Street & Collins Ave. Middle Beach

Perez, M.

pedestrian amenities and restrooms at select locations enjoyment for beach access at street end. Scope may include: street resurfacing; curb and gutter restoration sidewalks to provide continuous pedestrian ways; street lighting upgrades to correct deficiencies; enhanced pedestrian access to the beach; and Improvements include pedestrian comfort and or upgrades; repair, extension, or widening of enhanced landscaping within the street ROW; at the beach ends. The Project includes a variety of streetscape upgrades sidewalks to provide continuous pedestrian walkways; such as street resurfacing; curb and gutter restoration and/or upgrades; repair, extension, or widening of enhanced landscaping within the street ROW; and enhanced pedestrian access to the Indian Creek street lighting upgrades to correct deficiencies;

Oceanfront BP 6 ROW Improvements -

Carmenates, A. Middle Beach

Construction work completed, and accepted by Parks and Recreation Department on 9/27/10

NTP no. 2. The Utility Permit was submitted to FDOT on November 13, for the water. The contractor completed the pavement marking and signage after the required 30 days of asphalt curing and a walk thru will certificate, project schedule and schedule of values prior to issuance of sidewalk and drainage and the contractor is working on punch list items evising the As-builts for water and electrical and anticipate re-submittal work at Indian Creek Drive from 42nd through 43rd Street in addition to Street on June 22,2010 and non-compliant work identified in punch list was held on August 6, 2010 between 31st and 40th Street and a punch ist was submitted to the contractor. PWD has accepted the pavement Design-Build Firm will seek all the required permits, provide insurance permit was submitted to FDOT on January 22, 2010 was approved on has been corrected. A subsequent walk thru was held on August 17, completion walk thru for 29th and 30th street. A water main walk thru Department of Health granted clearance for side street between 27th and 40th street water mains. The contractor completed the drainage 2009 was approved on January 22, 2010 and permit extension was granted by FDOT until August 15, 2010. The FDOT Lane Closure Avenue and on side streets from 27th through 40th street and the 2010 for 27th, 28th, 42nd and 43rd Street together with substantial implementation of the Maintenance of Traffic plan on February 22, 2010. The water main and tie-ins were completed across Collins Notice to Proceed No. 1 was issued on December 11, 2009. The the above ground improvements at all side streets. A substantial completion walk thru was performed on 27th, 28th, 42nd and 43rd be scheduled the week of November 15, 2010. The contractor is February 10, 2010. Contractor mobilized and commenced or final review the week of November 22, 2010.

ready for inspection. Acceptance inspection conducted on 8/9/2010 and project accepted by Property Management. Project closeout documents Stucco work completed, paint work completed, shutters installed and submitted and final release of retainage

Public Works Yard - Exterior Waterproofing Middle Beach

Reyes, M.

Project includes the complete repair of stucco cracks at exterior walls and the new installation of sealant at all exterior doors and windows.

		Monthly Construction Report	
District Decises Man	D	Status through November 18, 2010	•
rrojeci Mgr.	rroject Name	Scope of Work	Construction Status
Middle Beach Fung, H.	Public Works Yard - Roof Replacement	Complete roof replacement of three (3) roof sections of the complex. Existing roof has extensive damage and water infiltration. A new built-up roofing system will be installed.	Roofing and flashing installation is complete. Final roofing inspection approved on July 26, 2010. Roofing Manufacturer inspected the completed roof on July 26, 2010. Closeout submittal pending from National Roofing.
			10/11/10: Closeout documents submitted with final payment application. Project Complete.
Middle Beach Cabañas, H.	Scott Rakow Youth Center Ph. II	The renovation of the existing Scott Rakow Youth Center facility.	Contractor received construction Notice-to- Proceed #2 on August 24, 2009. Project is approximately 98% complete.
·			In order to better coordinate this project, the roof replacement which was under the Capital Renewal & Replacement program has been added and approved to the scope of work as a GMP adjustment and is now 99% complete. In addition, Parks and Recreation has requested the replacement of the bowling alley be added to the scope as a GMP adjustment and approval was granted by commission to be funded from FF&E and it is 100% complete. The original contract completion date was extended by 35 days, due to the change order for 28th Street. The overall project completion is approximately 98%. TCO is planned for 11/22/2010. CO by December 21, 2010.
Middle Beach	Seawall Restoration - Sunset Lake Park	Restoration of seawall, new sheet pile wall, new concrete cap, and restoration of landscaping.	Seawall, rip-rap boulders and sod replacement is complete.
rung, n			Closeout documents pending from Contractor.
North Beach	Bandshell Facility Improvements	Renovation/rehabilitation of the Bandshell facility and restrooms.	NTP 2 was issued on July 12, 2010.
- 5 5 5 6			Backstage addition reconstruction: Shell is complete. Stucco finish in progress.
			Outdoor seating area: Rough electrical and stucco finish in progress.

Floor and ceiling framing, electrical rough in progress.

The interior hollow metal and hollow wood core doors are aged, not fire rated, beyond rated life expectancy scratched, utilizing non compliant hardware and, in general, not working properly. The exterior overhead, vehicle bay and doors do not close properly.

Fire Station 3 - Overhead Door & Interior Doors Replacement

Hernandez, M. North Beach

Existing backstage area and restrooms building: Interior framing and rough electrical complete. Rough mechanical and

plumbing in progress.

Stage:

and motors arrived on 9/27/10. Four out of the six doors and motors have been installed and are fully functional. A rusted pipe column in the Permit Issued for overhead doors 9/8/10. A total of 6 overhead doors rear garage area must be replaced prior to final two garage door replacements. Engineering details for the column has been prepared and is being submitted for approval to Building Department.

Status through November 18, 2010 Scope of Work

Project Name

Project Mgr.

District

Normandy Isle Normandie Sud BP 4 ROW Improvements

Carmenates, A. North Beach

Improvements include enhanced storm water drainage resurfacing/pavement markings; pedestrian access landscaping; extension or widening of sidewalks to ways; incorporation of traffic calming features, consistent with the community preferences. collection and disposal, streetscape, and comply with ADA requirements; street

Construction Status

Completion on July 14, 2010 with a final completion date of July 1, 2010 documents, guarantee and bonds, evidence of payment and releases of electrical, landscape, above ground and drainage installations. Stripping reduced due to credits pending on activities removed from the scope of iens and Certificate of Insurance and the Engineer of Record provided for the labor and incidentals. A JOC contractor (GR Electric) submitted conduits, junction boxes, wiring, uplighting and seven out of twenty nine east will maintain the angle parking but the angle parking on Bay Drive water, above ground and landscape components of the project. FDOT of parking on Bay Drive pending reconciliation between HOA and MDC abor and materials. The breakdown on the cost provided by HCI was The contractor completed the neighborhood improvements except for West was rejected by MDC and PWD. The contractor's payment was ighting on Marseille Drive from Rue Notre Dame to Rue Verdon. HCI incidentals. The City thru its JOC contractor requested separate bids closure and utility permits are closed. PWD has accepted the water, the date of commencement of applicable warranties required by the ighting materials in the amount of \$73,378 and executed a separate requirements for approval of the proposed parking layout. Bay Drive a bid for \$165,831. The City requested the contractor to provide the November 22, 2010. The contractor provided cost proposals for the abandoning of the existing water lines and relocation of fire hydrants hat were not depicted in the plans and specifications. The residents change order with the JOC contractor (GR Electric) for the labor and replacements. Walkthroughs were held on the electrical, drainage, contractor indicated the final CAD files will be submitted the week of requested uplighting on Trouville Drive north of Normandy Drive and accepted the project via email on December 4, 2009 and both lane provided a cost proposal in the amount of \$407,046 which included savings of \$167,837. GR electric has completed the installation of ncidental costs to perform the installation which resulted in a net acceptance. The As-built submitted did not have the CAD files. work. The Engineer of Record provided the Certificate of Final Final Certificate of Payment. The close out documentation was contract documents). The contractor submitted project record \$73,378 for the materials and \$333,668 for the labor and other submitted to PWD on September 24, 2010 for review and final the stripping for parking on Bay Drive and miscellaneous tree oole bases.

		Monthly Construction Report	
District		Status through November 18, 2010	
Froject Mgr.	Project Name	Scope of Work	Construction Status
North Beach Carmenates, A.	Normandy Shores BP 3 ROW Improvements	Improvements include storm water drainage collection and disposal infrastructure, enhanced landscaping and lighting; repair, extension or widening of sidewalks to comply with ADA requirements; street resurfacing/pavement markings and improvement of dead end streets with street lighting, landscaping, and/or parking, where appropriate; bicycle paths and pedestrian access ways; incorporation of traffic calming features, consistent with the community preferences.	The contractor completed the improvements per plans and specifications on the Normandy Shore Neighborhood. Walk thrus were performed on the drainage, landscape and irrigation, above ground, signing and pavement markings. The electrical, signing and pavement markings. The electrical, signing and pavement marking components were accepted by the City. A walk thru was held on October 7, 2010 for the landscape and irrigation punch list items and three items remained. The contractor completed the three pending landscape items and was accepted by parks on November 12, 2010. The contractor is negotiating with the well company to redevelop the drainage structure well that did not meet specification requirements. The contractor indicated the as-built documents will be submitted by end of November 2010. The contractor submitted a first request for time extension for 112 days out of which the consultant approved 56 days. The contractor submitted three more requests for time extension totalling 540 days which the consultant recommended approval on an additional 146 days. The total time extension recommended by the consultant revised the final completion date from September 14, 2009 to April 4, 2010. The contractor submitted another time extension request for 75 days which is being evaluated by the consultant and a recommendation will be provided to the City. The Normandy Shores Project is approximately 99% complete.
North Beach Cabañas, H.	Normandy Shores Golf Course Facilities - Club House	Replica of the Normandy Shores Golf Course Club House	The NTP #2 was issued on August 7, 2009. Exterior floor tile and side walks installed. FPL provided permanent power on February 19th, 2010. Teco Gas installed final gas meter on February 26, 2010. Phase II of the project will commence the first week of April 2010. Phase I TCO was obtained on March 26, 2010. Phase II of the project commenced 4/13/2010. Parks and Recreation started using the entire facility on April 12, 2010. Phase II(parking lot) is 100% complete. ROW contractor vacated site 10/30/2009. Overall completion was 8/23/2010. Ribbon cutting ceremony was held on September 16, 2010 Project is now complete with minor pending punch list items. (Total of 3 items)
North Beach Perez, M.	North Shore - Water main lines crossing FDOT Right-Of-Way along	Place 8" DIP that encroach FDOT Right of Way along 71st St.	Contractor was given NTP 1 on September 3rd, 2010. As of October 25, 2010, the contractor has not been successful in obtaining a DERM Class V Dewatering Permit.

Of the six water main lines, two of them are located in contaminated areas (Abbott Ct. and Harding Ct.), which require a more extensive DERM's review prior to issuance of the permit. In order to start construction at least in the area that has no contamination problems, the contractor has asked for two separate DERM Dewatering Permits, one for the non contaminated areas, and another for the contaminated

Contractor is expected to receive the DERM dewatering permit for Bonita Drive, Carlyle Avenue and Collins Court by November 17, 2010.

Status through November 18, 2010

Scope of Work

The project includes the structural restoration of the spalled concrete in the stairways, painting and waterproof coatings to protect the concrete. It also requires water proofing in the stairways.

07th Street Parking Garage Structural Repairs FY2008/09

Project Name

Project Mgr.

District

South Beach

Fung, H.

Construction Status

8/4/10: The structural restoration at the SW stair tower is 80% complete. The painting of the garage ceilings is 95% complete. The waterproofing of the garage 2nd Floor is 10% complete.

10/6/10: The structural restoration and waterproofing at the SW stair tower is complete. Painting of the garage is complete. Re-coating of waterproofing at level 2 is complete and the parking spaces have been re-striped. Structural restoration at NW stair is complete and waterproofing is in progress.

10/15/10: Waterproofing complete at the NW Stairs. Repair of remainder of concrete spalls in progress.

Anticipated completion of construction by 10/22/10.

Project Scope complete. Contractor awaiting approval for change order to repair deficient stairwell doors and miscellaneous electrical conduit repair.

11/1/10:

Project complete pending punchlist items. Change Order BPO in progress.

11/15/10:

NTP II issued to Contractor for Change Orders. New hollow metal doors and frames to be ordered and installed.

eport
Re
Construction
Monthly

Status through November 18, 2010 Scope of Work

Construction Status

1701 Meridian 2nd Floor Tenant Improvement

Project Name

Project Mgr.

District

South Beach

Fung, H.

Demolition and new build out for Fire Prevention offices. Improvements include: new ADA bathrooms; new air handling unit & associated ductwork; new ceilings & floors; and new paint finishes.

Demolition commenced on June 6, 2010. Design of Tenant Improvement underway. Demolition complete and finalized. HVAC Design/Build NTP 2 issued to FXP on 8/2/10. New AC unit delivered on 8/3/10. Permit for GC (Matrix)

10/11/10: HVAC is complete. Construction is in progress and contractor anticipates completion of their contracted scope of work for 3rd week of October. Fire alarm contractor has submitted drawings to the Building pending final acceptance from Building Department. Department for permit.

10/27/10:

Fire Final pending inspection today. All other inspections are approved. TCO application will be submitted upon receipt of Fire Final.

10/28/10:

All partial finals approved. TCC application submitted to the Building Department. Electrical, Engineering and Planning pending TCC approval.

11/1/10:

TCC issued by Building Department. Punchlist item work in progress.

Project complete. This is the last report.

clay tile roof over the Community Center - Parks and

Recreation Office Building.

Replace damaged clay tile roof for a complete new

21st St. Community Center - Clay Tile

South Beach

Sinnes, A.

Roof Replacement

Renovation of building to accommodate the new SIU office relocation.

225 Washington Avenue, SIU Office Relocation

South Beach

Sinnes, A.

10/11/10: Building Permit approved. Construction to commence October 13, 2010.

10/27/10:

Walls are framed and MEP roughs are on-going. Rough inspections are being scheduled for the week of 11/1/10.

Drywall installed. Finishing in progress. Painting of walls and installation of ceiling grid scheduled to be complete by 11/30/10.

Status through November 18, 2010

Scope of Work

Construction Status

Project Name Project Mgr.

District

South Beach

Iglesias, E.

City Center BP 9A ROW Improvements

curb and gutter, landscape, irrigation, lighting, potable water, and storm drainage infrastructure. The project limits include the area bounded to the north by Dade throughout City Center, including roadway, sidewalk, Boulevard, to the south by Lincoln Road, to the west The City Center Right of Way (ROW) Infrastructure infrastructure project which includes the restoration by Washington Avenue and to the east by Collins and enhancement of right-of-ways/streetscapes Improvement Project BP9A is a \$12.6 million

Construction commenced on August 24, 2009. The following is the current status of all improvements

Art Basel weekend. Temporary lighting is in process. Final landscaping scheduled for week of Nov. 22, 2010 with completion scheduled prior to Washington Ave: Water main replacement, stormwater improvements, The first lift of roadway milling and resurfacing is 90% complete in both sidewalk replacement and pedestrian lighting installation are complete. directions and second lift of asphalt on the northbound lane is and irrigation is complete.

between Lincoln Road and 17th Street. Stormwater improvements have portion of the gas lines with completion by November 24, 2010. Sewer line replacement will commence between 17th and 18th Street on James Avenue - Water main replacement, stormwater improvements, sidewalk replacement and pedestrian lighting installation is complete. sidewalk replacement and pedestrian lighting installation is complete commenced from 18th to 19th Street and TECO Gas is relocating a 18th Street - Water main replacement, stormwater improvements, November 29, 2010.

21st Street - Park Ave. to Collins Ave. is complete. The contractor has commenced stormwater improvements and watermain with completion 9th Street - Installation of water main replacement and stormwater iberty Ave. - Drainage is complete between 19th and 20th Street. Drainage is underway between 20th and 21st Street. Watermain mobilized between Washington Ave. and Park Ave. and has replacement is underway between 19th and 20th Street. targeted by Art Basel weekend.

Drainage Wells - Installation is 85% complete throughout the project. Project substantial completion is currently projected for May, 2011. mprovements are complete.

		Monthly Construction Report	
District		Status through November 18, 2010	
Project Mgr.	Project Name	Scope of Work	Construction Status
South Beach Iglesias, E	City Center BP 9B ROW Improvements	The City Center Right of Way (ROW) BP9B Infrastructure Improvement Project is a \$9.8 million infrastructure project which includes the restoration and enhancement of right-of-ways/streetscapes throughout City Center, including roadway, sidewalk, curb and gutter, landscape, streetscape irrigation, lighting, potable water, and storm drainage infrastructure as needed.	One hundred percent (100%) Construction Documents were submitted by Chen on November 25, 2008. The DERM Class II Permit, FDOT Utility and Special Permits, DERM Wastewater Permit, and FDOH Water Main Extension, and FDEP Permits have already been approved. The extension of Lincoln Lane North to connect to Washington Avenue is complete and was opened to vehicular traffic on Aptil 6, 2010. The water main replacement on 17th Street from Washington Avenue to Pennsylvania Avenue has been completed and the area restored. Pennsylvania Avenue was completed and open to the public on October 30, 2010. Ongoing coordination is occurring with the New World Symphony Project which includes the construction of Lincoln Lane North from Pennsylvania Avenue to Washington Avenue and a portion of 17th Street. This phase of the work is scheduled to be completed by early January, 2011. Additional stormwater infrastructure improvements are being planned for Lincoln Road which shall be designed to handle a 5-year, 1-day storm event. An initial stormwater model shall be prepared which will determine the final design and the resulting scope will be added to the City Center overall scope of work.
South Beach Fung, H.	City Hall - Building Department Renovation Phase II	Renovation of the different sections of the Building Department, located in the 2nd floor of City Hall. New reviewer's stations, demo interior glass partitions, new ceilings, new floors, new partitions and upgrades.	10/11/10: Phase II consists of 3 areas. The first area is 80% complete waiting for desk partitions. 10/27/10: The funding allocation for the desk partition change order was received from the Building Department on 10/21/10. BPO increase is being processed. Project is on hold until BPO increase is approved.
			11/15/10: The desk partition change order has not been approved to date. The reviewers stations are on hold until CO is approved. The violations office build-out is to commence on 11/22/10.
South Beach Fung, H.	City Hall - Upgrade Halon System	Replacement of two 45 pounds halon 1301 tanks by two new environmentally acceptable protection system (HFC-125).	7/2/10: All suppression systems have been installed. The fifth floor is pending replacement of the AC unit and sealing the room for pressurization. 10/6/10: Permitting of the new AC unit for the 5th floor is underway.

inding allocation for the desk partition change order was received he Building Department on 10/21/10. BPO increase is being ssed. Project is on hold until BPO increase is approved. 11/16/10: Permit received for the AC unit at the 5th floor. Completion All suppression systems have been installed. The fifth floor is g replacement of the AC unit and sealing the room for ssk partition change order has not been approved to date. The 0: Permitting of the new AC unit for the 5th floor is underway. plations office build-out is to commence on 11/22/10. ers stations are on hold until CO is approved of this project anticipated for 12/3/10. rization.

District		Monthly Construction Report Status through November 18, 2010	
Project Mgr.	Project Name	Scope of Work	Construction Status
South Beach Fossler, C.	Convention Center Improvements - Phases C & D	Renovation and ADA improvements to 29 existing restrooms, doors and door hardware. (Includes budget for Phases A,B,C, and D).	The Restroom project is currently at 95% completion, pending resolution of issue with the Fire Inspector on the obstructed coverage of sprinkler heads, due to water closet stall partition height. The door replacement project is at 80% complete. There are 99 doors remaining to be installed. The City has reduced the current contractor's scope of work, and hired a new JOC contractor to complete the doors. A new permit for the remaining doors will be processed.
South Beach Hernandez, M.	Fire Station 1 - Replace Exterior Windows to Impact Resistant	Replacement of all glass windows and doors with new Dade County Product Approved impact resistant systems.	A preconstruction meeting with the Fire Department and Property Management took place on 6/30/2010. First floor windows replaced and inspections passed. 2nd floor was completed on 10/4/10. Final building department sign off and inspections are in process.
South Beach Vieira, T.	Flamingo Lummus BP 10F ROW Improvements	A portion of Flamingo A, between 7th, Meridian, 9th, and Washington will be constructed via JOC as Flamingo F. It is intended that this construction will relieve stormwater bottlenecks from Washington Avenue while making water, streetscaping, and lighting improvements to this area.	Water main: Complete Drainage: 7th Street: In progress.
South Beach Fossler, C.	Little Acorn Theater / Limited Improvements	Upgrades to the theater to allow SoBe Music, (lessor) under a lease with the City, the use of the facility to further expand the educational programs they now offer at the Carl Fisher Clubhouse building. These improvements will allow the facility to serve as a performance venue, as well as instructional space for programs in theater, sound, lighting, and stage set design.	Work related to the maintenance improvements to the Little Stage Theater have been completed by Property Management. The construction of the "tech booth" has been completed. All other purchases of theater, sound equipment, theater chairs, and dance flooring have been completed, and have been delivered to the site. CIP staff inspected the site on November 30, 2009, and verified the delivery of City purchased goods and services. CIP has requested copies of all delivery receipts obtained by SoBe Music to verify vendor compliance with terms. CIP has not received the copies of all material receipts. A request will be made again to SoBe by February 6,2010. All additional scope of work has been completed and the facility is in use by SoBe Music.
South Beach Sanchez, O.	Lummus Park - Temperature and Date Monument	Restoration of the Temperature and Date Monument, located at Lummus Park, next to the 10th Street Auditorium.	Contractor mobilized on October 11th, 2010. Reconstruction of knee wall is complete. Tile removal and concrete repairs complete. New tile installation underway.

Report
Construction
Monthly

Status through November 18, 2010

Scope of Work

Avenue. The following Departments will relocate to this building: Parking, Finance, IT, OBPI conference room and Cultural and Tourism Department

Facility - 5. Office Build-out Package Multi-Purpose Municipal Parking

Project Name

Project Mgr.

District

South Beach

Fung, H.

A component of the City Hall Garage is to construct a 5-story office building (32,000 SF) along Meridian

Project has received a TCO.

Construction Status

installation complete. Roller shade installation 95% complete pending HVAC final Test and Balance report completed and sent to the Architect. Pending final approval by MEP Engineer. Office furniture ounchlist items.

10/11/10:

Harbour Construction. Permitting for this work is underway and JOC Roller Shades are installed. All furniture is installed. Miscellaneous additional tenant requests are being performed under a JOC with Contract is being processed.

0/27/10:

Dept. Link's CO is pending low voltage final inspection from Gisnet and Fire Final. Fire requires additional stair signage for final sign off. These Permits for Breakroom and Misc. Items are still in review at Building signs are being supplied by the JOC Contractor.

11/15/10:

Permits for Breakroom and Misc. Items are still in review at Building Dept. (2nd round of comments) All items are completed for CO. Fire to reinspect on 11/18/10.

structural steel damage on October 20, 2009 and has requested that the for the additional structural engineering services was completed on 2/9/10 and Notice to Proceed to the Engineer was provided to complete structural engineer be retained to evaluate. The Purchase Order to pay Sculpture relocated to a storage location where it will be restored and remain in storage for a period of one year. Conservator has noted

Engineer has approved the final shop drawings for the renovation. The Conservator, Engineer and the Scott Rakow Youth Center contractor will insure that the slab that will support the sculpture is appropriate for the sculpture.

Sculpture is scheduled to be placed back at site in October 2010

Perry Sculpture Restoration

Restoration of sculpture located at Scott Rakow Youth

South Beach Cabañas, H.

×	
8	
8.	
ž.	
8	
٥.	
ş.	•
r	~~
8.	~
	•
	<u>-</u>
2	_
٤	
ê	_
۶	•
٤	~
8	11.4
ŝ.	٠.
8	~
	•
è	\sim
ŝ.	
٠	٠.
٤.	_
	ъ
:	
	_
	_
	_
	_
	•
	\sim
	2.4
	`
	^ i
	, 4
	\sim
	11/22/2010 4:28:39 PM
	`
	-
	_
	_
	-

Monthly Construction Report Status through November 18, 2010

Scope of Work

Replacement of the existing glass block staircase at the Police Building Garage with Dade County approved

Police Garage Glass Blocks

replacement

Fung, H.

Project Name

Project Mgr. South Beach

District

impact glass system.

Construction Status

Contractor has obtained permit and is waiting for delivery of windows. Window delivery scheduled for the week of 10/25/10. Installation to commence by 11/1/10. Completion of Project by 12/1/10.

10/27/10:

Contractor commenced work on 10/25.

10/28/10:

Contractor installations approximately 50% complete.

11/15/10:

Contractor installations approximately 80% complete. Anticipated completion by 11/30/10.

Fourth floor: complete Third floor: complete

Acoustical ceiling system replacement in hallways first floor through 4th floor.

Second floor: in progress

Seawall construction complete. Outfall structures and rip-rap boulders nstalled.

Drainage inlets and pollution control structures delivered. Installation underway.

Drainage Improvements added at cul-de-sac due to

existing ponding conditions.

paved area, irrigation and exterior lighting.

adjacent Public Park and cul-de-sac located at the west end of Lincoln Road. New landscaping, new Restoration of the seawall, improvement to the

Seawall Improvements - Lincoln Road Street End

South Beach

Fung, H.

Police Station - Ceiling Replacement

South Beach

Sanchez, O.

Underground work is 90% complete. Sidewalks and curb and gutters were poured on 10/7/2010 and 10/8/2010.

Expected completion by mid November.

10/27/2010:

Final tie in of 36" stormwater pipe to outfall structure pending the receipt of an internal compression fitting. When Envirowaste receives, progress at the streetend park will recommence.

11/15/2010:

light bollards, landscaping, irrigation, pavers, benches and street lighting installations anticipated to be complete by 12/3/10. Final installations of the park amenities have commenced. Bollards,

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

South Pointe Park

South Beach Fossler, C.

area, new restroom facility, pedestrian walkways, playground, landscaping, irrigation, and site lighting. redesigned park entrance, new pavilion and maintenance buildings including a small concession Park Improvements consisting of the following:

Construction Status

Pylon lights continue to fail due to the copper conductor control cabling. We have received a quote to replace this wiring with fiberoptic cables. The contractor is providing additional back-up for his proposal so the City can proceed with his work.

P.O. is being cut for the necessary a/c modifications in the pavillion.

Check valve is being installed on the Washington Avenue fountain overflow drain. MCM is completing their punch list. They are finishing the last item this week.

Pricing has been approved for new beach shower pad. Work to begin after c/o is processed.

The City is requesting an additional TCO extension from the Building

Department.

Met with Delta Fountains to get recommendations for repairs to interactive water feature.

Pricing repairs necessary to correct slope on water feature.

Check valve installation complete.

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

South Beach

Dixon, C.

South Pointe Streetscape Phase II BP 12C ROW Improvements

The Project area encompasses the entire Public Right-Michigan Avenue, including Michigan Court and Lenox flow, new stormwater infrastructure to meet the Master water lines to enhance the water pressure and water access, landscaping, irrication, lighting, and parking Plan recommended level of service throughout the project area; Streetscape Improvements including improvements include the replacement of existing (excluding Third Street) west of Euclid Avenue to of-Way between Fifth Street and Second Street. Avenue between Fourth and Fifth Streets. The raffic calming measures, enhanced pedestrian mprovements

Construction Status

Horizon Contractors (HCI) has completed the following:

STORMWATER:

Class II permit and the request was approved. TTidal control valves are The installation of approximately 6,160 linear feet of stormwater piping, 30 structures, 21 gravity wells is complete, including certification from the testing of the system currently 98% complete. Repair method has been accepted for HCl to initiate repair of aproximately seven sections Stormwater system, with the exception of the contaminated areas. On scheduled for delivery in late November and will be installed following 07/15/10 CIP requested that DERM include this area in the existing dewatering permit for the cleaning and testing of the South Pointe FDEP dated April 22, 2010. On July 16, 2010, DERM issued a of stormwater piping.

WATER MAINS:

services has been obtained. Change Order has been executed for Labor scope of work (approx 1050 linear feet) on 4th Street between Jefferson water services and fire lines have been completed, including the added The installation of approximately 5,610 linear feet of water mains, 151 Ct and Washington Avenue. HRS authorization to connect the new and Materials and Equipment on the 4th Street water main, and the water main services connections are complete. Water main record drawings/as-builts are being finalized by the contractor.

ELECTRICAL/IRRIGATION AND LANDSCAPING:

inspection results/punch list of items which were completed by HCI. As-Engineer of Record (EOR) and CIP. On 07/15/10, the EOR issued their Inspections of the streetlighting system were conducted with PWD, HCI builts/record drawings are being prepared HCI for Final Certification by the EOR and turnover of the system to the City.

through/inspection was held on September 2, 2010, and Greenspace Managent has issues a report to be evaluated along with the Landscape landscape architect was conducted on 06/17/10. A secong walk The irrigation system preliminary walk through with Parks and Architects Report. ADA and Landscape inspections were conducted on 07/19/10. A Report was generated on 07/22/10. Additional irrigation lines installation is 85% complete.

The Addapave installation on 4th Street is complete, and will commence on 2nd Street in four to six weeks, following the reconstruction of 2nd Street.

DEMOLITION/RECONSTRUCTION:

Streets and Avenues are complete. Reconstruction of the alleyway is The sidewalks, curb and gutter, and roadway (1st lift of asphalt) on

Status through November 18, 2010 Scope of Work

Project Name

Project Mgr.

District

Construction Status

along Michigan, Meridian, Jefferson and Euclid Courts between 3rd and 85% complete. Valley Gutters and 2nd lift of asphalt has been placed 5th Street. The remaining alleyways between 2nd and 3rd are scheduled to be completed by mid November, 2010.

Placement of the 2nd lift of asphalt throughout the Project area is pending the repairs to the stormwater system.

Signage installation is complete.

116 calendar days have been added to the Contract Time and Substantial Completion is scheduled for March 10, 2011.

Will meet with Sonny Moore from the Fire Department by July 2, 2010 to (under separate permit) that are now creating a confusion in the final / finalize scope of work required to address life safety items remaining. determine how to address subsequent changes made by Live Nation Re: Interiors Project, Contractor is coordinating final inspections and permit is closed-out. A meeting was held with the Building Dept., to close-out process. Met with Miami Skyline to resolve remaining work. remaining on life safety issues will be done on a new capital project Re: ADA Project, Contractor has completed final inspections and No Additional work is going to be done on this contract. All work Master Permit is finalized.

agreement with the City. The City has requested back-up documents for Work has been completed by Live Nation, per the terms of their ittled TOPA Life Safety. This is the last report.

submitted request for additional information to Live Nation for supporting completed the review of the documents submitted on April 28,2010. CIP costs incurred by Live Nation in order to provide reimbursement. Backup documents were finally received on November 9, 2009. CIP documentation. To date, no response received.

TOPA Phase I South Beach Fossler, C.

compliant doors & hardware, exterior ADA ramp, and main lobby galleries and entranceways, extension of include renovations to restrooms, dressing rooms, balcony, fire sprinkler system, installation of ADA Box Office renovations to meet ADA requirement. ADA and Interior Improvements; Improvements

South Beach

TOPA Phase III

South mezzanine level bar

Status through November 18, 2010

Scope of Work

Project Name

Project Mgr.

District

Rodriguez, R. South Beach

Venetian Islands BP-13C1 - Venetian Causeway Cross Street Water Main

Causeway Cross Streets, at San Marino, Di Lido, and Rivo Alto Islands, prior to Miami-Dade County This project is part of BP-13C ROW Improvements and targets water main replacements at Venetian Causeway construction activity.

Construction Status

connections to existing 16" water mains. All 8" water main installation at the south side of East and West Rivo Alto Drive was completed and the On August 20, 2010, Ric-Man International (RMI) began the notification installation of the 8" water mains that cross the Venetian Causeway are completed. RMI is scheduled to complete the balance of the 8" water main installation on the north side of East and West Rivo Alto Drive to residents that work was beginning on the Venetian Causeway to upgrade existing water mains. On August 30, 2010, RMI began to 2010. By September 17, 2010, RMI had completed the four tapping mobilize to Rivo Alto Island and started on Rivo Alto on August 31, during the week of September 20 through 24.

2010, RMI completed the proposed tapping connections to the existing On September 27, 2010, work began at Dilido Island. On October 4, intersections of and East Di Lido Drive and West Di Lido Drive and 20" cast iron water main. On October 5, 2010, RMI began the installation of the proposed 8" DIP water mains located at the Venetian Causeway (Venetian Di Lido Way)

Rivo Alto Island. On October 11, 2010, samples of the water were taken On October 6, 2010, RMI began to chlorinate the new water mains at for bacteriological testing. Results will be transmitted within a week.

On October 26, 2010, pressure test were conducted at DiLido Island and approved. RMI is scheduled to start at San Marino Island on November 1, 2010.

Point STA 1+19 W, (Approx. 565 L.F.) was completed on November 12, 2010. RMI is working on the lateral connections on the south side of the The water main that runs from Station Point STA 4+20 E to Station Causeway on west and east San Marino Drive.

10/11/10:

Reconstruction of 315 Lf of seawall using vinyl sheet pilling with a reinforced concrete cap

Washington Court Seawall Renovation

South Beach

Sinnes, A.

Estimated completion of Project: January 10, 2011. Sheet piling installation is 60% complete.

10/27/10:

Sheet pile installation complete. Contractor commenced with excavation and formwork of the seawall cap.

The first 100 I.f. of seawall cap was poured on 11/9/10. The second section is being formed. Anticipated second pour date by 11/23.

REPORT OF THE ITEMIZED REVENUES AND EXPENDITURES OF THE

MIAMI BEACH REDEVELOPMENT AGENCY'S CITY CENTER DISTRICT

&

SOUTH POINTE
(PRE-TERMINATION CARRY FORWARD BALANCES)

FOR THE MONTH OF OCTOBER 2010

Agenda Item <u>LTC</u>
Date <u>12-08-10</u>



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

REDEVELOPMENT AGENCY MEMORANUM

TO:

Chairperson and Members of the

Miami Beach Redevelopment Agency

FROM:

Jorge M. Gonzalez, Executive Director(

DATE:

December 8, 2010

SUBJECT: Report of the Itemized Revenues and Expenditures of the Miami Beach Redevelopment Agency's City Center District and the South Pointe (Pre-Termination Carry Forward Balances) for the Month Ended October 31, 2010.

On July 15, 1998 the Chairman and Members of the Board of the Miami Beach Redevelopment Agency resolved that an itemized report of the revenues and expenditures of the Miami Beach Redevelopment Agency, with respect to each redevelopment area. would be made available to the Chairman and Members of the Board of the Miami Beach Redevelopment Agency at the end of each month. Further, it was resolved that such report would be made available no later than five days prior to the second regularly scheduled Redevelopment Agency meeting in the month immediately following the month for which such report is prepared and that the report would be placed on the Redevelopment Agency Agenda for the second meeting of each month as a discussion item. Because the distribution date for the second Commission meeting of some months falls prior to our receipt of bank statements for the month, we advised on October 21, 1998, that beginning with the report for the month ending October 31, 1998 all monthly Redevelopment Agency reports would henceforth be included as part of the agenda for the first Commission meeting of each month.

As of September 30, 2005, the South Pointe Redevelopment District ceased to be a redevelopment area within the Miami Beach Redevelopment Agency's jurisdiction. At that point, the City of Miami Beach assumed the responsibilities for the South Pointe Area. This report will continue to summarize the capital expenditures incurred for the South Pointe construction projects that have been appropriated as of September 30, 2005 and that are being paid from the remaining RDA South Pointe TIF balance.

The attached material includes the following:

Section A – South Pointe (Pre-Termination Carry Forward Balances)

- Summary of Cash Basis Transactions by Project and by Expenditure Type for the Fiscal Years Ended September 30, 1988 through 2010 and the Month Ended October 31, 2010
- Check and Wire Transfer Register Sorted by Project and Type of Expenditure for the Month Ended October 31, 2010
- Narrative of Major Projects Planned and/or Underway

Section B – City Center District

- Summary of Cash Basis Transactions by Project and by Expenditure Type for the Fiscal Years Ended September 30, 1988 through 2010 and the Month Ended October 31, 2010
- Check and Wire Transfer Register Sorted by Project and Type of Expenditure for the Month Ended October 31, 2010
- Narrative of Major Projects Planned and/or Underway

JMG:PDW:ky

SOUTH POINTE

(PRE-TERMINATION CARRY FORWARD BALANCES)

FINANCIAL INFORMATION

FOR THE MONTH ENDED

OCTOBER 31, 2010



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

REDEVELOPMENT AGENCY MEMORANUM

TO:

Jorge M. Gonzalez, City Manager

FROM:

Patricia D. Walker, Chief Financial Officer

DATE:

December 8, 2010

SUBJECT: South Pointe Financial Information for the Month Ended October 31, 2010

At the July 15, 1998 Commission/Redevelopment Agency meeting a request was made for monthly financial information for the South Pointe Redevelopment District. As of September 30, 2005, the South Pointe Redevelopment District ceased to be a redevelopment area within the Miami Beach Redevelopment Agency's jurisdiction. However, this report will continue to summarize the capital expenditures incurred for the South Pointe construction projects that have been appropriated as of September 30, 2005 and that are being paid from the remaining RDA South Pointe TIF balance (pre-termination carry forward balances). The information has been compiled and is attached.

Historical Cash Basis Financial Information

The summary report included in the attached material reflects that during the period from October 1, 1987 through October 31, 2010 approximately \$119,928,000 of revenues were received in the South Pointe Area.

The primary sources of these revenues included approximately:

- 94,048,000 Incremental Ad Valorem tax;
- 6,860,000 Bond proceeds;
- 5,188,000 Land sale:
- 8,122,000 Interest income:
- 3,170,000 Rental income:
- 1,000,000 Loan from the City of Miami Beach;
- 350,000 State Grant; and
- 1,190,000 From various sources.

The opening cash balance for October 1, 1987 was approximately \$1,042,000; therefore, the total amount of funds available for the period was \$120,970,000.

On the expenditure side, approximately \$109,955,000 has been expended from October 1, 1987 through October 31, 2010.

These approximate expenditures were primarily made in the following areas:

- \$ 16,385,000 Cobb/Courts Project;
- \$ 14,028,000 Debt Service Payments;
- \$ 12,330,000 Portofino Project;
- \$ 35,944,000 South Pointe Streetscape/Park;
- \$ 7,331,000 Administrative Costs;
- \$ 6,447,000 SSDI Project;
- \$ 5,913,000 Marina Project;
- \$ 2,466,000 Community Policing;
- \$ 1,542,000 Washington Avenue;
- \$ 1,045,000 Carner-Mason Settlement and Other Reimbursements; and
- \$ 1,500,000 Miami Beach Community Development Corporation Funding
 Agreement 530 Meridian Building Affordable Housing
- \$ 5,024,000 Other Project Costs.

The cash balance as of October 31, 2010 is approximately \$11,015,000. This balance consisted of the following amounts:

\$ 11,015,000 - Cash and Investment balance.

JMG:PDW:ky /ug

SUMMARY OF

CASH BASIS TRANSACTIONS

FOR THE MONTH ENDED

OCTOBER 31, 2010

RDA - South Pointe Pre-Termination Balances Summary of Cash Basis Transactions by Project Fiscal Years 1988 - 2011

	•		outh Pointe ermination		
	RDA-South Pointe	Balances	Carry Forward		Total
	Prior Years		FY 2011	<u> </u>	ev./Expend.
OPENING CASH/INVSTMT BALANCE \$	1,041,730	\$	11,016,561		
REVENUE					
- Tax increment - City	55,162,212		_	\$	55,162,212
- Tax increment - County	37,562,671				37,562,671
- Tax increment (Interest) - County	26,627		_		26,627
- Tax increment - Children's Trust	1,296,759		<u> </u>		1,296,759
- Bond proceeds	6,860,000		<u> </u>		6,860,000
- Cobb Partners - Closing Parcel 1, 2	5,187,944		_		5,187,944
- Marina rental income	3,169,547		<u> </u> :		3,169,547
- Interest income	8,122,695		(248)		8,122,447
- Loan from City	1,000,000				1,000,000
- Grants (Fla. Inland Navig.; shoreline restore.)	350,000		_		350,000
- Other Grants	5,000				5,000
- St. sales tax (receipt - income for pmt. to St)	209,358		_		209,358
- Daughters of Israel contribreloc. Mikvah	28,000				28,000
- Consulting fee refund-Rahn S. Beach	27,026				27,026
- Olympus Hldgreimb. Portofino advertsg.	24,405				24,405
- Mendelson environ. reimb./refund	10,000				10,000
- Regosa Engineering refund - Marina	8,500		-		8,500
 Portofino DRI Payment from Greenberg T. 	121,531		1		121,531
- Payment received from Greenberg T. for CMB	23,500				23,500
- Payment received from Olympus Holdings, Inc	96,276			٠.	96,276
 Payment received from Marquesa, Inc. 	2,000				2,000
- Contribution from Continuum II for S. Pointe P	ark 200,000				200,000
 Cost of asbestos remediation reimbCobb 	5,800		-		5,800
- Miscellaneous income	8,267		-		8,267
- Galbut & Galbut contribreloc. Mikvah	3,500		1		3,500
- Murano Two, Ltd-Cash Bond per Agreement	242,000		1		242,000
- Other (void ck; IRS refund; Am. Bonding)	175,227	<u> </u>			175,227
Total Revenues	119,928,845		(248)	\$	119,928,597

RDA - South Pointe Pre-Termination Balances Summary of Cash Basis Transactions by Project Fiscal Years 1988 - 2011

		RDA-South Pointe Pre-Termination	
	RDA-South Pointe	Balances Carry Forward	Total
	Prior Years	FY 2011	Rev./Expend.
EXPENDITURES			
<u>PROJECTS</u>			i
Cobb/Courts	(16,384,670)		(16,384,670)
Marina	(5,913,256)		(5,913,256)
Portofino	(12,330,291)		(12,330,291)
South Pointe Streetscape	(35,942,974)	(1,548)	(35,944,522)
SSDI	(6,446,941)		(6,446,941)
Fifth St. Beautification	(300,000)		(300,000)
Beach Colony (l'scape/stscape/site imprvmt)	(80,912)	1	(80,912)
Marriott	(53,061)	Tamana a	(53,061)
Washington Ave.	(1,541,983)		(1,541,983)
Washington Ave Surface Lot	(280,790.00)		(280,790)
Design guidelines	(43,708)	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	(43,708)
MBTMA/Mobility	(32,225)		(32,225)
S. Pointe Zoning	(20,819)	-	(20,819)
Alaska Baywalk	(218,323)	<u> </u>	(218,323)
Victory/Community Gardens	(174,477)		(174,477)
Washington Park	(50,590)	,	(50,590)
Water/Sewer Pump Station Upgrade	(1,012,781)		(1,012,781)
Flamingo S. Bid A R.O.W.	(394,548)		(394,548)
Flamingo Neigh-Lummus	(428,246)		(428,246)
Potamkin Project	(318,525)		(318,525)
Lummus Park	(103,916)		(103,916)
Wayfinding Project	(176,481)	<u> </u>	(176,481)
Jewish Museum of Florida	(500,000)		(500,000)
MBCDC Loan - 530 Meridian Bldg.	(1,500,000)		(1,500,000)
6th & Lenox Infrastructure Project	(770,438)		(770,438)
Beachwalk II Project	(4,026)		(4,026)
Miscellaneous	(60,132)	1	(60,132)
Total Projects	(85,084,113)	(1,548)	(85,085,661)
-	(35,55 ., 110)	(1,040)	(00,000,001)
<u>ADMINISTRATIVE</u>	(7,331,245)		(7,331,245)
en e			,,==,==,
DEBT SERVICE/LOAN REPAYMENT	(14,028,441)		(14,028,441)

RDA - South Pointe Pre-Termination Balances Summary of Cash Basis Transactions by Project Fiscal Years 1988 - 2011

	RDA-South Pointe Prior Years	RDA-South Pointe Pre-Termination Balances Carry Forward FY 2011	Total Rev./Expend.
<u>MISCELLANEOUS</u>			
Carner Mason settlement	(946,163)		(946,163)
City of Miami Beach (reimburse water main)	(74,067)		(74,067)
Miscellaneous	(24,503)		(24,503)
	(1,044,733)		(1,044,733)
COMMUNITY POLICING	(2,465,482)		(2,465,482)
TOTAL EXPENDITURES	(109,954,014)	(1,548)	\$ (109,955,562)
ENDING CASH/INVSTMT. BALANCE	11,016,561	\$ 11,014,765	

RDA - South Pointe Pre-Termination Balances Summary of Cash Basis Transactions by Expenditure Type Fiscal Years 1988 - 2011

		South Pointe	Pı	e-Terr ces Ca	th Pointe nination nrry Forward 2011	Re	Total ev./Expend.
OPENING CASH/INVSTMT BALANCE	\$	1,041,730	\$		11,016,561	,	· · · · · · · · · · · · · · · · · · ·
REVENUE							
- Tax increment - City		55,162,212			_	\$	55,162,212
- Tax increment - County		37,562,671			_	•	37,562,671
- Tax increment (Interest) - County		26,627			_		26,627
- Tax increment - Children's Trust		1,296,759			_		1,296,759
- Bond proceeds		6,860,000		•	_		6,860,000
- Cobb Partners - Closing Parcel 1, 2		5,187,944			_		5,187,944
- Marina rental income		3,169,547			-		3,169,547
- Interest income		8,122,695			(248)		8,122,447
- Loan from City		1,000,000			-		1,000,000
- Grants (Fla. Inland Navig.; shoreline restore	e.)	350,000			-		350,000
- Other Grants		5,000					5,000
- St. sales tax (receipt - income for pmt. to S	t)	209,358			-		209,358
- Daughters of Israel contribreloc. Mikvah		28,000			-		28,000
- Consulting fee refund-Rahn S. Beach		27,026		+ :	-		27,026
- Olympus Hldgreimb. Portofino advertsg.		24,405					24,405
- Mendelson environ. reimb./refund		10,000			-		10,000
- Regosa Engineering refund - Marina	÷.	8,500			_		8,500
- Portofino DRI Payment from Greenberg T.		121,531			-		121,531
- Payment received from Greenberg T. for C	МВ	23,500					23,500
- Payment received from Olympus Holdings,	Inc.	96,276					96,276
- Payment received from Marquesa, Inc.		2,000			-		2,000
- Contribution from Continuum II for S. Pointe	e Park	200,000			-		200,000
- Cost of asbestos remediation reimbCobb		5,800			-		5,800
- Miscellaneous income	٠	8,267			-		8,267
- Galbut & Galbut contribreloc. Mikvah		3,500			-		3,500
- Murano Two, Ltd-Cash Bond per Agreemer	nt	242,000			-		242,000
- Other (void ck; IRS refund; Am. Bonding)		175,227					175,227
Total Revenues	/	119,928,845			(248)	\$	119,928,597

RDA - South Pointe Pre-Termination Balances Summary of Cash Basis Transactions by Expenditure Type Fiscal Years 1988 - 2011

	RDA-South Pointe Prior Years	RDA-South Pointe Pre-Termination Balances Carry Forward FY 2011		Total v./Expend.
nditures				
nd acquisition	(9,444,065)			(9,444,065)
gal fees/costs	(9,392,304)	-		(9,392,304)
ofessional services	(17,519,445)	(1,548)	٠	(17,520,993)
nstruction	(30,254,739)	(1,0,0)		(30,254,739)
lities relocation	(1,873,213)	:		(1,873,213)
vironmental	(397,344)			(397,344)
bmerged land lease	(2,017,803)	-		(2,017,803)
ase agreements	(6,863,371)	-		(6,863,371)
scellaneous	(3,500,194)	· ·		(3,500,194)
operty Taxes	(389,260)	_		(389,260)
mmon Area Maintenance	(131,140)	_		(131,140)
ministration	(7,331,245)	_		(7,331,245)
bt Service/loan repayment	(14,028,441)	_		(14,028,441)
fund of Cash Bond	(242,000)	-		(242,000)
scellaneous Project Costs	(2,103,968)	_		(2,103,968)
ant	(500,000)	_		(500,000)
BCDC Loan - 530 Meridian Bldg.	(1,500,000)	_		(1,500,000)
mmunity Policing	(2,465,482)	-		(2,465,482)
	(109,954,014)	(1,548)	\$	(109,955,562)
NG CASH/INVSTMT. BALANCE	\$ 11,016,561	\$ 11,014,765	. <u>*</u>	<u>.109,9</u>

CHECK & WIRE TRANSFER REGISTER

SORTED BY

PROJECT & TYPE OF EXPENDITURE

FOR THE MONTH ENDED OCTOBER 31, 2010

RDA - South Pointe Pre-Termination Check & Wire Transfer Register by Project & Type of Expense Fiscal Year 2011

Check#	Date	Payee	Amount	Type of Expense	Project or N/A
244	10/28/10	Chen and Associates	1,547.98 1,547.98	Professional Services Ph.4 & 5	S. Pointe Streetscape
		TOTAL S. POINTE STREETSCAPE	1,547.98		
		REPORT TOTAL	\$ 1,547.98		

ATTACHMENT "A"

SUMMARY OF MAJOR PROJECTS

SOUTH POINTE PROJECTS (Planned and/or Underway)

South Pointe

South Pointe Streetscape Improvements Phase II

This project includes the replacement of existing water lines to enhance the water pressure and water flow, new stormwater infrastructure to meet the Master Plan recommended level of service throughout the project area as well as streetscape improvements including traffic calming measures and enhanced pedestrian access. The project area encompasses the entire Right-of-Way of Lenox Avenue, Michigan Court, Jefferson Court, Jefferson Avenue, Meridian Court, Meridian Avenue, Euclid Court and Euclid Avenue between 5th St. and 2nd St. (excluding 3rd St. east of Michigan).

Project Management Department: CIP Office

Total Project Cost: \$16,225,067 Total CRA participation: \$8,254,725

Source: Pg. 341 - Capital Improvement Plan and FY 08/09 Capital

Budget

South Pointe Streetscape Improvements Phase III-V

This project includes the installation of new infrastructure within priority Basin 1 to meet the recommended level of service. The project limits are bounded by Ocean Drive to the East and Alton Road to the West, and includes: 1st Street between Alton and Ocean, Commerce Street from Alton to Washington, Ocean Drive, Ocean Court from 5th to South Pointe Drive, Collins Avenue and Collins Court from 5th to South Pointe Drive, South Pointe Drive, Jefferson Avenue between Drive and 1st, and other adjacent alleys, roadways and rights of way.

Project Management Department: CIP Office

Total Project Cost: \$25,603,389 Total CRA participation: \$4,927,566

Source: Pg. 343 - Capital Improvement Plan and FY 08/09 Capital

Budget

South Pointe Park

This project includes improvements to the 17 acre regional park per the City of Miami Beach Parks Master Plan, 1996. Elements include: redesigned park entrance, new restroom building, pedestrian paving, site lighting, playgrounds, signage, landscaping and irrigation. Improvements to the park will provide a memorable and safer park experience. The park is now open to the public and a grand opening ceremony was held March 22, 2009.

Project Management Department: CIP Office

Total Project Cost: \$28,246,772

Total CRA participation: \$12,657,580

Source: Pg. 253 - Capital Improvement Plan and FY 08/09 Capital

Budget

South Pointe

South Pointe Wastewater Pump Station

This project is for a new master in-line wastewater booster station to be located at 1st Street and Jefferson Avenue location. It is an integral part of the city-wide wastewater pump station upgrades that are currently under construction under the 1995 Water and Sewer bond.

Project Management Department: CIP Office

Total Project Cost: \$24,431,281 Total CRA participation: \$1,442,348

Source: Pg. 420 - Capital Improvement Plan and FY 08/09 Capital

Budget

Washington Avenue Streetscape

This project is for streetscape improvements along Washington Avenue per the Master Plan. These improvements will include sidewalks, curb and gutter, sidewalk lighting, landscaping, median planting, irrigation and median design elements. This work will also be coordinated with water line replacements, upgrades and drainage upgrades.

Project Management Department: CIP Office

Total Project Cost: \$17,112,249 Total CRA participation: \$1,342,188

Source: Pg. 355 - Capital Improvement Plan and FY 08/09 Capital

Budget

6th & Lenox ROW Improvements (Flamingo BP-1A)

This work is being undertaken in conjunction with the Fifth and Alton project. The City is making drainage, road, sidewalk, landscaping, and hardscape improvements on the two streets adjacent to the project, Sixth Street and Lenox Avenue. The work for these streets is contained in the Basis of Design Report for the Flamingo Neighborhood Right of Way improvements.

Project Management Department: CIP Office

Source: LTC 212-2009 CIP Bi weekly Construction Report

dated August 7, 2009.

South Pointe

Beachwalk II

The Beachwalk II project will establish a southern Lummus Park and South Pointe Park. Beachwalk II will be a 0.6 mile path running North-South, west of the dune system and east of Ocean Drive. The project will include an extensive dune enhancement component including use of turtle friendly lighting, removal of invasives, planting of native plants, dune fill, rope and post, and sand fencing. Additional objectives of the project includes physical improvements multimodal transportation, link bicycle and destinations, increase pedestrian and bicycle safety, improve trail network connectivity, eliminate barriers that prevent bicycle trips, and develop future bikeway corridors.

Project Management Department: Public Works

Total Project Cost: \$4,736,731 Total CRA participation: \$2,800,600

Source: Pg. 455 - Capital Improvement Plan and FY 09/10 Capital Budget

CITY CENTER

REDEVELOPMENT DISTRICT

FINANCIAL INFORMATION

FOR THE MONTH ENDED

OCTOBER 31, 2010



City of Miami Beach, 1700 Convention Center Drive, Miami Beach, Florida 33139, www.miamibeachfl.gov

REDEVELOPMENT AGENCY MEMORANUM

TO:

Jorge M. Gonzalez, Executive Director

FROM:

Patricia D. Walker, Chief Financial Officer

DATE:

December 8, 2010

SUBJECT: City Center Redevelopment District Financial Information

For the Month Ended October 31, 2010

At the July 15, 1998 Commission/Redevelopment Agency meeting a request was made for monthly financial information for the City Center Redevelopment District. The information has been compiled and is attached.

Historical Cash Basis Financial Information

The summary report included in the attached material, reflects that during the period from October 1, 1993 through October 31, 2010 approximately \$520,956,000 of revenues were received in the City Center District of the Redevelopment Agency ("RDA").

The primary sources of these revenues included approximately:

- \$ 242,442,000 Incremental Ad Valorem tax:
- \$ 108,780,000 Bond proceeds:
- \$ 27,499,000 Loews Hotel Exercise Option:
- \$ 35,505,000 Resort tax contributions;
- \$ 19,190,000 Draws from the line of credit from the City of Miami Beach;
- \$ 24,746,000 Anchor Garage receipts;
- \$ 12,562,000 Royal Palm Land Sale:
- \$ 19,602,000 Interest income:
- 8,235,000 Loews Ground Lease receipts; \$
- 6,488,000 Anchor Shops receipts;
- 3,000,000 Loan from the City of Miami Beach;
- 2,700,000 Contributions from GMCVB toward debt service payments;
- \$ 1,976,000 - Reimbursements from other state and local agencies;
- \$ 700,000 - Contribution from CMB Parking Department;
- \$ 470,000 - RDP Royal Palm Ground Lease receipts;
- 402,000 Cost of Issuance Proceeds-Series 2005; and,
- 6,659,000 From Various Sources.

On the expenditure side, approximately \$443,915,000 has been expended from October 1, 1993 through October 31, 2010.

These approximate expenditures were primarily made in the following areas:

```
$144,777,000 - Debt Service Payments;
$ 61,516,000 - Convention Center Hotel Project (Loews Hotel);
$ 28,867,000 - Lincoln Road/Bass Museum Loan Repayment to CMB;
$ 18,248,000 - Hotel Garage Project;
$ 12,969,000 - African-American Hotel Project:
$ 15,605,000 - Collins Park Cultural Center;
$ 6,497,000 - Colony Theater;
$ 16,550,000 - Anchor Garage Operations;
$ 17,194,000 - Administrative Costs;
$ 5.182.000 - Beachwalk Project:
$ 5,420,000 - Miami City Ballet;
$ 16,452,000 - Community Policing;
  2,385,000 - Secondary Pledge Repayments (Resort Tax);
   3.198,000 - Washington Avenue Streetscapes:
  1,443,000 - Lincoln Road Project;
  1,229,000 - Water & Wastewater Pump Station;
$ 2,356,000 - R.O.W. Improvements;
$ 10,060,000 - Capital Projects Maintenance;
  1,477,000 - South Beach Area Property Management
  1,682,000 - Anchor Shops Operations;
     375,000 - Cost of Issuance-Series 2005A&B;
     182,000 - Movie Theater Project:
$ 14,155,000 - Purchase of the Barclay, the Allen and the London House for MBCDC
     700,000 - Washington Avenue Bridge Restoration Loan ($630,987 - Refunded)
$ 55,396,000 - Other Project Costs.
```

The cash balance as of October 31, 2010 is approximately \$77,041,000. This balance consisted of the following amounts:

```
$ 70,558,000 - Cash and Investments Balance;
$ 6,473,000 - Fully Funded Debt Service Reserve Accounts;
```

\$ 10,000 - Petty Cash – Pay on Foot Machine

JMG:PDW:ky

SUMMARY OF

CASH BASIS TRANSACTIONS

FOR THE MONTH ENDED

OCTOBER 31, 2010

Redevelopment Agency - City Center/Historic Convention Village Summary of Cash Basis Transactions by Project Fiscal Years 1994 - 2011

					Total
	Prior Years		FY 2011		Rev./Expend.
OPENING CASH/INVESTMENT BALANCE \$		\$	78,549,759	*********	
REVENUE					
- Tax increment - County	107,239,928		-	\$	107,239,928
- Tax increment - City	127,957,529		-		127,957,529
- Tax increment (Interest) - County	19,057		-		19,057
- Tax increment - Children's Trust	7,225,401		· -		7,225,401
- Bond proceeds	108,779,453		-		108,779,453
- Rental income	183,683		-		183,683
- Anchor Garage receipts	24,310,021		279,650		24,589,671
- Anchor Garage deposit card receipts	29,628		30		29,658
- Anchor Shops rental income	6,339,876		60,316		6,400,192
- Anchor Shops rental deposits	88,241		-		88,241
- Legal settlement	100,000		-		100,000
- Loews Facility Use/Usage Fee	126,504		-		126,504
- Loews Ground Lease Receipts	8,234,784		-		8,234,784
- Loew Hotel - exercise option	27,498,975		-		27,498,975
 RDP Royal Palm Ground Lease Receipts 	470,222		-		470,222
- RDP Royal Palm - Sale of Land	12,562,278.00		-		12,562,278
- Interest income	19,597,793		4,432		19,602,225
- Resort tax contributions	35,270,689		234,903		35,505,592
- Cost of Issuance Proceeds-Series 2005	402,221		-		402,221
- Bid deposits - hotels	375,000		-		375,000
- Bid deposits - cinema	100,000		-		100,000
- Loan from City	3,000,000		. -		3,000,000
- Line of credit from City	19,190,000		-		19,190,000
- Cultural Campus	1,975,762		• -		1,975,762
- St. Moritz Hotel - refund/reimbursement	925,450		-		925,450
- Reimbursements (GMCVB/RE taxes/Grants)	3,864,530		_		3,864,530
- St. sales tax (receipt - income for pmt. to St)	2,087,417		24,095		2,111,512
- Miami City Ballet environmental clean-up	31,698	:			31,698
- Anchor Garage insurance reimbursement	26,170		_		26,170
- Real Estate taxes refund	231,824		_		231,824
- Refund from Dept. of Mgmt Services	139,239		_		139,239
- Refund - Loews - Water/Sewer Impact Fees	303,278		4,302		307,580
- Refund - Police Salaries and Wages	559,831		7,002		559,831
- Miscellaneous/Prior Year Refunds & Voids	1,102,452				1,102,452
	1,102,402			-	1,102,432
TOTAL REVENUE	520,348,934		607,728	\$	520,956,662
EXPENDITURES					
RRO JECTS					
PROJECTS African American Head	(40.000.000				
African-American Hotel	(12,968,666)		-		(12,968,666)
Convention Hotel	(61,516,007)	1	-		(61,516,007)
Hotel Garage - Construction	(18,247,976)		• -		(18,247,976)
Movie Theater Project	(182,200)		•		(182,200)
Lincoln Road	(1,443,063)	1	-		(1,443,063)
Beachwalk	(5,182,646)				(5,182,646)
Collins Park Cultural Center	(15,604,822)	1	-		(15,604,822)
Bus Prop. Ctr.	(159)		- ·		(159)
Chamber of Commerce Relocation Study	(2,000)		-		(2,000)
Colony Theater	(6,496,392)	:	·		(6,496,392)
Construction of Library	(14,586)	,	-		(14,586)
East/West Corridor	(88)		-		(88)
		1			

Redevelopment Agency - City Center/Historic Convention Village Summary of Cash Basis Transactions by Project Fiscal Years 1994 - 2011

			Total
	Prior Years	FY 2011	Rev./Expend.
Electrowave	(3,161)		(3,161)
Garden Center	(93)	. -	(93)
Guidelines	(12,450)	· -	(12,450)
Old City Hall	(499)	-	(499)
17th Street Surface Lot	(256,887)	-	(256,887)
10A Surface Lot-Lennox	(382,854)	•	(382,854)
Streetscapes	(324,849)	-	(324,849)
6th Street Streetscape	(577)		(577)
Botanical Gardens	(123,136)	(32,093)	(155,229)
Transportation Mobility Study	(32,225)	-	(32,225)
Convention Center Storm Water Improve.	(1,412,705)	(4,000)	(1,416,705)
New World Symphony	(20,825,369)	-	(20,825,369)
New World Symphony Park Project	(1,675,121)	(1,608,365)	(3,283,486)
Washington Avenue Streetscape	(3,198,183)	-	(3,198,183)
Rotunda	(101,122)	-	(101,122)
R.O.W. Improvements	(2,356,207)	•	(2,356,207)
Flamingo (16 St. Corridor)	(4,721)	•	(4,721)
Flamingo Neigh.South - Bid A	(10,186)		(10,186)
Flamingo Neigh. Lummus - Bid B	(456,047)	-	(456,047)
Flamingo Bid C - N/E/W Neigh.	(13,877)	•	(13,877)
Beachfront Restrooms	(403,947)	-	(403,947)
Water & Wastewater Pump Station	(1,228,541)	-	(1,228,541)
Miami City Ballet	(5,420,416)	-	(5,420,416)
Wayfinding Project	(324,219)		(324,219)
West Ave/Bay Road Neigh. Improve.	(687,720)		(687,720)
Multi-Purpose Building Adj. City Hall	(14,637,162)	(15,000)	(14,652,162)
Bass Museum	(488,175)	(10,000)	(488,175)
Purchase of the Barclay, the Allen and the	(100,110)		(400,170)
London House for MBCDC	(14,154,643)	_	(14,154,643)
Alleyway Restoration Program	(201,770)		(201,770)
Lincoln Road Between Lennox and Alton	(6,151,710)		(6,151,710)
Lincoln Road Between Collins/Washington	(71,139)		(71,139)
Little Stage Complex	(275,190)	_	(275,190)
Preferred Parking Surface Lot	(526,649)	_	(526,649)
Tree Wells Pilot Project	(409,571)	_	(409,571)
Washington Ave. Bridge Restoration Loan	(700,000)	_	(700,000)
Collins Canal Enhancement Project	(66,053)	_	(66,053)
CCHV Neighborhood Improvements	(3,342,562)	(277,355)	(3,619,917)
Animal Waste Dispensers & Receptacles	(25,000)	(277,000)	(25,000)
Pedestrian Countdown Signals	(54,868)	_	(54,868)
Maze Project - 21st Street & Collins	(135,000)	_	(135,000)
Bicycle Parking Project	(268)	(5,175)	(5,443)
,	(200)	(0,170)	(3,443)
Total Projects	(202,153,477)	(1,941,988)	(204,095,465)
CAPITAL PROJECTS MAINTENANCE	(10,060,012.00)	-	(10,060,012)
SOUTH BEACH AREA PROPERTY		,	
MANAGEMENT	(1,477,012)	(190)	(1,477,202)
ADMINISTRATION	(17,182,809)	(11,137)	(17,193,946)
COST OF ISSUANCE-SERIES 2005A&B	(375,047)	-	(375,047)
DEBT SERVICE/LOAN REPAYMENT	(147,162,326)		
	(177,102,320)		(147,162,326)

Redevelopment Agency - City Center/Historic Convention Village Summary of Cash Basis Transactions by Project Fiscal Years 1994 - 2011

CITY OF MIAMI BEACH/LOAN REPAYMENT	Prior Years (28,867,107)	FY 2011	Total Rev./Expend. (28,867,107)
ANCHOR GARAGE OPERATIONS	(16,407,950)	(142,662)	(16,550,612)
ANCHOR SHOPS OPERATIONS	(1,673,880)	(8,204)	(1,682,084)
COMMUNITY POLICING	(16,439,555)	(12,234)	(16,451,789)
TOTAL EXPENDITURES	(441,799,175)	(2,116,415)	\$ (443,915,590)
ENDING CASH/INVSTMT. BALANCE	\$ 78,549,759	\$ 77,041,072	

Redevelopment Agency - City Center/Historic Convention Village Summary of Cash Basis Transactions by Expenditure Type Fiscal Years 1994 - 2011

				Total
	Prior Years	FY 2011	F	Rev./Expend.
OPENING CASH/INVESTMENT BALANCE	\$	\$ 78,549,759		
DEVENUE				
REVENUE	407.000.000		_	
- Tax increment - County	107,239,928	-	\$	107,239,928
- Tax increment - City	127,957,529	-		127,957,529
- Tax increment (Interest) - County	19,057	-		19,057
- Tax increment - Children's Trust	7,225,401	-		7,225,401
- Bond proceeds	108,779,453	-		108,779,453
- Rental income	183,683	-		183,683
- Anchor Garage receipts	24,310,021	279,650		24,589,671
- Anchor Garage deposit card receipts	29,628	30		29,658
- Anchor Shops rental income	6,339,876	60,316		6,400,192
- Anchor Shops rental deposits	88,241	-		88,241
- Legal settlement	100,000	-		100,000
- Loews Facility Use/Usage Fee	126,504	-		126,504
- Loews Ground Lease Receipts	8,234,784	-		8,234,784
- Loew Hotel - exercise option	27,498,975	-		27,498,975
- RDP Royal Palm Ground Lease Receipts	470,222	-		470,222
- RDP Royal Palm - Sale of Land	12,562,278	-		12,562,278
- Interest income	19,597,793	4,432		19,602,225
- Resort tax contributions	35,270,689	234,903		35,505,592
- Cost of Issuance Proceeds-Series 2005	402,221	-		402,221
- Bid deposits - hotels	375,000	-		375,000
- Bid deposits - cinema	100,000	-		100,000
- Loan from City	3,000,000	: !		3,000,000
- Line of credit from City	19,190,000	-		19,190,000
- Cultural Campus	1,975,762	<u> </u>		1,975,762
 St. Moritz Hotel - refund/reimbursement 	925,450	-		925,450
- Reimbursements (GMCVB/RE taxes/Grants)	3,864,530	· •		3,864,530
- St. sales tax (receipt - income for pmt. to St)	2,087,417	24,095		2,111,512
- Miami City Ballet environmental clean-up	31,698	-		31,698
- Anchor Garage insurance reimbursement	26,170	_		26,170
- Real estate taxes refund	231,824	: -		231,824
- Refund from Dept. of Mgmt Services	139,239	-		139,239
- Refund - Loews - Water/Sewer Impact Fees	303,278	4,302		307,580
- Refund - Police Salaries and Wages	559,831	_		559,831
- Miscellaneous/Prior Year Refunds & Voids	 1,102,452			1,102,452
TOTAL REVENUE	 520,348,934	607,728	\$	520,956,662
EXPENDITURES	 			
Administrative fees	(04.004)			
	(31,684)	-		(31,684)
Appraisal fees	(125,368)	-		(125,368)
Bid refund	(230,000)	-		(230,000)
Board up	(60,758)	-		(60,758)
Bond costs	(211,440)	-		(211,440)
Building permit fees	(173,269)	-		(173,269)
Construction	(53,426,067)	-		(53,426,067)
Delivery Demolition	(2,995)	-		(2,995)
Demolition	(203,195)	-		(203,195)
Electric service	(1,976)	-		(1,976)
Environmental	(354,908)	-		(354,908)
Equipment rental	(55,496)	.=		(55,496)

Redevelopment Agency - City Center/Historic Convention Village Summary of Cash Basis Transactions by Expenditure Type Fiscal Years 1994 - 2011

	Total
Prior Years FY 2011	Rev./Expend.
Hotel negotiation consultant (849,243) -	(849,243)
Hotel selection/study (263,357) - Land acquisition (41,240,564) -	(263,357)
	(41,240,564)
Legal fees/costs (2,770,339) - Lighting (60,805) -	(2,770,339)
Lot clearing (34,771) -	(60,805) (34,771)
Maintenance (245,288) -	(245,288)
Miscellaneous (710,659)	(710,659)
Owner's representative fee & expenses (1,823,466)	(1,823,466)
Postage, printing & mailing (27,855)	(27,855)
Professional services (6,722,190)	(6,722,190)
Public notice/advertisement (26,472)	(26,472)
Purchase of the Barclay, the Allen and the	
London House for MBCDC (14,154,643)	(14,154,643)
Refund of deposits (185,000)	(185,000)
Reimburse closing costs to C.M.B. (3,000,000)	(3,000,000)
Reimbursements (78,041)	(78,041)
Relocation (131,784)	(131,784)
Revitalization (960,522) -	(960,522)
Security guard service (277,825) -	(277,825)
Streetscape (401,312) - Temporary staffing (69,158) -	(401,312)
	(69,158)
Title insurance (25,271) - Traffic parking study (8,600) -	(25,271)
Training, conferences & meetings (3,268)	(8,600)
Travel & related expenses (28,730)	(3,268) (28,730)
Utilities (336,532)	(336,532)
Washington Ave. Bridge Restoration Loan (700,000)	(700,000)
Water/Sewer (impact fees) (25,240)	(25,240)
Total (130,038,091) -	(130,038,091)
- Miscellaneous Projects (72,115,386) (1,941,988)	(74,057,374)
Total Projects (202,153,477) (1,941,988)	(204,095,465)
CAPITAL PROJECTS MAINTENANCE (10,060,012)	
SOUTH BEACH AREA PROPERTY	(10,060,012)
<u>MANAGEMENT</u> (1,477,012) (190)	(10,060,012)
COST OF ISSUANCE SERVED COSTA OR	(10,060,012)
COST OF ISSUANCE-SERIES 2005A&B (375,047)	
	(1,477,202)
ADMINISTRATION (17,182,809) (11,137)	(1,477,202)
	(1,477,202)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) -	(1,477,202) (375,047) (17,193,946) (147,162,326)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) - CITY OF MIAMI BEACH/LOAN REPAYMENT (28,867,107) -	(1,477,202) (375,047) (17,193,946)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) -	(1,477,202) (375,047) (17,193,946) (147,162,326)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) - CITY OF MIAMI BEACH/LOAN REPAYMENT (28,867,107) -	(1,477,202) (375,047) (17,193,946) (147,162,326) (28,867,107)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) - CITY OF MIAMI BEACH/LOAN REPAYMENT (28,867,107) - ANCHOR GARAGE OPERATIONS (16,407,950) (142,662)	(1,477,202) (375,047) (17,193,946) (147,162,326) (28,867,107) (16,550,612)
ADMINISTRATION (17,182,809) (11,137) DEBT SERVICE/LOAN REPAYMENT (147,162,326) - CITY OF MIAMI BEACH/LOAN REPAYMENT (28,867,107) - ANCHOR GARAGE OPERATIONS (16,407,950) (142,662) ANCHOR SHOPS OPERATIONS (1,673,880) (8,204)	(1,477,202) (375,047) (17,193,946) (147,162,326) (28,867,107) (16,550,612) (1,682,084)

CHECK & WIRE TRANSFER REGISTER

SORTED BY

PROJECT & TYPE OF EXPENDITURE

FOR THE MONTH ENDED OCTOBER 31, 2010

Redevelopment Agency - City Center District Check & Wire Transfer Register by Project & Type of Expense Fiscal Year 2011

Check	# Date	Payee	Amount	scal fear 2011	Type of Expense	Project or N/A
WIRE WIRE WIRE	10/07/10	US Bank, NA US Bank, NA US Bank, NA	5,387.50 750.00 5,000.00	Other Administration 9	Series - 9/1/10 - 8/31/2011 36/98 A Series-9/1/10-8/31/2011 2005A Series-9/1/10-8/31/2011	Administration Administration Administration
•		TOTAL ADMINISTRATION	11,137.50			
2266	10/05/10	El Toro Exterminator Corp.	190.00 190.00	Exterminator Service		South Beach Area Property Management
		TOTAL SOUTH BEACH AREA PROPERTY MGMT	190.00			
2271 2276 2278 2281 2282 2286 2295	10/07/10 10/12/10 10/12/10 10/13/10 10/13/10 10/19/10 10/26/10	Radiotronics Radiotronics Security Alliance Fechheimer Brothers Police City of Miami Beach Security Alliance Verizon Wireless	120.00 1,141.67 4,777.95 426.56 421.78 4,785.90 560.14	Repairs & calibrations Repairs on Smart Trai Security Service Uniforms Reimb.CMB -Visa: Sp Security Service Aircards		Community Policing
		TOTAL COMMUNITY POLICING	12,234.00			
2278 2286	10/12/10 10/19/10	Security Alliance Security Alliance	2,720.76 1,690.41 4,411.17	Security Services Security Services		Anchor Garage Operations Anchor Garage Operations
WIRE	10/12/10	City of Miami Beach	2,593.68 2,593.68	Utility Billing - Septen	nber 2010	Anchor Garage Operations
2293 2294	10/26/10 10/26/10	Ashley Policare Janessa Lopez	117.00 10.00 127.00	Return Parking Acces Return Parking Acces	s Card Deposit & 1 Month Payment s Card Deposit	Anchor Garage Operations Anchor Garage Operations
2279	10/12/10	Transvalue, Inc.	485.33 485.33	Armor Car Services -	Sept 10	Anchor Garage Operations
2268	10/05/10	Superior Landscaping & Lawn	340.00 340.00	Weekly Landscape - S	September 10	Anchor Garage Operations
2280	10/12/10	Vista Building Maintenance Services	6,528.20 6,528.20	Janitorial Services for	the Garage - Sept '10	Anchor Garage Operations
2270 2283 2283	10/07/10 10/13/10 10/19/10	City of Miami Beach City of Miami Beach City of Miami Beach	606.00 44.98 151.92 802.90	Annual Elevator Billing Reimb.CMB-Visa: Atla Reimb.CMB-Visa: AT		Anchor Garage Operations Anchor Garage Operations Anchor Garage Operations
2288	10/21/10	Miami Beach Redevelopment, Inc	70,712.73 70,712.73	Facility Use / Usage F	ee - April - June 2010	Anchor Garage Operations
2285	10/19/10	Impark Impenal Parking (impark)	41,617.52 41,617.52	Salary Reimbursemen	its	Anchor Garage Operations
WIRE	10/20/10	Florida Department of Revenue	15,043.50 15,043.50	Sales Tax		Anchor Garage Operations
		TOTAL ANCHOR GARAGE OPER.	142,662.03			
WIRE	10/20/10 10/01/10	Florida Department of Revenue Florida Department of Revenue	4,481.84 3,722.54 8,204.38	Sales Tax Sales Tax		Anchor Shops Oper. Anchor Shops Oper.
		TOTAL ANCHOR SHOPS OPER.	8,204.38			
2277	10/12/10	Raymond Jungles, Inc.	32,092.99 32,092.99	Professional Services		Garden Center Renovations
		TOTAL BOTANICAL GARDENS PROJECT	32,092.99			
2284 2289	10/19/10 10/21/10	All American Barricade PBS&J	599.95 48,375.00 48,974.95	Maintenance of Traffic Drexel Ave. Transports		New World Symphony Park Project New World Symphony Park Project
2275 2297	10/12/10 10/28/10	New World Symphony New World Symphony	9,994.17 1,540,495.40 1,550,489.57		ditional Improv Res 543-2007, 552-2007 rk - Res 543-2007, 552-2007	New World Symphony Park Project New World Symphony Park Project
2287	10/21/10	Eastern Metal Supply, Inc.	6,308.85	Reso 543-2007, 552-20		New World Symphony Park Project
2290	10/21/10	Town and County Industries	2,591.16 8,900.01	Lincoln Park Project - (Reso 543-2007, 552-20	Construction costs/ materials as provided for in 007, and 560-2008.	New World Symphony Park Project
		TOTAL NEW WORLD SYMPHONY PARK PROJECT	1,608,364.53			

Redevelopment Agency - City Center District Check & Wire Transfer Register by Project & Type of Expense Fiscal Year 2011

				:		
Check #	Date	Payee	Amount	Туре о	f Expense	Project or N/A
2269	10/07/10	AECOM USA, Inc.	4,000.00 4,000.00	Traffic Impact & Mobility Study		Convention Center Streetscape
		CONVENTION CENTER STREETSCAPE	4,000.00	The second secon		
2265	10/05/10	Link Construction Group, Inc.	15,000.00 15,000.00	Construction Services		Multi-Purpose Build.Adj.City Hall
		TOTAL MULTI-PURPOSE BUILD.ADJ.CITY H.	15,000.00			
2292	10/21/10	Universal Engineering Sciences	380.00 380.00	Professional Services		CCHV Neigh. Improv Historic Dist.
2267	10/05/10	M. Vila & Associates, Inc.	276,974.60 276,974.60	Construction Services		CCHV Neigh. Improv Historic Dist.
	•	TOTAL CCHV NEIGHBORHOOD IMPROVEMENTS	277,354.60	i i i i i i i i i i i i i i i i i i i		
2291	10/21/10	UIA Management LLC	5,175.00 5,175.00	Professional Services		Bicycle Parking Project
		TOTAL BICYCLE PARKING PROJECT	5,175.00			
		REPORT TOTAL	\$ 2.116.415.03	1		

ATTACHMENT "A"

SUMMARY OF MAJOR PROJECTS

REDEVELOPMENT PROJECTS (Planned and/or Underway)

City Center

Collins Park/Streetscape/Rotunda

This project is for the renovation and redesign of Collins Park on the west side of Collins Avenue (approx. 4.5 acres) per Cultural Campus Master Plan after the demolition of the existing library. This project does not include Collins Park improvements on the east side of Collins Avenue (approx. 3.3 acres), for which design and construction are to be coordinated with the streetscape improvements and beach walk improvements.

Project Management Department: CIP Office

Total Project Cost: \$10,342,106 Total CRA participation: \$8,522,106

Source: Pg. 312 - Capital Improvement Plan and FY 08/09 Capital

Budget

Collins Park Children's Feature

This project is for the construction of a child oriented art/interactive feature as part of the Collins Park project. The project will complement the previously approved Collins Park project and will provide a needed children's space within the Collins Park/Oceanfront Neighborhood.

Project Management Department: CIP Office

Total Project Cost: \$150,000 Total CRA participation: \$150,000

Source: Pg. 289 - Capital Improvement Plan and FY 09/10 Capital

Budget -

Colony Theatre Renovation

This project is for the renovation of the existing ground floor restrooms of the Colony Theatre to comply with the Americans with Disabilities Act (ADA), and to provide a remote trash disposal enclosure at an adjacent City owned surface parking lot. These projects are not going to be done concurrently.

Project Management Department: CIP Office

Total Project Cost: \$734,690

Total CRA participation: \$734,690 (\$500,000 Grant Funded)

Source: Pg. 117 - Capital Improvement Plan and FY 08/09 Capital

City Center Right-of-Way Improvement Project (City Center-Commercial District BP9B)

This project includes the restoration and enhancement of right-of ways/streetscapes throughout the City Center, including roadway, sidewalks, curb and gutter, landscape, streetscape, irrigation, lighting, potable water, and storm drainage infrastructure as needed. The project limits include Drexel Avenue from Lincoln Lane to Lincoln Lane North, Pennsylvania Avenue from 16th to 17th Street, Euclid Avenue from Lincoln Lane to Lincoln Road Mall, Meridian Avenue from 16th to 17th, Jefferson Avenue from Lincoln Lane to 17th St., Michigan Avenue from 16th to 17th, Lenox Avenue from 16th to 17th, Lenox Court, Lincoln Lane to 16th, Lincoln Lane from Drexel to Alton Rd., Lincoln Lane North from Washington to Alton, Washington to Dade Blvd, Convention Center Drive and 19th Street.

Project Management Department: CIP Office

Total Project Cost: \$13,209,842 Total CRA participation: \$13,209,842

Source: Pg. 310 - Capital Improvement Plan and FY 08/09 Capital

Budget

New World Symphony Garage Project

This project is for replacement parking as part of the Sound Space Project. Pursuant to the direction of the City Commission, the proposed design of the parking facility maximizes the total number of available spaces at 644 spaces. Pursuant to the development and lease agreement for the Sound Space Project, the New World Symphony is responsible for building replacement parking in order to mitigate the impact to surrounding business and retail uses that currently utilize the surface parking lots which comprise the development site.

Project Management Department: RDA

Total Project Cost: \$15,210,185 Total CRA participation: \$15,210,185

Source: Pg. 199 - Capital Improvement Plan and FY 08/09 Capital

Budget

New World Symphony Park Project

This project is for a new park which is an integral component of the overall Master Plan involving the New World Symphony Sound Space Project. The park will become a key attraction for residents and visitors alike.

Project Management Department: RDA

Total Project Cost: \$22,300,000 Total CRA participation: \$22,300,000

Source: Pg. 273 - Capital Improvement Plan and FY 08/09 Capital

Multi-Purpose Municipal Parking Facility

This project is a seven level parking facility having 651 parking spaces, approximately 32,000 sq. ft. of commercial office space facing Meridian Avenue and associated site improvements. The project is located on the East side of Meridian Avenue at 17th Street in the City of Miami Beach Florida behind City Hall. The project is to be constructed in five separate construction phases: Demolition, Piling, Underground Utilities, Garage & Office Complex and Tenant Build-Out. The garage and office complex contract was awarded to the Tower Group. This project is currently in Phase 4 which includes construction of the main building structure as well as site improvements such as landscaping and the new plaza area, street resurfacing, sidewalks, etc.

Project Management Department: CIP Office

Total Project Cost: \$40,140,255 Total CRA participation: \$19,653,098

Source: Pg. 192 - Capital Improvement Plan and FY 08/09 Capital Budget and Page 10 of CIP's Bi-Weekly Construction Report dated

January 15, 2010

Lincoln Road between Collins & Washington

This project is between the Lincoln Road Mall and the Beachfront Area, and will be designed to address the needs of the commercial and retail area as well as the pedestrian, private and public vehicular access. The project includes roadway reconfiguration to accommodate uniform traffic lanes throughout, installation of a landscaped center median with uplighting, sidewalk replacement, installation of a brick paver crosswalk with ADA curb ramps, installation of a bump out to formalize the parking area and reduce the crosswalk distance, installation of street furniture and resurfacing of the asphalt pavement.

Project Management Department: CIP Office

Total Project Cost: \$2,488,093 Total CRA participation: \$2,488,093

Source: Pg. 324 - Capital Improvement Plan and FY 08/09 Capital

Budget

Collins Canal Enhancement Project

The Collins Canal Enhancement Project includes the development of the Dade Blvd. Bike path, which is a recreational greenway that will connect to the Venetian Causeway Bike Path and the Beachwalk, as well as seawall restoration for the north bank of the canal. The major bikeway artery will tie into a regional network of planned recreational trails/alternative transportation routes, called the Atlantic Greenway Network, connecting five public parks, eight beach access areas, and seven regional parking facilities in Miami Beach. This project is part of the larger Atlantic Greenway Network which aims to promote the use of alternative transportation and reduce traffic

Collins Canal Enhancement Project cont'd...

congestion. The Collins Canal Project will provide environmental, social and human health benefits to the community.

Project Management Department: Public Works

Total Project Cost: \$8,555,127 Total CRA participation: \$1,600,000

Source: Pg. 94 - Capital Improvement Plan and FY 08/09 Capital

Budget

Little Stage Complex

The Little Stage Complex project scope includes planning, programming, design, bid and award and construction administration, restoration and/or rehabilitation of the Little Stage Theater (Acorn Theater), Carl Fisher Clubhouse, Outdoor Dance Plaza / Bandshell (proposed to be demolished), and associated walkway areas adjacent to these facilities to accommodate pedestrian circulation and limited vehicular routes as necessary.

Project Management Department: CIP Office

Total Project Cost: \$7,937,392 Total CRA participation: \$637,200

Source: Pg. 121 Capital Improvement Plan and FY 08/09 Capital

Budget

Lincoln Road Between Lennox & Alton

This project is for closure of the 1100 block of Lincoln Road to vehicular traffic and restoration of the pedestrian mall between Lennox Ave. and Alton Road.

Project Management Department: Public Works

Total Project Cost: \$5,951,710 Total CRA participation: \$5,951,710

Source: Pg. 377 - Capital Improvement Plan and FY 08/09 Capital

Budget

West Avenue/Bay Road Improvements

The West Avenue/ Bay Road Improvements project is an area-wide street improvement which may include street resurfacing, swale restoration, repair of sidewalks, street lighting upgrades, enhanced landscaping and entryway features. The scope of this project includes West Avenue and Bay Road from 5th St. to Collins Canal, east/west side streets west of Alton Road from 6th to Lincoln Road and Lincoln Court, integrated with drainage improvements to Basins 7, 8, 11, 12, and 13 per the Stormwater Master Plan.

Project Management Department: CIP Office

Total Project Cost: \$25,735,556 Total CRA participation: \$750,000

Source: Pg. 357 - Capital Improvement Plan and FY 08/09 Capital

CCHC Neighborhood Improvements - Historic District

This project includes improvements to the stormwater collection and disposal system upgrades, water distribution center upgrades, roadway resurfacing and streetscape enhancements, landscaping, traffic calming installations, additional pedestrian lighting, and enhanced pedestrian linkages. The project limits are bounded by Washington Avenue to the west, Collins Avenue to the east, Lincoln Road to the South, and Dade Blvd to the north, and includes James, Park and Liberty Avenue, 17th, 18th, 19th and 20th Streets, and 21st Street west of Park Avenue. The City entered into an agreement with Chen and Associates for the design of the project.

Project Management Department: CIP Office

Total Project Cost: \$18,502,024 Total CRA participation: \$18,463,939

Source: Pg. 309 - Capital Improvement Plan and FY 08/09 Capital

Budget

Botanical Garden (Garden Center)

This project is for Phase II of renovations to the Garden Center. Phase I improvements, which are complete, included new fencing, new roof with related asbestos abatement, restroom renovations, exterior paint, new doors, trash cans, benches and other site furnishings. The Phase II project will include renovations to the building, entry, patio roof, pergola, maintenance area, site improvements, lighting, signage, planting, irrigation, interior renovations and interior acoustic improvements. Raymond Jungles, Inc. was ranked first by the committee as the firm to develop the concept plan prior to proceeding to design development.

Project Management Department: CIP Office

Total Project Cost: \$1,851,925 Total CRA participation: \$351,925

Source: Pg. 91 - Capital Improvement Plan and FY 08/09 Capital

Budget

Pedestrian Countdown Signals

This project is to provide pedestrian countdown signals at key intersections. Pedestrian countdown signals provide an extra level of public safety. Pedestrians crossing an intersection can visually see how many seconds are left before the traffic light changes. Phase I of the program will provide for pedestrian countdown signals in thirty-two intersections.

Project Management Department: Public Works

Total Project Cost: \$496,000 Total CRA participation: \$56,000

Source: Pg. 480 - Capital Improvement Plan and FY 09/10 Capital

Maze Project 21st Street & Collins Avenue

This project is to provide for art in public places in the Collins Park area. The Collins Park area was selected as one of the specific areas where public art would be incorporated and prioritized. The public, as well as the Collins Park Neighborhood Association and the Collins Park Oversight Committee all endorsed the concept of public art in Collins Park. Subsequently, a call to artists was completed and "The Maze" was chosen.

Project Management Department: Tourism and Cultural

Development

Total Project Cost: \$250,000 Total CRA participation: \$135,000

Source: Pg. 333 - Capital Improvement Plan and FY 09/10 Capital



OFFICE OF THE MAYOR AND COMMISSION

MEMORANDUM

TO:

Jorge Gonzalez, City Manager

FROM:

Matti Herrera Bower, Mayor

DATE:


November 18, 2010

SUBJECT: For Your Information-Provided by the Miami-Dade Metropolitan Planning Organization

(MPO)

Attached please find the summary minutes of the October 21, 2010 Metropolitan Planning Organization Committee meeting and the agenda for the upcoming meeting on November 18, 2010.

MHB/lw





METROPOLITAN PLANNING ORGANIZATION FOR THE MIAMI URBANIZED AREA GOVERNING BOARD

SUMMARY MINUTES

MEETING OF THURSDAY, OCTOBER 21, 2010 AT 2:00 P.M.

STEPHEN P. CLARK CENTER 111 NW FIRST STREET COUNTY COMMISSION CHAMBERS

The following members were present for the meeting of the Miami-Dade County Metropolitan Planning Organization on October 21, 2010:

Board Member Zevin V. Auerbach	Board Member Joe A. Martinez
Board Member Bruno A. Barreiro	Board Member Julio Robaina
Board Member Carlos L. Curbelo	Board Member Dorrin D. Rolle
Board Member Shirley M. Gibson	Board Member Natacha Seijas
Board Member Carlos A. Gimenez	Board Member Katy Sorenson
Board Member Maritza Gutierrez	Board Member Rebeca Sosa
Board Member Sally A. Heyman	Board Member Francis Suarez
Board Member Barbara J. Jordan	Vice Chairwoman Perla T. Hantman

Chairman Dennis C. Moss

The following staff members were present: Mr. Jose Luis Mesa Director, MPO Secretariat; Mr. Bruce Libhaber, Assistant County Attorney; and Mrs. Zainab Salim, MPO Board Clerk.

CALL TO ORDER

Chairman Moss called the meeting to order at 2:20 p.m.

ROLL CALL

Chairman Moss requested Mrs. Salim call the roll.

Board Member Auerbach Board Member Barreiro Board Member Bateman Board Member Bower Board Member Curbelo Board Member Diaz Board Member Edmonson Board Member Gibson Board Member Gimenez	-Present -Absent -Absent -Present -Absent -Absent -Absent -Absent -Absent	Board Member Heyman Board Member Jordan Board Member Martinez Board Member Pierre Board Member Robaina Board Member Rolle Board Member Seijas Board Member Sorenson Board Member Sosa -Absent -Present -Absent -Present -Present -Present -Present
		Board Member Suarez -Present

Vice Chairwoman Perla Tabares Hantman-Present Chairman Dennis C. Moss-Present Mrs. Salim announced quorum was attained.

1. APPROVAL OF AGENDA

Attorney Libhaber informed the Board that the following modifications to the agenda had been requested:

- Deferral of Items 4.B.2 South Florida East Coast Corridor (SFECC)
 Transit Analysis Study and 4.B.3 Endorsing the Continuation of the South Florida East Coast Corridor (SFECC) Study
- Correction of typographical error on Item 2 Approval of Minutes should read June 17, 2010 minutes

Chairman Moss recommended that Item 4.B.8 MPO Secretariat 2011 Operating Budget be deferred to allow staff an opportunity to address the concerns of several Board members as it relates to this item.

At the request of Board Member Curbelo, the deferral request of Item 4.B.2 South Florida East Coast Corridor (SFECC) Transit Analysis Study would be considered later in the agenda.

Board Member Martinez expressed he could not support the deferral of 4.B.8 MPO Secretariat 2011 Operating Budget.

Board Member Sosa moved for approval of the agenda as amended. Board Member Suarez seconded the motion. The agenda as amended was approved with one dissent (Board Member Martinez).

Chairman Moss acknowledged Vice Chairwoman Hantman and Board Member Sosa on being reelected to their respective office.

2. APPROVAL OF MINUTES

Vice Chairwoman Hantman moved for approval of the June 17, 2010 minutes. Board Member Sosa seconded the motion. The minutes were approved.

3. MPO COMMITTEES AND SPECIAL REPORTS

A. SPECIAL PRESENTATION

1. Recognition of Commissioner Katy Sorenson

B. CITIZEN COMMITTEES

1. COMMITTEES VACANCY LIST

Board Member Martinez appointed Mrs. Carolina Gutierrez to BPAC. Board Member Suarez appointed Mr. Jose Javier Rodriguez to CTAC replacing Mrs. Barbara Walters.

Board Member Curbelo appointed Mr. Michael O. Mena and Mr. Gerald M. Del Amo to CTAC. He also appointed Mr. Javier Asis Lopez to TARC.

2. COMMITTEES ATTENDANCE REPORT

C. MPO REVIEW COMMITTEE

No report provided.

4. ACTION ITEMS

A. PUBLIC HEARING ITEMS

1. 2035 LONG RANGE TRANSPORTATION PLAN AMENDMENT: WEST AVENUE BRIDGE

RESOLUTION APPROVING AN AMENDMENT TO THE 2035 LONG RANGE TRANSPORTATION PLAN (LRTP) TO INCLUDE IN PRIORITY I OF THE PLAN THE WEST AVENUE BRIDGE OVER THE COLLINS CANAL PROJECT (ROLL CALL REQUIRED)

Chairman Moss opened the public hearing. Chairman Moss closed the public hearing.

Board Member Barreiro moved for the approval of the resolution. Board Member Martinez seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Auerbach	-Aye	Board Member Heyman	-Aye
Board Member Barreiro	-Aye	Board Member Jordan	-Aye
Board Member Bateman	-Absent	Board Member Martinez	-Aye
Board Member Bower	-Absent	Board Member Pierre	-Absent
Board Member Curbelo	-Aye	Board Member Robaina	-Aye
Board Member Diaz	-Absent	Board Member Rolle	-Aye
Board Member Edmonson	-Absent	Board Member Seijas	-Aye
Board Member Gibson	-Aye	Board Member Sorenson	
Board Member Gimenez	-Aye	Board Member Sosa	-Aye
Board Member Gutierrez	-Aye	Board Member Souto	-Absent
		Board Member Suarez	-Aye

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 17-0.

2. FY 2010 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: ROAD IMPACT FEE DISTRICT 8

RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO REALLOCATE ROAD IMPACT FEE DISTRICT 8 FUNDS TO THE WEST AVENUE BRIDGE OVER THE COLLINS CANAL PROJECT (ROLL CALL REQUIRED)

Chairman Moss opened the public hearing. Chairman Moss closed the public hearing.

Board Member Barreiro moved for the approval of the resolution. Board Member Heyman seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Auerbach	-Aye	Board Member Heyman	-Aye
Board Member Barreiro	-Aye	Board Member Jordan	-Aye
Board Member Bateman	-Absent	Board Member Martinez	-Aye
Board Member Bower	-Absent	Board Member Pierre	-Absent
Board Member Curbelo	-Aye	Board Member Robaina	-Aye
Board Member Diaz	-Absent	Board Member Rolle	-Aye
Board Member Edmonson	-Absent	Board Member Seijas	-Aye
Board Member Gibson	-Aye	Board Member Sorenson	-Aye
Board Member Gimenez	-Aye	Board Member Sosa	-Aye
Board Member Gutierrez	-Aye	Board Member Souto	-Absent
	•	Board Member Suarez	-Aye

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 17-0.

3. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: SR 953/SW 42ND AVENUE RESURFACING PROJECT

RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO INCLUDE SR 953/SW 42ND AVENUE RESURFACING PROJECT (ROLL CALL REQUIRED)

Chairman Moss opened the public hearing. Chairman Moss closed the public hearing.

Vice Chairwoman Hantman stated that the proposed project will impact Coral Gables Senior High School. She further stated that District staff is coordinating with FDOT project team to ensure that there is no disruption to the school's operation. She then informed the Board that at the November 24th School Board meeting an agenda item is being drafted to convey 116 square feet of school property to facilitate a portion of the project located at SW 42nd Avenue adjacent to the school.

Board Member Barreiro moved for the approval of the resolution. Board Member Heyman seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Bower Board Member Curbelo Board Member Diaz Board Member Edmonson Board Member Gibson Board Member Gimenez	-Absent -Aye -Absent -Aye -Aye	Board Member Heyman Board Member Jordan Board Member Martinez Board Member Pierre Board Member Robaina Board Member Rolle Board Member Seijas Board Member Sorenson Board Member Sosa	-Absent -Aye -Aye -Aye
	-Aye -Aye	Board Member Sosa Board Member Souto	-Aye -Absent
		Dome Michigal South	-MOSCIII

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 17-0.

4. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: CITY OF SWEETWATER RESURFACING PROJECTS

RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO ADD THE CITY OF SWEETWATER RESURFACING PROJECTS (ROLL CALL REQUIRED)

Chairman Moss opened the public hearing. Chairman Moss closed the public hearing.

Board Member Heyman moved for the approval of the resolution. Board Member Sorenson seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Auerbach	-Aye	Board Member Heyman	-Aye
Board Member Barreiro	-Aye	Board Member Jordan	-Aye
Board Member Bateman	-Absent	Board Member Martinez	-Aye
Board Member Bower	-Absent	Board Member Pierre	-Absent
Board Member Curbelo	-Aye	Board Member Robaina	-Absent
Board Member Diaz	-Absent	Board Member Rolle	-Aye
Board Member Edmonson	-Absent	Board Member Seijas	-Aye
Board Member Gibson	-Aye	Board Member Sorenson	-Aye
Board Member Gimenez	-Aye	Board Member Sosa	-Aye
Board Member Gutierrez	-Aye	Board Member Souto	-Absent
	-	Board Member Suarez	-Aye

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 16-0.

5. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: ROLL-FORWARD PROJECTS

RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO INCLUDE FLORIDA DEPARTMENT OF TRANSPORTATION (FDOT) ROLL-FORWARD PROJECDTS THAT WERE ORIGINALLY SCHEDULED IN THE STATE FISCAL YEAR 2010 TIP FOR AUTHORIZATION AND WERE NOT OBILGATED BY JUNE 30, 2010 (ROLL CALL REQUIRED)

Chairman Moss opened the public hearing. Chairman Moss closed the public hearing.

Board Member Sosa stated that the item failed to list the specific financial impact of the proposed projects. She further stated that she requested information on projects within her district and did not receive

the information from the MPO staff. She concluded by stating that she could not support the item because staff did not have the ability to provide the information prior to the meeting. She further concluded by moving to defer the item with the exception of projects that are federally funded and could not delayed. Board Member Seijas seconded the motion.

Board Member Heyman stated that she did not support deferral of the item. She further stated that the projects on the list have been previously vetted by the MPO Board. She then stated that deferral of the item will impact projects located near Oleta State Park and will have a direct impact to two new public schools in the area. She concluded by urging the MPO Board members to look at the projects in their respective areas before moving forward with deferral.

Board Member Martinez requested clarity on whether the proposed amendment is to add new projects to the Program. Mrs. Linda Glass-Johnson, FDOT, responded that the amendment does not include new projects. She further explained that the projects were previously included in the FY 2010 TIP but were not included in the newly adopted FY 2011 TIP because it was expected for the projects to be obligated with the federal government prior to the September 30, 2010 deadline. She concluded that this amendment is part of the formal process of moving these projects from the FY 2010 TIP and adding them to the FY 20111 TIP because of not being obligated.

Board Member Curbelo expressed concern that a clear answer by FDOT has not been provided on whether the projects federally funded would be impacted by the deferral. Mrs. Glass-Johnson responded that her office did not receive an information request by Board Member Sosa and therefore do not have an answer today. She further stated that deferral would delay the federal approval of a project once it is submitted through the process especially if they are not listed in the FY 2011 TIP. She then stated that the federal funding decision for each project is the discretion of the Federal Highway Administration or the Federal Transit Administration. She concluded by stating that based on her experience the execution of agreements for transit work is usually impacted.

Chairman Moss requested that Mrs. Salim conduct a roll call vote on the deferral

Board Member Auerbach	-Aye	Board Member Heyman	-Nay
Board Member Barreiro	-Aye	Board Member Jordan	-Aye
Board Member Bateman	-Absent	Board Member Martinez	-Aye
Board Member Bower		Board Member Pierre	-Absent
Board Member Curbelo	-Aye	Board Member Robaina	-Absent
Board Member Diaz	-Absent	Board Member Rolle	-Aye
Board Member Edmonson		Board Member Seijas	-Aye
Board Member Gibson	-Aye	Board Member Sorenson	
Board Member Gimenez	-Aye	Board Member Sosa	-Aye
Board Member Gutierrez	-Aye		-Absent
•	•	Board Member Suarez	-Aye

Mrs. Salim announced the deferral passed 15-1.

6. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: TRANSFER OF FUNDS TO THE UNIVERSITY PEDESTRIAN OVERPASS PROJECT

RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO TRANSFER TO THE UNIVERSITY METRORAIL STATION PEDESTRIAN OVERPASS PROJECT PREVIOUSLY PROGRAMMED FUNDS PROPOSED FOR OVERPASSES AT DADELAND NORTH, DADELAND SOUTH, AND SOUTH MIAMI METRORAIL STATIONS; DELETING LATTER PROJECTS FROM THE PROGRAM

Chairman Moss opened the public hearing.

Mr. Glenn Kephart, City of Coral Gables Public Works Director, stated that the city supports the funding of the University Pedestrian Overpass project. He informed the Board that the project would be a tremendous safety improvement for the area.

Chairman Moss closed the public hearing.

Board Member Martinez expressed concern with the language of deleting projects. Mr. Mesa clarified that the language refers to the projects being removed from the funded portion of the TIP. He further stated that the TIP has an unfunded portion and the projects would be added to that list. He further clarified by stating that the projects could not stay in the funded portion of the program without funds being allocated to them.

Board Member Martinez requested that the resolution be amended to include language that does not delete the projects from the Program. He then requested that the attorney provide the appropriate language. Attorney Libhaber responded that the amendment language would state:

"...removing from the funded portion of the Program to the unfunded portion of the Program the latter projects".

Board Member Gimenez stated that the South Miami Metrorail Overpass had been in the works for several years and later it was discovered that it was not feasible. He concluded by requesting clarity on whether at grade improvements could be provided between US-1 and Sunset Avenue and US-1 and SW 57th Avenue. Ms. Aileen Boucle, FDOT, responded that Department is currently working with the City of South Miami to implement improvements within the corridor.

Board Member Sorenson stated that the areas around Dadeland North and South Metrorail Stations currently have low density in comparison to the University Metrorail Station. She further stated that the City of Pinecrest may eventually implement some high density zoning. However, there are no eminent plans to do so. She then concluded by

stating she appreciates the language to include projects in the unfunded portion of the Program in case the future needs of the area changes.

Board Member Gutierrez informed the Board that the proposed amendment is a great opportunity for the MPO to prevent further tragic pedestrian involved accidents with students to occur. The project has been in the pipeline for many years. She further encouraged the City of Coral Gables to join the University of Miami in partnering with the County to fill the \$950,000 gap to complete this project. She then informed the Board that she and her son started seeking funding for this project in 2004 after the tragic accident of a young University of Miami student, Ashley Kelly. She concluded by stating that unfortunately funding was never there for the project and that today the opportunity exists to honor those who have been tragically affected. She further concluded by commending the MPO staff, Clinton Forbes and Albert Hernandez of Miami-Dade Transit for meeting with everyone and moving this project forward.

Board Member Sosa requested that the improvements on SW 57th Avenue be extended to SW 8th Street because the need is present.

Board Member Seijas expressed concern with not knowing if the municipalities impacted by this amendment were in support of the funds being transferred. She then requested clarity on why this project was not previously funded considering its importance to improving the safety of the community. Mr. Albert Hernandez, MDT, responded that funds for the project were identified in the People's Transportation Plan (PTP). He further stated that originally five projects were selected and went through a series of engineering criteria analysis from which only two areas, University and South Miami Metrorail Stations, warrant priority funding. He then stated that the analysis was based on the velocity of cars passing in the area and the number of pedestrians crossing in the area. He concluded by stating that the MDT staff worked with the City of South Miami to identify a feasible location without success.

Board Member Gimenez moved for the approval of the resolution. Board Member Gutierrez seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Auerbach Board Member Barreiro Board Member Bateman Board Member Bower Board Member Curbelo Board Member Diaz Board Member Edmonson Board Member Gibson Board Member Gimenez Board Member Gutierrez	-Absent -Aye -Absent	Board Member Heyman Board Member Jordan Board Member Martinez Board Member Pierre Board Member Robaina Board Member Rolle Board Member Seijas Board Member Sorenson Board Member Sosa Board Member Sosa Board Member Souto	-Absent -Absent -Aye -Aye -Aye -Aye
Board Member Gutierrez	-Aye	Board Member Souto Board Member Suarez	-Absent -Aye
		Dome Manifold Suarcz	-A y C

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye Mrs. Salim announced the motion passed 16-0.

7. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: ADDING FUNDS TO MODIFY SCOPE OF SERVICES AND ADVANCE A SAFETY PROJECT RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO ADD FUNDS TO MODIFY THE SCOPE OF SERVICES AND ADVANCE

Board Member Martinez moved for the approval of the resolution. Board Member Heyman seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

SAFETY PROJECT FM #4252131 FROM FY 2012 TO FY 2011

Board Member Auerbach	-Aye	Board Member Heyman	-Aye
Board Member Barreiro	-Aye	Board Member Jordan	-Aye
Board Member Bateman	-Absent	Board Member Martinez	
Board Member Bower		Board Member Pierre	-Absent
Board Member Curbelo	-Aye	Board Member Robaina	-Aye
Board Member Diaz	-Absent	Board Member Rolle	-Aye
Board Member Edmonson		Board Member Seijas	-Aye
Board Member Gibson	-Aye	Board Member Sorenson	
Board Member Gimenez	-Aye	Board Member Sosa	-Aye
Board Member Gutierrez	-Aye		-Absent
	•	Board Member Suarez	-Aye

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 17-0.

8. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM AMENDMENT: ADDITION OF A SAFETY PROJECT RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO ADD SAFETY PROJECT FM #429040-1

Board Member Martinez moved for the approval of the resolution. Board Member Heyman seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Auerbach Board Member Barreiro Board Member Bateman Board Member Bower Board Member Curbelo Board Member Diaz Board Member Edmonson Board Member Gibson Board Member Gimenez Board Member Gutierrez	-Absent -Absent -Absent -Aye -Aye	Board Member Heyman Board Member Jordan Board Member Martinez Board Member Pierre Board Member Robaina Board Member Rolle Board Member Seijas Board Member Sorenson Board Member Sosa Board Member Sosa	-Absent -Aye -Aye -Aye -Aye -Aye
Board Member Gutierrez	-Aye	Board Member Souto Board Member Suarez	-Aye -Absent -Aye

Chairman Dennis C. Moss - Aye Vice Chairwoman Perla Tabares Hantman - Aye

Mrs. Salim announced the motion passed 17-0.

B. NON-PUBLIC HEARING ITEMS

1. REQUEST BY MPO BOARD MEMBER ZEVIN V. AUERBACH
RESOLUTION APPROVING THE SCOPE OF WORK AND BUDGET
FOR THE FEASIBILITY STUDY CREATING A UNITED TOLL
FUNDING SOURCE

Board Member Sosa expressed concern with supporting an initiative that would combine funding from different entities. She further explained that the public should know what monies each entity collects and how they are using those funds. She then explained that she was concerned that combining these funds would have a negative impact on the Board of County Commissioners (BCC) should something would go wrong. She concluded by stating she could not be in support of spending \$100,000 on a study during these tough economic times.

Board Member Curbelo expressed that this concept could lead to a new vehicle of tolling. He further expressed that this would not be a good time to move this initiative forward. He then expressed concern that this type of concept could have an adverse impact on entities like MDX that are currently doing an excellent job in efficiently handling toll revenues.

Board Member Sorenson stated that she supports the proposed concept because the potential result could include greater efficiency of toll funds. She further stated it would be in the best interest of the Board to investigate further the feasibility of this concept. She then stated that more transit projects could be realized as a result of this initiative. She concluded by stating that more toll funds should be used to support more transit projects.

Board Member Gutierrez stated that the MPO Board could be saving \$100,000 by not approving this scope of work and instead ask the MDX, Turnpike and the other entities that collect tolls to explain their bond covenant. She further stated that toll funds can only be used for the purpose for which they were collected. She then stated in the case of MDX the toll funds can only be used on their five expressways. She concluded by informing the Board that MDX provided on July 30, 2010, a written explanation for the reason MDX's tolls could not be used for any other purpose than what they are collected for. She further concluded by encouraging the Board to deny the proposed resolution.

Board Member Jordan stated that she would like to get more information relative to the feasibility of the United Toll Concept. She further stated that she does not believe it is necessary to spend \$100,000 to determine this. She concluded by suggesting Board Member Auerbach to consider having the MPO Board conduct a workshop with the necessary tolling agencies to discuss the issue further.

Board Member Heyman stated that at first glance the item on the agenda appears to be a great idea. She further stated that the idea of having a creative look at tolling funds to assist in funding transit projects is great. She then concluded by expressing concern that staff did not provide the necessary input on the item besides ensuring that it was legal.

Chairman Moss responded that staff will not censor agenda items requested by an MPO Board member. He further stated that the decision to approve an item is that of the MPO Board.

Board Member Auerbach offered clarity for the proposed scope of work. He stated that the intent of the item was not to introduce a new toll to the residents of Miami-Dade County. He further stated that his resolution is to determine if a portion of the toll funds could be allocated to a united toll funding source to be used to fund bigger transportation projects. He further stated that he expressed similar concerns with staff that the study's budget was too high. He also reminded the Board that the spirit of the law is to protect the people who are paying the tax. He then stated that the proposed study is to not only to provide that protection but to offer more services through enhancements and traffic continuity. He concluded by stating that he supports a workshop or any option that would ask the question how to get this accomplished.

Board Member Auerbach moved for approval of the resolution. Board Member Gibson seconded the motion.

Chairman Moss requested that Mrs. Salim conduct a roll call vote.

Board Member Curbelo Board Member Diaz Board Member Edmonson Board Member Gibson Board Member Gimenez	-Absent -Nay -Absent		-Absent -Absent -Nay -Nay -Aye -Nay -Absent
		Board Member Suarez	-Nay

Chairman Dennis C. Moss - Nay Vice Chairwoman Perla Tabares Hantman -Nay

Mrs. Salim announced the motion failed 12-4.

2. SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) TRANSIT ANALYSIS STUDY

RESOLUTION SUPPORTING FLORIDA DEPARTMENT OF TRANSPORTATION'S SOUTH FLORIDA EAST COAST CORRIDOR STUDY FOR TRANSIT SERVICE BETWEEN MIAMI AND JUPITER AND ENDORSING A LOCALLY PREFERRED ALTERNATIVE Board Member Curbelo expressed concern with deferring the item. He stated that the Board received presentations on the item from staff and believed the project needed to move forward without further delay.

Board Member Sosa stated that she requested information regarding this item from staff and had not received it. She further stated that she did not feel comfortable voting on an item without the necessary information. She concluded by stating that more time was necessary to allow staff an opportunity to address the concerns of the Board.

Chairman Moss stated that he was not prepared to vote on the item today. He further expressed concern that the information on how the project would be funded was not clear considering Miami-Dade County's commitment to the North and East/West Corridors as priority projects for the community.

Board Member Jordan moved to defer the item. Board Member Rolle seconded the motion.

This item was deferred.

3. ENDORSING THE CONTINUATION OF THE SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) STUDY RESOLUTION ENDORSING THE CONTINUATION OF THE SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) STUDY TO COMPLETE THE ENVIRONMENTAL DOCUMENTS NECESSARY FOR ADVANCING PUBLIC TRANSIT SERVICES IN THE FLORIDA EAST COAST RAILWAY CORRIDOR

This item was deferred.

4. REQUEST BY MPO BOARD MEMBER CARLOS L. CURBELO RESOLUTION URGING THE FLORIDA DEPARTMENT OF TRANSPORTATION'S FLORIDA RAIL ENTERPRISE TO ADOPT THE SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) AS A PRIORITY FOR IMPLEMENTATION OF PASSENGER RAIL SERVICE IN SOUTHEAST FLORIDA

Board Member Curbelo requested that the resolution be amended to include language:

"...contingent upon the MPO Board selecting a rail alternative as the locally preferred alternative".

Board Member Curbelo moved for the approval of the resolution as amended. Board Member Martinez seconded the motion. The resolution as amended was approved 14-1 (Dissent: Board Member Barreiro).

5. FYs 2011 AND 2012 UNIFIED PLANNING WORK PROGRAM (UPWP) AMENDMENTS

RESOLUTION APPROVING THE AMENDMENTS TO THE FYS 2011 AND 2012 UNIFIED PLANNING WORK PROGRAM (UPWP) UNDER TASKS 3.02 GENERAL PLANNING CONSULTANT AND 4.07 TRANSPORTATION DISADVANTAGED PLANNING

Board Member Rolle moved for the approval of the resolution. Board Member Sorenson seconded the motion. The resolution was approved.

6. TRANSPORTATION ENHANCEMENTS PROGRAM PRIORITIES

RESOLUTION APPROVING THE 2010 TRANSPORTATION ENHANCEMENTS PROGRAM (TEP) PRIORITIES

Board Member Rolle moved for the approval of the resolution. Board Member Sorenson seconded the motion. The resolution was approved.

7. MPO PROGRAM PRIORITY LISTING FOR FDOT 2012-2016 TENTATIVE WORK PROGRAM

RESOLUTION APPROVING THE INCLUSION OF THE ANNUAL LISTING OF THE METROPOLITAN PLANNING ORGANIZATION PROGRAM PRIORITIES IN THE FLORIDA DEPARTMENT OF TRANSPORTATION TENTATIVE FIVE YEAR WORK PROGRAM

Board Member Rolle moved for the approval of the resolution. Board Member Sorenson seconded the motion. The resolution was approved.

8. FISCAL YEAR 2011 MPO SECRETARIAT OPERATING BUDGET

RESOLUTION APPROVING THE MPO SECRTARIAT FISCAL YEAR 2011 PROPOSED OPERATING BUDGET

This item was deferred.

9. MPOAC LEGISLATIVE ADVOCACY ACTIVITIES FOR 10/11
RESOLUTION APPROVING \$500 TO BE PROVIDED TO THE
STATEWIDE METROPOLITAN PLANNING ORGANIZATION
ADVISORY COMMITTEE (MPOAC) FOR THEIR LEGISLATIVE
ADVOCACY ACTIVITIES

Board Member Rolle moved for the approval of the resolution. Board Member Sorenson seconded the motion. The resolution was approved.

10. MPO BOARD APPOINTMENT TO THE LOCAL COORDINATING BOARD

RESOLUTION APPOINTING SELECTED INDIVIDUALS TO THE MIAMI-DADE LOCAL COORDINATING BOARD

Board Member Rolle moved for the approval of the resolution. Board Member Sorenson seconded the motion. The resolution was approved.

5. INFORMATION ITEM

A. ALL ELECTRONIC OPEN ROAD TOLLING PROJECT ON THE HEFT

Mr. Raymond Ashe and Kent Rice provided the Board with a presentation on the All Electronic Open Road Tolling Project on the HEFT.

Chairman Moss requested clarity on whether the rental car and the administrative fee relative to the Sunpass lanes have been addressed. Mr. Ashe stated that the Turnpike continues to work with the rental car companies to address these concerns.

6. REPORTS

A. MPO BOARD MEMBERS

1. Request by MPO Board Member Bruno A. Barreiro: Status Report on I-395 Reconstruction Project

No discussion under this item.

- B. COUNTY MANAGER
- C. COUNTY ATTORNEY
- D. MIAMI-DADE EXPRESSWAY AUTHORITY
 - 1. Status Report

No discussion under this item.

E. FLORIDA DEPARTMENT OF TRANSPORTATION (DISTRICT VI)

- 1. Monthly Progress Report on the Port of Miami Tunnel
- 2. Monthly Progress Report on the SR 826/SR 836 Interchange Reconstruction
- 3. The 2060 Florida Transportation Plan

No discussion under these items.

F. MPO SECRETARIAT

1. MPO June meeting Follow-up Report

No discussion under this item.

7. ADJOURNMENT The meeting adjourned at 4:15 PM.



Chairman
Dennis C. Moss

Vice Chairwoman
Perla Tabares Hantman

Voting Members Zevin V. Auerbach Bruno A. Barreiro Steven C. Bateman Matti Herrera Bower Carlos L. Curbelo Jose "Pepe" Diaz Audrey M. Edmonson Shirley M. Gibson Carlos A. Gimenez Maritza Gutierrez Sally A. Heyman Barbara J. Jordan Joe A. Martinez Andre D. Pierre Julio Robaina Dorrin D. Rolle Natacha Seijas Katy Sorenson Rebeca Sosa Javier D. Souto

Non-Voting Members (FDOT District VI) Gus Pego, P.E.

Francis Suarez

MPO Secretariat
Director
Jose Luis Mesa, Ph.D.

Contact Information

Mrs. Zainab Salim, Clerk
Miami-Dade MPO
111 NW First Street
Suite 920
Miami, Florida 33128
305.375.4507
305.375.4950 (fax)
zsalim@miamidade.gov
www.miamidade.gov/mpo

METROPOLITAN PLANNING ORGANIZATION GOVERNING BOARD

MEETING OF THURSDAY, NOVEMBER 18, 2010 AT 2:00 PM

STEPHEN P. CLARK CENTER
111 NW FIRST STREET
MIAMI, FLORIDA 33128
COUNTY COMMISSION CHAMBERS

AGENDA

- 1. APPROVAL OF AGENDA
- 2. APPROVAL OF MINUTES
 - October 21, 2010
- 3. MPO COMMITTEES AND SPECIAL REPORTS
 - A. SPECIAL PRESENTATION
 - 1. Recognition of MPO Director Jose Luis Mesa
 - **B. CITIZEN COMMITTEES**
 - 1. COMMITTEES VACANCY LIST
 - 2. FREIGHT TRANSPORTATION ADVISORY COMMITTEE (FTAC)
 - 3. TRANSPORTATION AESTHETICS REVIEW COMMITTEE (TARC)
 - 4. BICYCLE PEDESTRIAN ADVISORY COMMITTEE (BPAC)
 - Resolutions
 - 5. CITIZENS TRANSPORTATION ADVISORY COMMITTEE (CTAC)
 - Resolutions
 - C. MPO REVIEW COMMITTEE
- 4. ACTION ITEMS
 - A. NON-PUBLIC HEARING ITEMS
 - 1. FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) AMENDMENT: ROLL-FORWARD PROJECTS
 RESOLUTION APPROVING AN AMENDMENT TO THE FY 2011 TRANSPORTATION IMPROVEMENT PROGRAM (TIP) TO INCLUDE FLORIDA DEPARTMENT OF TRANSPORTATION (FDOT) ROLL-FORWARD PROJECTS THAT WERE ORIGINALLY SCHEDULED IN THE STATE FISCAL YEAR 2010 TIP FOR AUTHORIZATION AND WERE NOT OBLIGATED BY JUNE 30, 2010 (ROLL CALL REQUIRED)
 - 9-29-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.
 - 10-21-10 Item deferred by the MPO Governing Board.
 - 2. SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) TRANSIT ANALYSIS STUDY

RESOLUTION SUPPORTING FLORIDA DEPARTMENT OF TRANSPORTATION'S SOUTH FLORIDA EAST COAST CORRIDOR STUDY FOR TRANSIT SERVICE BETWEEN MIAMI AND JUPITER AND ENDORSING A LOCALLY PREFERRED ALTERNATIVE

9-29-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.

10-21-10 Item deferred by the MPO Governing Board.

3. ENDORSING THE CONTINUATION OF THE SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) STUDY

RESOLUTION ENDORSING THE CONTINUATION OF THE SOUTH FLORIDA EAST COAST CORRIDOR (SFECC) STUDY TO COMPLETE THE ENVIRONMENTAL DOCUMENTS NECESSARY FOR ADVANCING PUBLIC TRANSIT SERVICES IN THE FLORIDA EAST COAST RAILWAY CORRIDOR

9-29-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.

10-21-10 Item deferred by the MPO Governing Board.

- 4. FISCAL YEAR 2011 MPO SECRETARIAT OPERATING BUDGET RESOLUTION APPROVING THE MPO SECRETARIAT FISCAL YEAR 2011 PROPOSED OPERATING BUDGET
 - 9-29-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.
 - 10-21-10 Item deferred by the MPO Governing Board.
- 5. MIAMI-DADE MPO 2010 PUBLIC INVOLVEMENT PLAN
 RESOLUTION APPROVING THE MIAMI-DADE MPO 2010 PUBLIC INVOLVEMENT PLAN
 - 11-8-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.
- 6. INTERLOCAL AGREEMENT: MPO ANNUAL NEWSLETTER
 RESOLUTION APPROVING AN INTERLOCAL AGREEMENT BETWEEN
 THE MIAMI-DADE METROPOLITAN PLANNING ORGANIZATION
 (MPO) AND THE FLORIDA INTERNATIONAL UNIVERSITY
 METROPOLITAN CENTER TO PREPARE THE 2011 ANNUAL
 REPORT/SUMMER NEWSLETTER
 - 11-8-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.
- 7. 2035 LONG RANGE TRANSPORTATION PLAN MAINTENANCE OF EFFORT RESOLUTION APPROVING THE SCOPE OF WORK AND BUDGET FOR THE 2035 LONG RANGE TRANSPORTATION PLAN MAINTENANCE OF EFFORT
 - 11-8-10 Item waived by Chair onto MPO Board agenda due to cancellation of MPO Review Committee meeting.

5. INFORMATION ITEM

A. NEAR-TERM TRANSPORTATION PLAN FOR MIAMI-DADE COUNTY: 2012-2015

6. REPORTS

- A. MPO BOARD MEMBERS
- B. COUNTY MANAGER
- C. COUNTY ATTORNEY
- D. MIAMI-DADE EXPRESSWAY AUTHORITY
 - 1. Status Report
- E. FLORIDA DEPARTMENT OF TRANSPORTATION (DISTRICT VI)
- F. MPO SECRETARIAT

7. CORRESPONDENCE

It is the policy of Miami-Dade County to comply with all of the requirements of the Americans with Disabilities Act. The facility for this meeting is accessible. For sign language interpreters, assistive listening devices, or materials in accessible format please call 305-375-4507 at least five business days in advance
